

Contractor: Hayes Pipe Supply

Plant: 100



Size: 28" x 28"

Rim to Invert: 5.26'

Floor Height: 6"


Slack: 0.876"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 28" x 28" - CASTING HEIGHT - 6"
P2) 28" x 28" - BOX RISER 6inW - 24"
P1) 28" x 28" - BOX BASE 6inW, 6inF, Variable Ht - 33"
2) 28" x 28" - Conseal CS-102 1.00"
1) Hole - 14

0 lb
1643 lb
2988 lb
0 lb
0 lb


Structure Total: 4631 lb

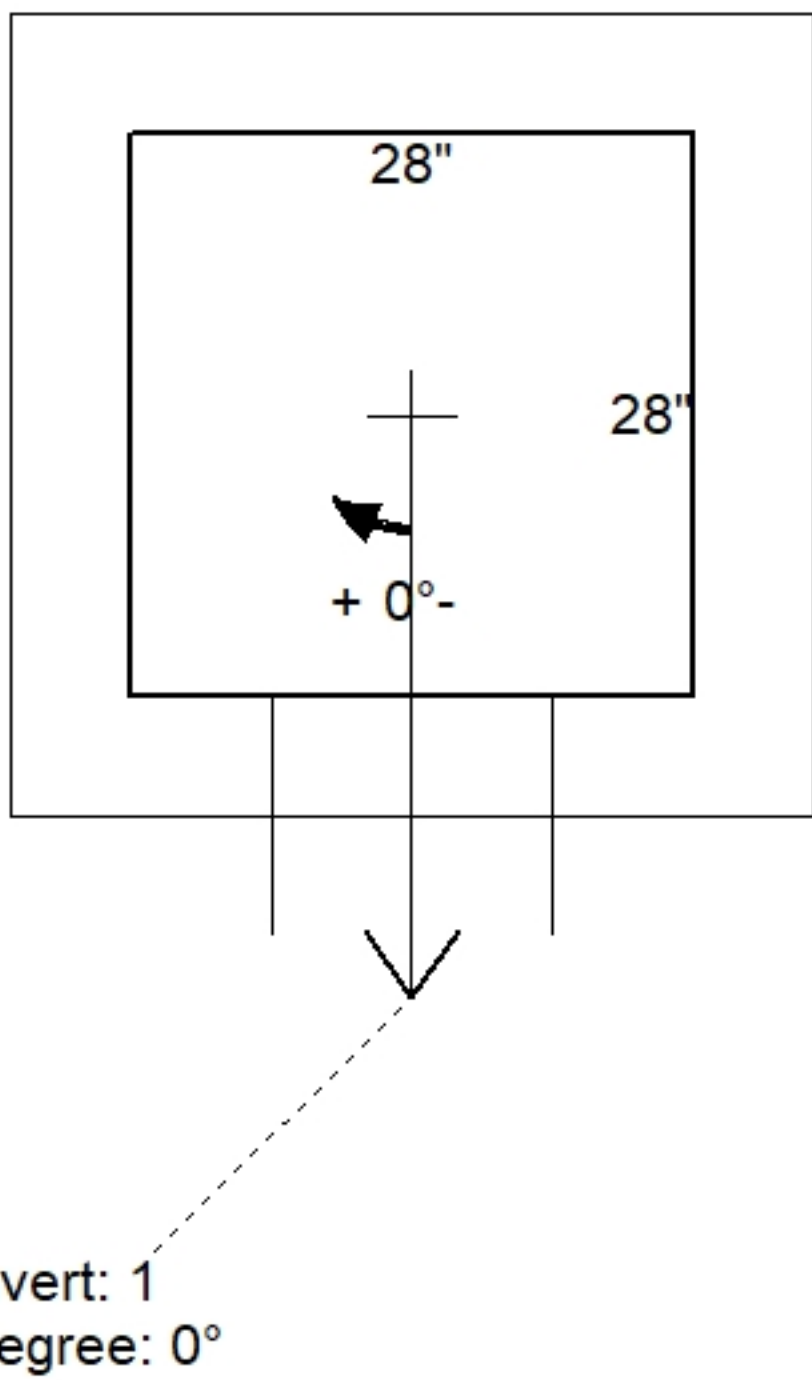

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	428.12'							
Reducer								
Invert 1	422.86'	0°	10" HDPE	11.4"	14"	Hole 14	0.056"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

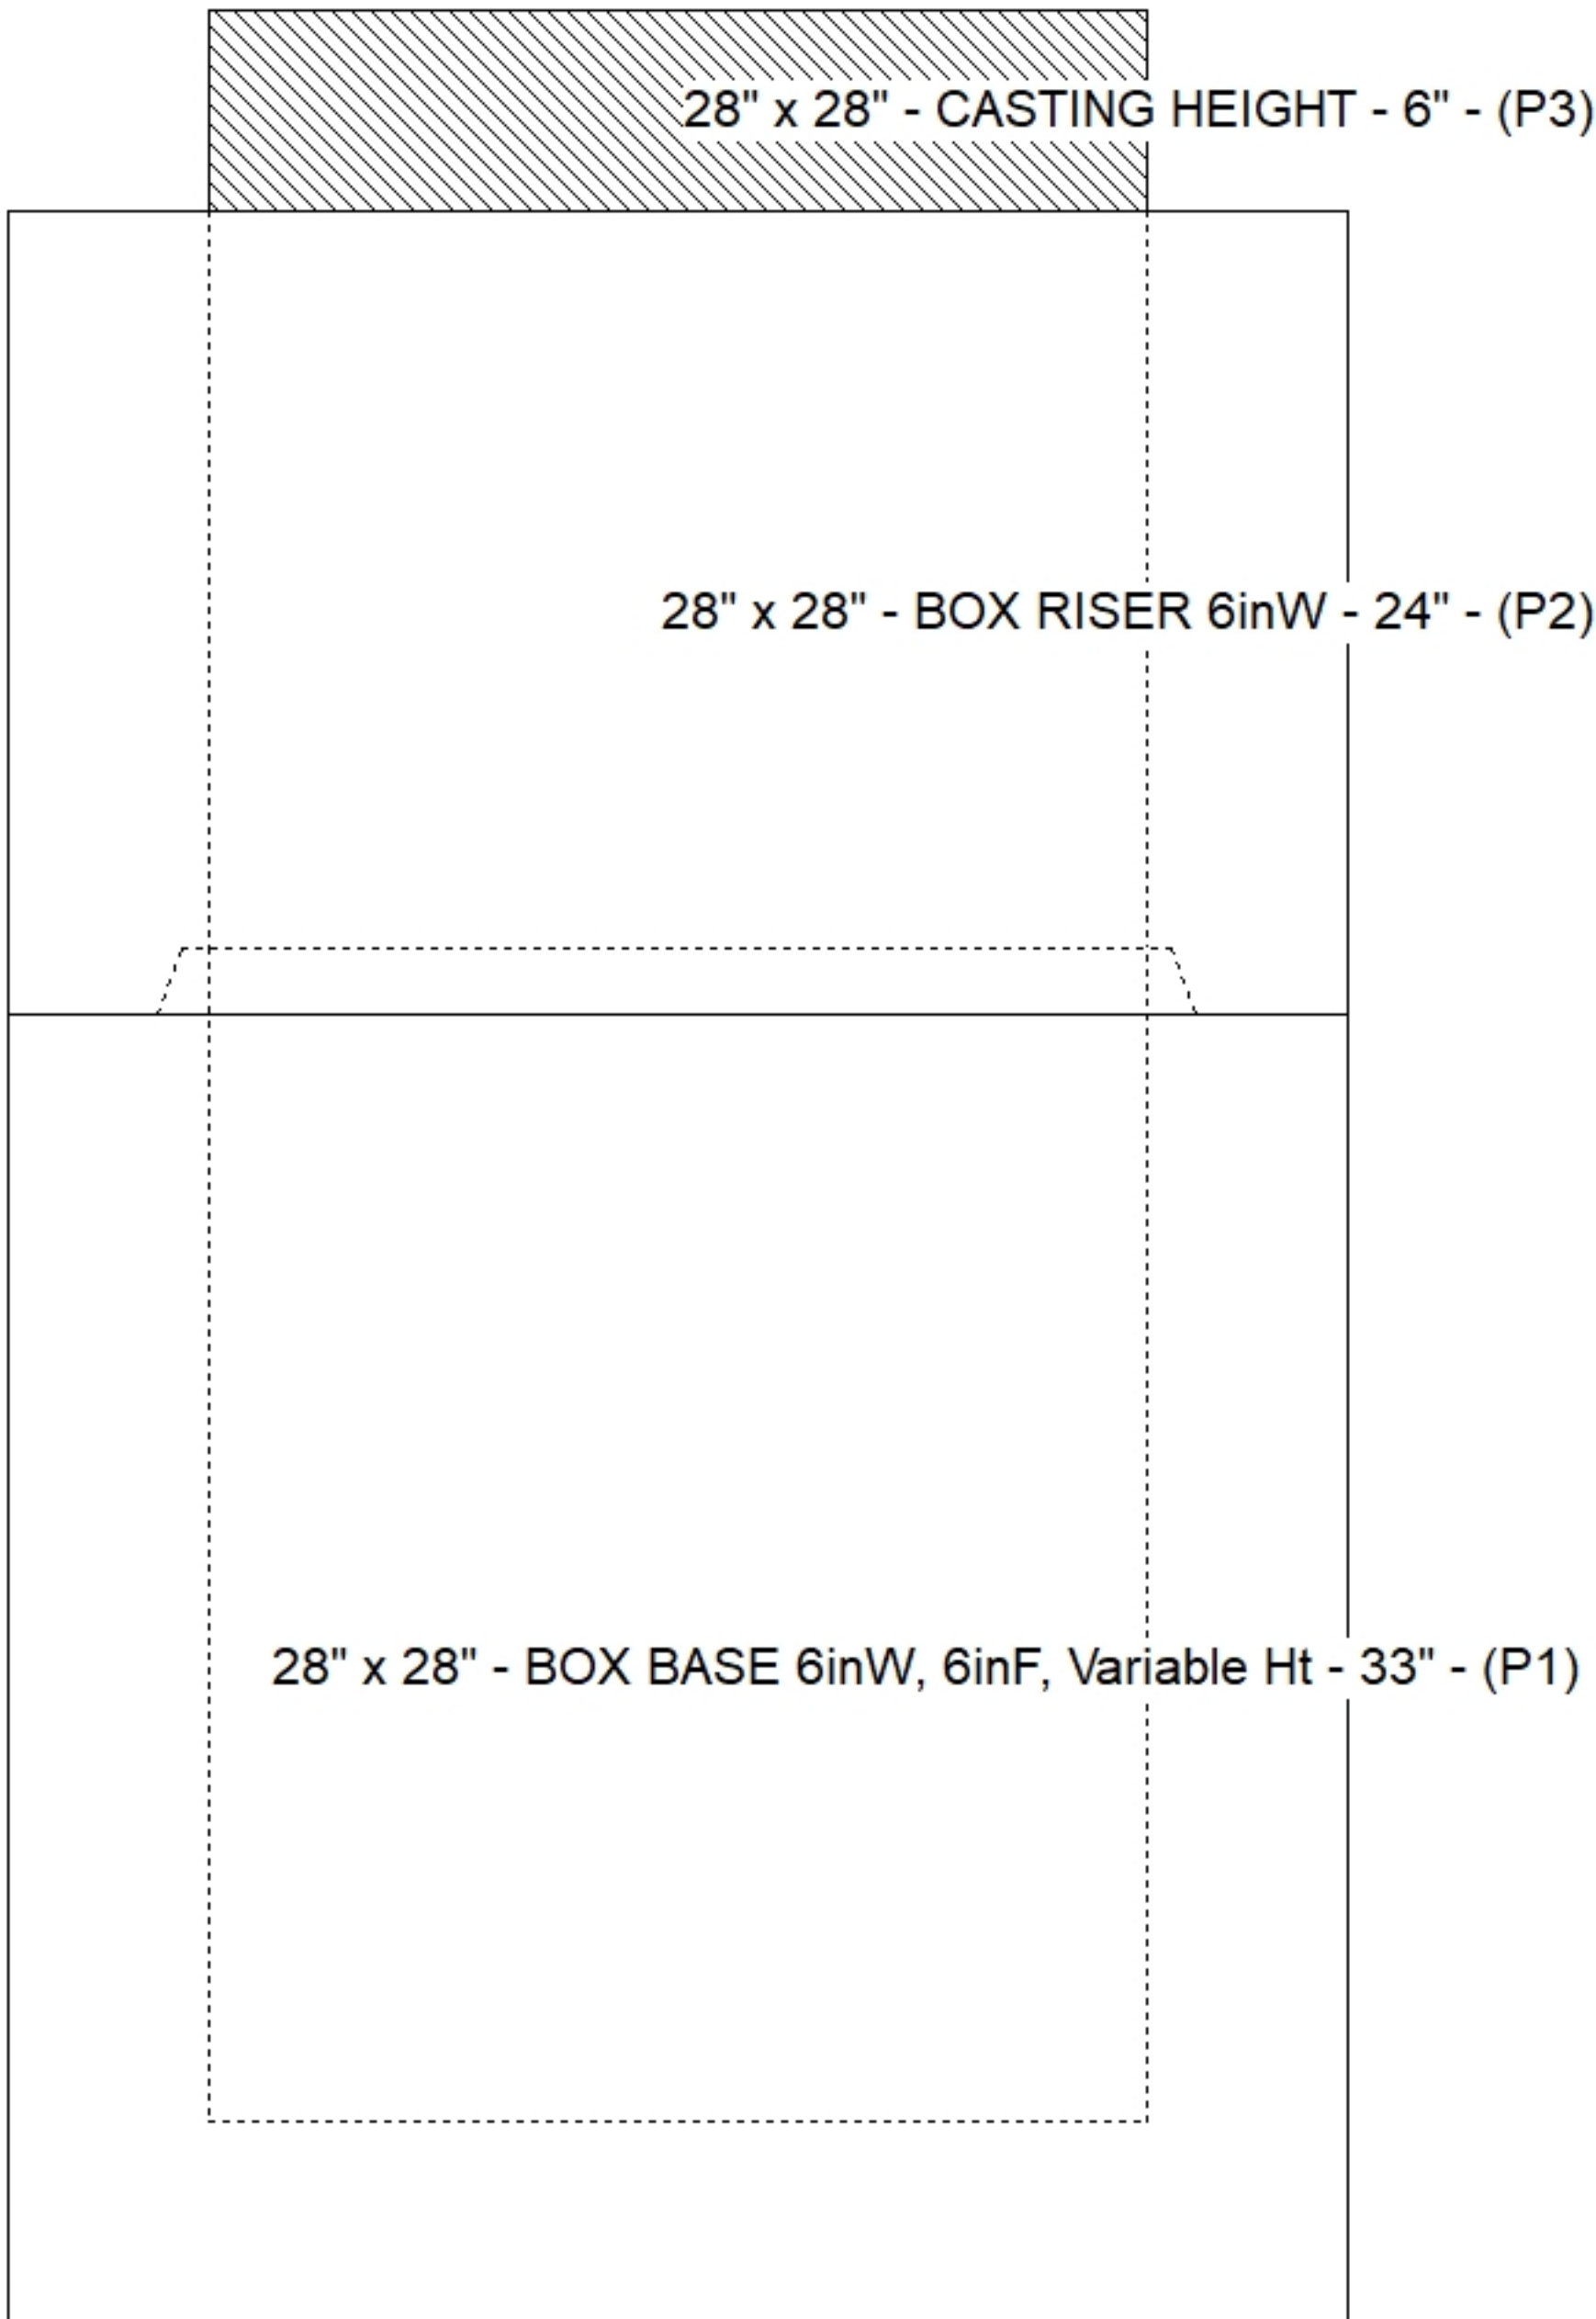

Default - Interior Dimensions

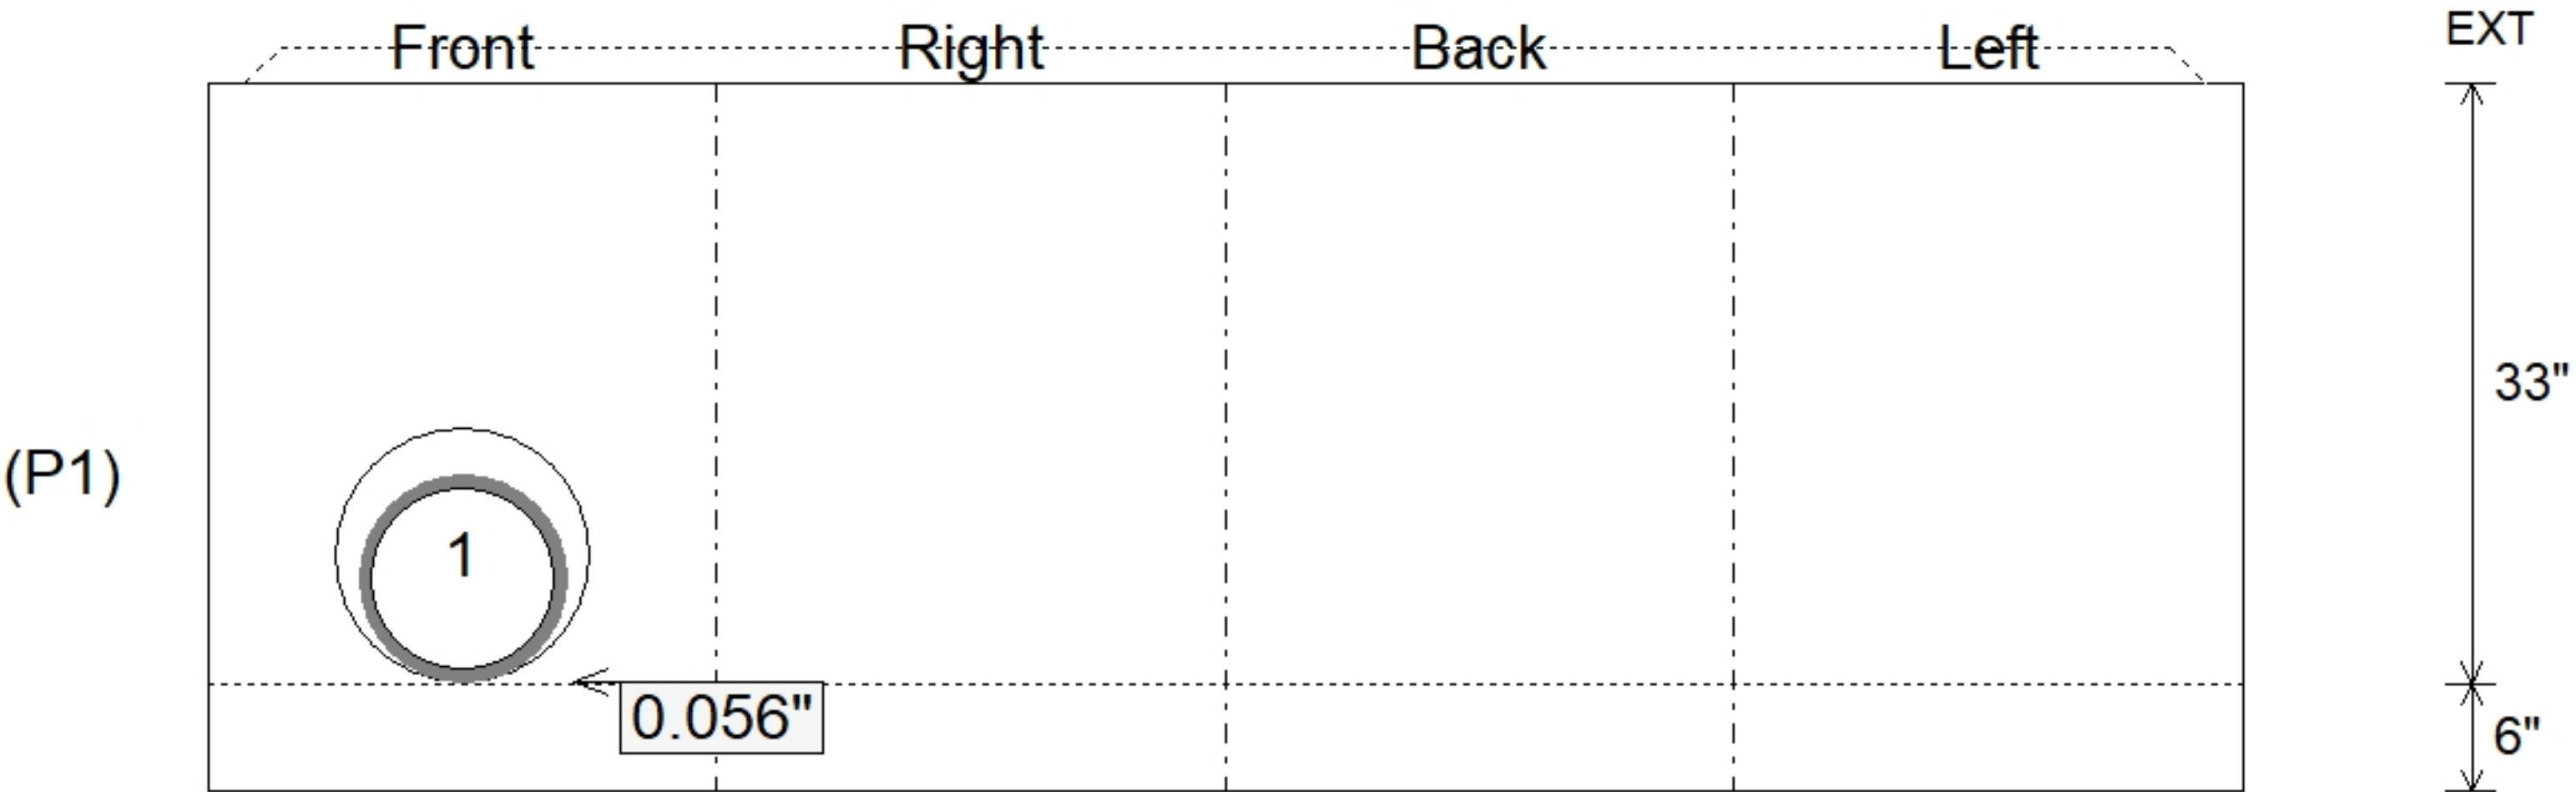

Submittal Drawing
6/16/2026 9:05:51 AM

SUBMITTAL
APPROVED BY:
