

Contractor: Hayes Pipe Supply

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 3.45'

Floor Height: 6"

Slack: 1.4"

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING SUPPLIED BY OTHERS.

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 32" - CASTING HEIGHT - 6"

P2) 48" - MH FLAT TOP w/32" Hole CC w/ConBlock-CDA Red - 12"

0 lb

P1) 48" - MH BASE w/ConBlock-CDA Red - 24"

2911 lb

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

0 lb

1) ADMIXTURE CONBLOCK CDA RED

0 lb

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

0 lb

1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT

1440 lb

1) 48" - Conseal CS-102 1.00" (Double)

0 lb

1) PSX - 12-08 NYLO

8 lb


1) PSX - 12-06 NYLO

8 lb

2) MH Step ML-10-TDS-NCR - 10"



0 lb

Structure Total: 5718 lb

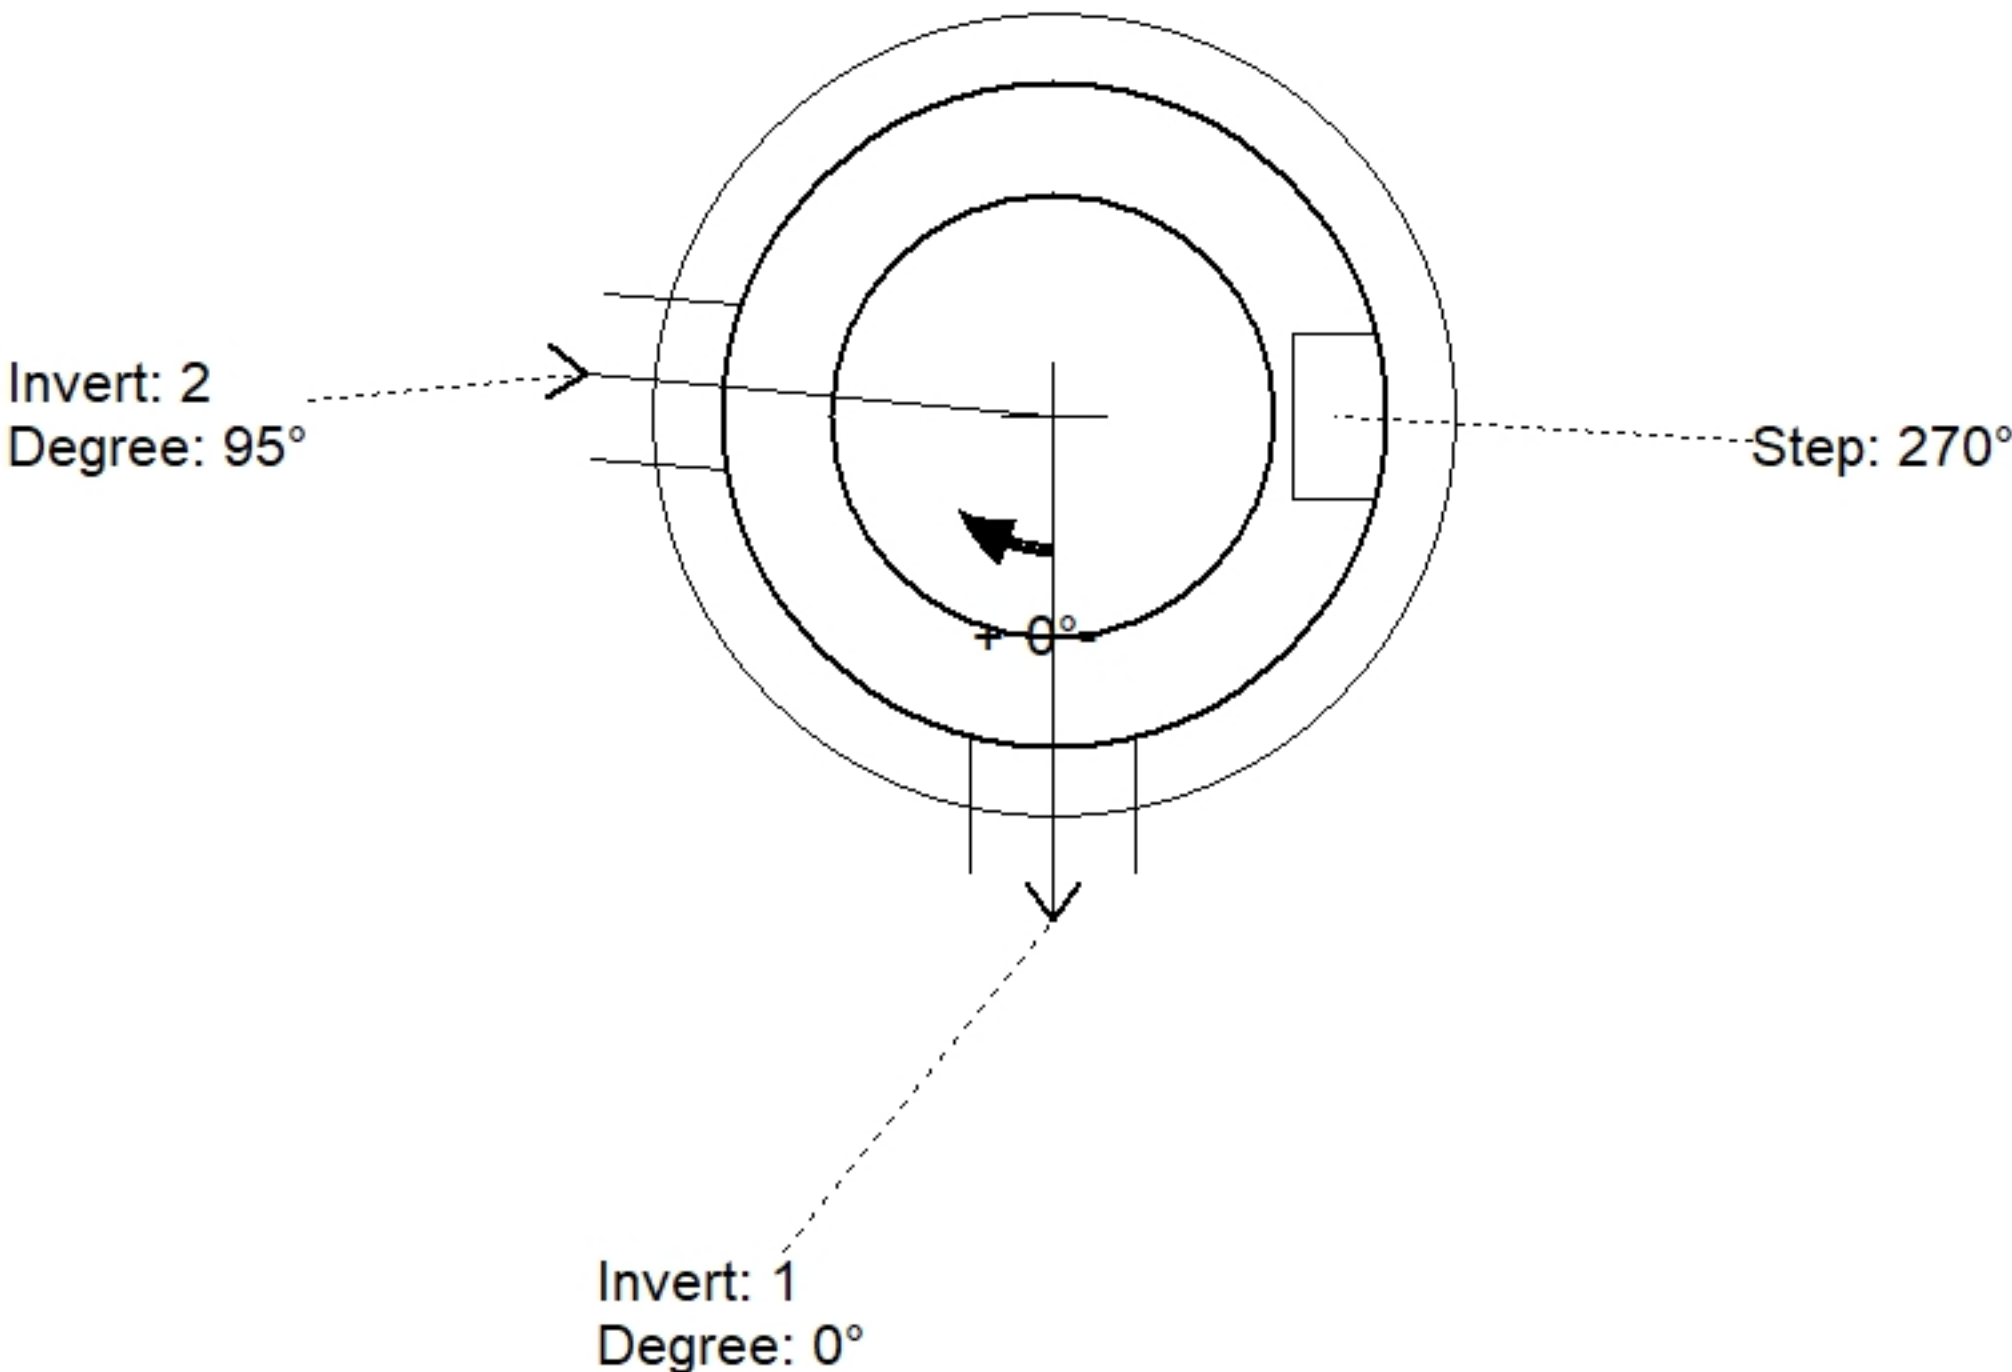

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	431.91'							
Reducer								
Invert 1	428.46'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	428.66'	95°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	1.4"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

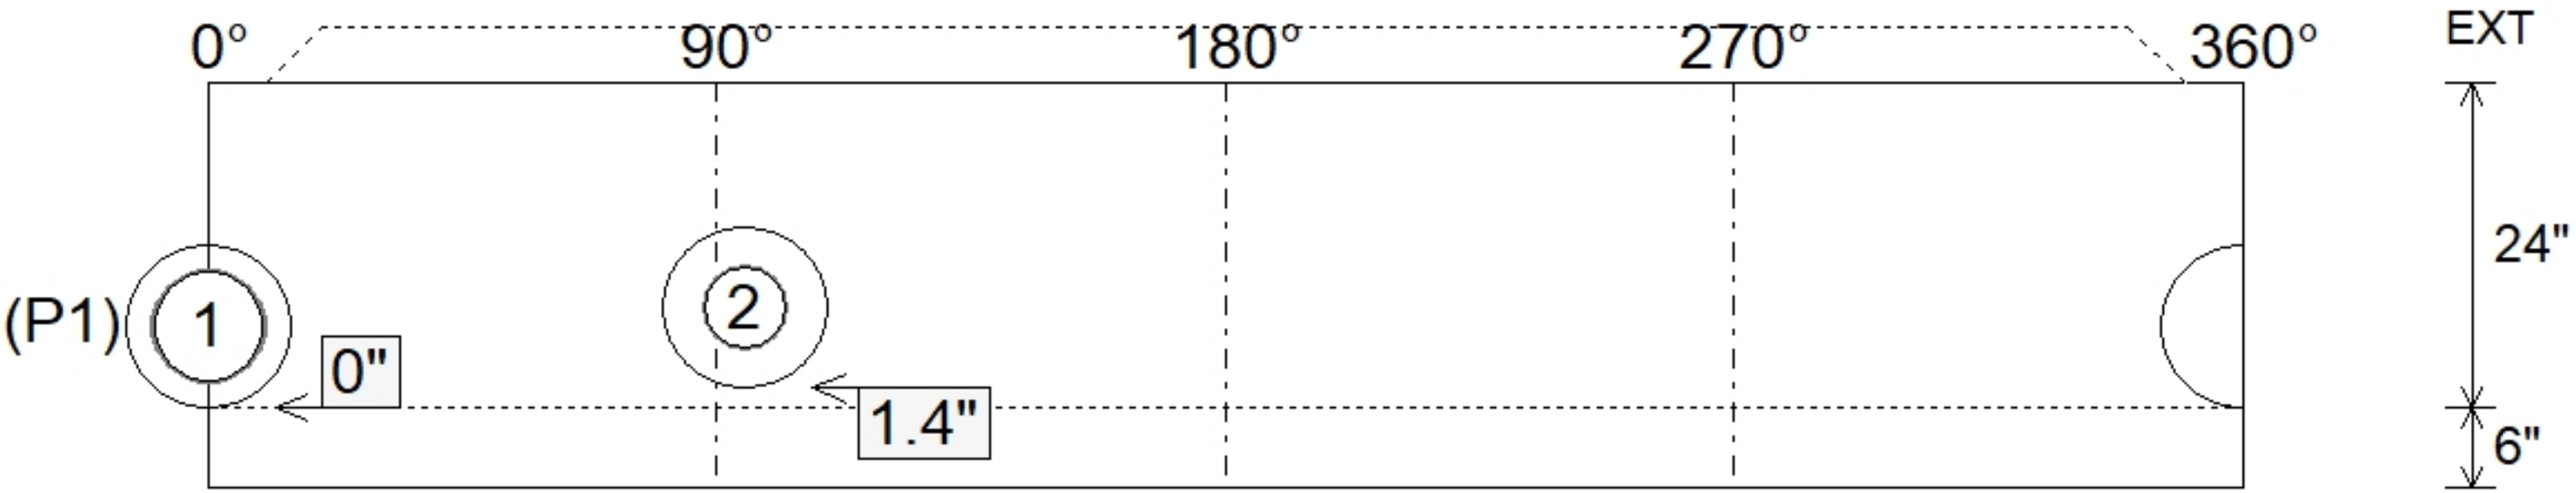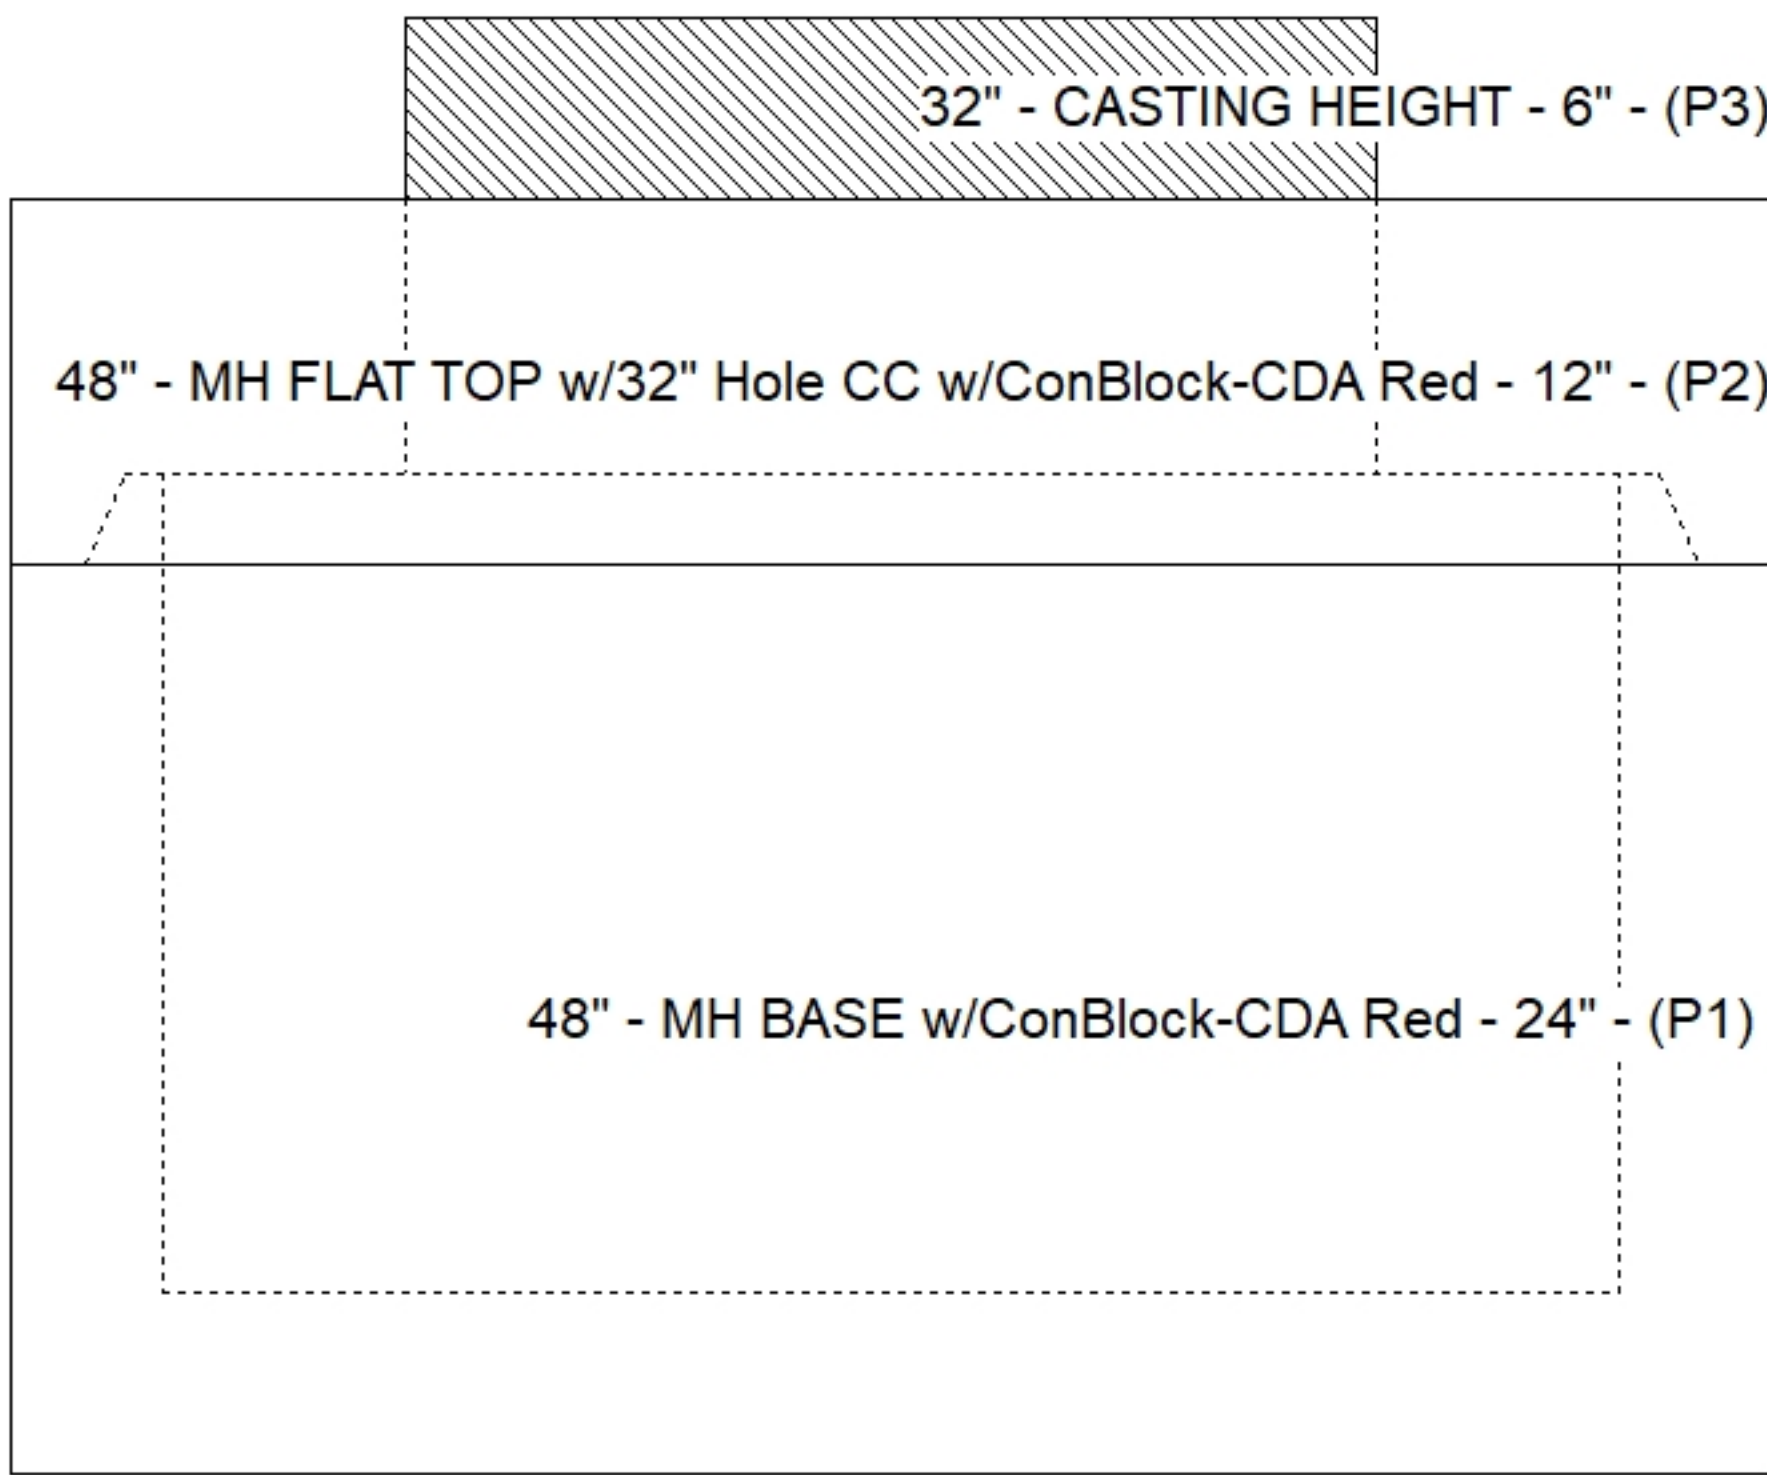

Submittal Drawing
7/9/2026 8:10:28 AM

SUBMITTAL
APPROVED BY:
