

Job Name: 26-2310 - 3rd & Madison Townhomes - Ph. 1 Job Location: Nashville, TN 37208 Contractor: Hayes Pipe Supply					Plant: 100		Tech: Jared - F			
					6/15/2026 11:39:51 AM		PC: E. Bradley			
Structure ID: PMH3 SS-MH										
P1 MH048BA18CDARED					MH BASE w/ConBlock-CDA Red T/n					
P3) 24" - CASTING HEIGHT - 7" P2) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 36" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 18" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) ADMIXTURE CONBLOCK CDA RED 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 4) MH Step ML-10-TDS-NCR - 10"					0 lb 2251 lb 2540 lb 0 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 8 lb 0 lb ----- Structure Total: 6239 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 427.86' Rim to Invert: 5.04' Slack: 1.48" Sump: 2" Step Position: 180										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	422.82'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 18" Height (Ext): 24"	Weight (Net): 2540 lb Volume (Net): 0.65cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-2310 - 3rd & Madison Townhomes - Ph. 1

Job Location: Nashville, TN 37208

Contractor: Hayes Pipe Supply

Plant: 100

6/15/2026 11:39:51 AM

Tech: Jared - F

PC: E. Bradley



Structure ID: PMH3 SS-MH

P1 MH048BA18CDARED

MH BASE w/ConBlock-CDA Red T/n

P3) 24" - CASTING HEIGHT - 7"

P2) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 36"

P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 18"

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) ADMIXTURE CONBLOCK CDA RED

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT

1) 48" - Conseal CS-102 1.00" (Double)

1) 24" - Conseal CS-102 1.00" (Double)

1) PSX - 12-08 NYLO

4) MH Step ML-10-TDS-NCR - 10"

0 lb

2251 lb

2540 lb

0 lb

0 lb

0 lb

1440 lb

0 lb

0 lb

8 lb

0 lb

Structure Total: 6239 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. ADMIXTURE = CONBLOCK CDA RED.

4. CASTING SUPPLIED BY OTHERS.

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)


- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


Rim: 427.86' Rim to Invert: 5.04' Slack: 1.48" Sump: 2" Step Position: 180


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	422.82'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

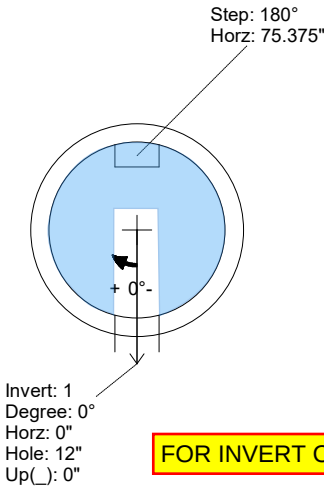


UPSIDE-DOWN VIEW (int. dimensions)

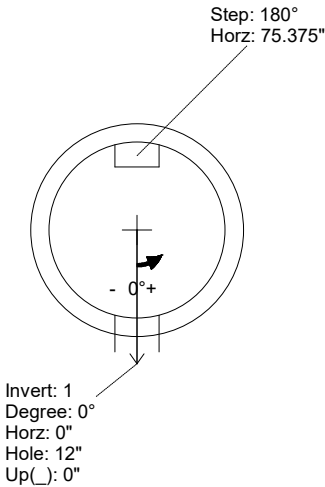

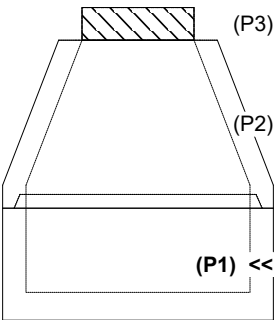

INSIDE WALL DIMENSIONS



Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 5"

Floor Height: 6"

Height (Int): 18"

Height (Ext): 24"

Weight (Net): 2540 lb

Volume (Net): 0.65cu.yd
