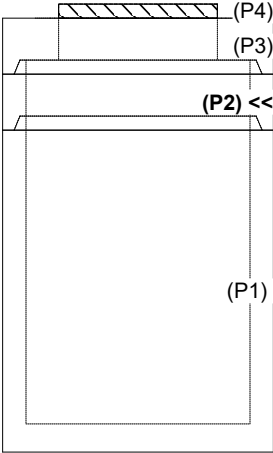




Job Name: 26-2372 - Bosse Field Turf and Drainage Upgrade Job Location: Evansville, IN Contractor: Hahn Excavating, Inc.					Plant: 100 10/8/2026 12:57:54 PM		Tech: Jared - F PC: E. Bradley				
Structure ID: AD 102 ST-AD											
P2		MH048RS12		MH RISER T/G							
P4) 34" x 34" - CASTING HEIGHT - 3" P3) 48" - MH FLAT TOP w/34"x34" Hole F/G - 12" P2) 48" - MH RISER T/G - 12" P1) 48" - MH BASE Custom Ht T/n - 63" 1) CASTING - HOE 595 F/G 2) 48" - Conseal CS-102 1.00" 2) Hole - 26 1) Hole - 12 5) MH Step ML-10-TDS-NCR - 10"					0 lb 1194 lb 838 lb 5217 lb 376 lb 0 lb 0 lb 0 lb 0 lb ----- 7625 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 595 F/G). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 380.13' Rim to Invert: 7.3' Slack: 0.1" Sump: 2.5" Step Position: 120											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
(P2)										EXT 12"	
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 12" Height (Ext): 12"		Weight (Net): 838 lb Volume (Net): 0.21cu.yd	
