



Job Name: 26-2372 - Bosse Field Turf and Drainage Upgrade Job Location: Evansville, IN Contractor: Hahn Excavating, Inc.					Plant: 100 10/8/2026 12:04:10 PM		Tech: Jared - F PC: E. Bradley				
Structure ID: AD 104 ST-AD											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P3) 34" x 34" - CASTING HEIGHT - 3" P2) 48" - MH FLAT TOP w/34"x34" Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 46" 1) CASTING - HOE 595 F/G 1) 48" - Conseal CS-102 1.00" 1) Hole - 26 1) Hole - 20 4) MH Step ML-10-TDS-NCR - 10"					0 lb 1194 lb 4175 lb 376 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5745 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 595 F/G). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 384.53' Rim to Invert: 4.92' Slack: 0.54" Sump: 2.5" Step Position: 270											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	379.61'	0°	0"	18" RCP B WALL	23"	Hole 26	26"	27.476"	0"	0"	
Invert 2	379.61'	161°	81.5"	15" HDPE	17.6"	Hole 20	20"	20.629"	1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

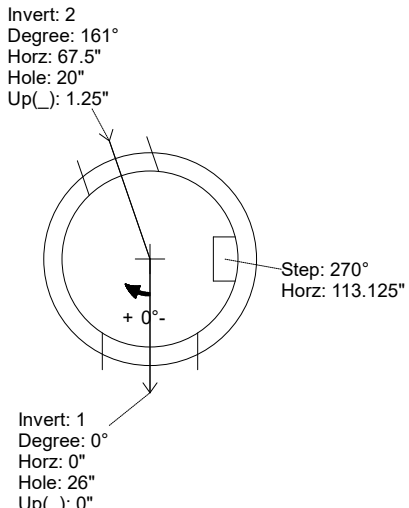

UPSIDE-DOWN VIEW (int. dimensions)

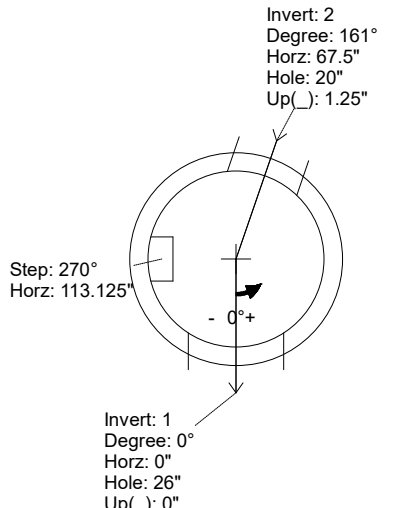

INSIDE WALL DIMENSIONS

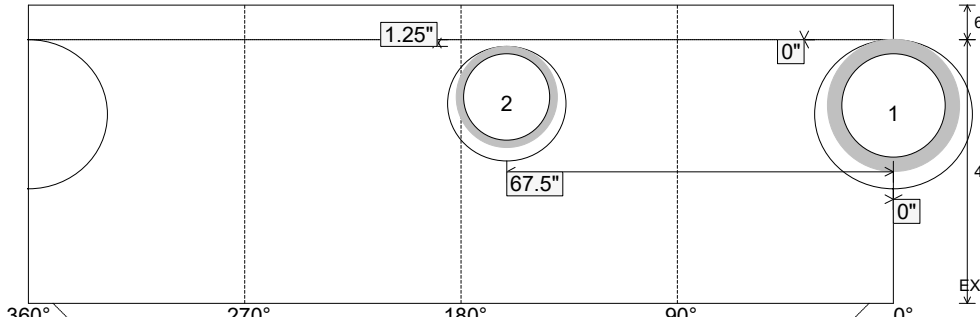

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 46" Height (Ext): 52"	Weight (Net): 4175 lb Volume (Net): 1.07cu.yd
----------------------------------	---------------------------------	--	--	--
