



Job Name: 26-2372 - Bosse Field Turf and Drainage Upgrade Job Location: Evansville, IN Contractor: Hahn Excavating, Inc.					Plant: 100 10/8/2026 12:04:12 PM		Tech: Jared - F PC: E. Bradley				
Structure ID: Ex. AD ST-AD											
P1 BX3636-08BAVF BOX BASE 8inW, 8inF, Variable Ht F/n											
P2) 36" x 36" - CASTING HEIGHT - 3" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 35" 1) CASTING - HOE 595 F/G 1) 36" x 36" - Conseal CS-102 1.00" 1) Hole - 32 1) Hole - 20 1) Hole - 26					0 lb 4809 lb 376 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5185 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 595 F/G). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 373.7' Rim to Invert: 2.96' Slack: 0.52" Sump: 3" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	370.74'	0°	26"	24" RCP B WALL	30"	Hole 32	32"	32"	0"	0"	
Invert 2	370.74'	115°	29.25"	15" VCP	17.75"	Hole 20	20"	22.068"	1.625"	-8"	
Invert 3	370.74'	195°	27.75"	18" RCP B WALL	23"	Hole 26	26"	26.917"	0.5"	-5"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

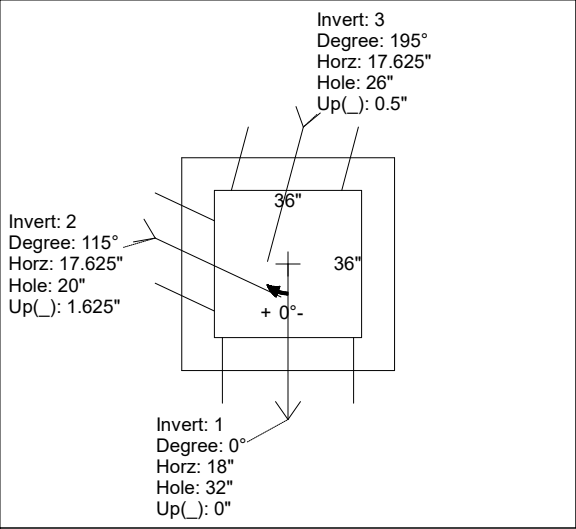

UPSIDE-DOWN VIEW (int. dimensions)

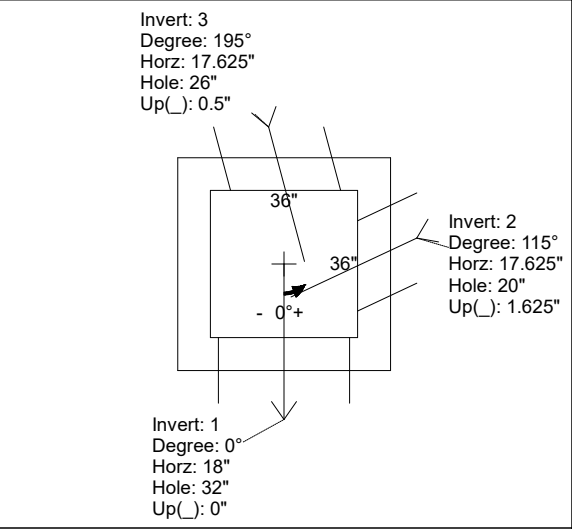

INSIDE WALL DIMENSIONS

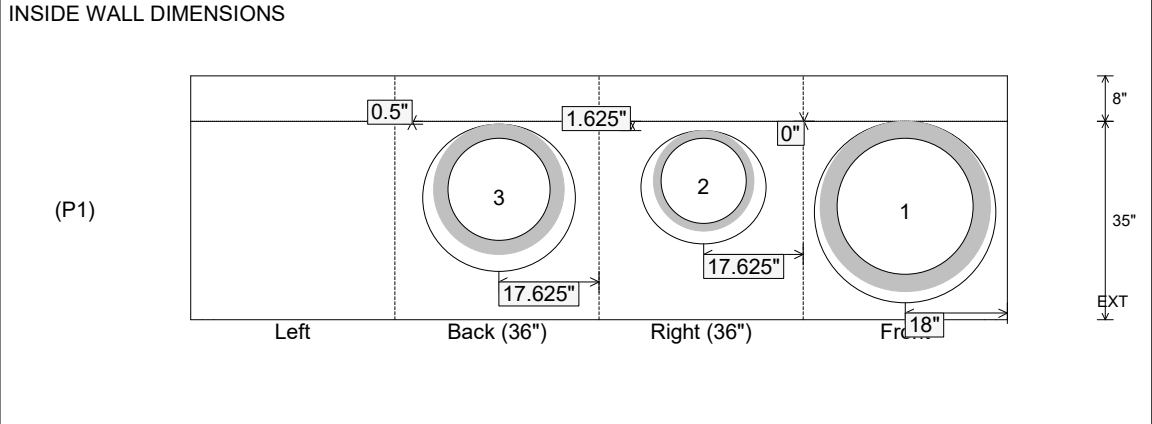

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 35" Height (Ext): 43"	Weight (Net): 4809 lb Volume (Net): 1.23cu.yd
----------------------------------	-------------------------------	--	--	--
