

Job Name: 26-2435 838635 Bridge Park Block J

Job Location: Dublin, OH

Contractor: Contech Engineering Solutions

Plant: Beaver Dam

6/4/2026 8:06:40 AM

Tech: S. Felletter

PC: C. Goff



Structure ID: 20-CS-8

P1MH096BAVF

MH MONOBASE 13F, Custom Ht T/n

P5) 24" - CASTING HEIGHT - 4"

P4) 96" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 17"

P3) 96" - MH RISER T/G - 36"

P2) 96" - MH RISER T/G - 96"

P1) 96" - MH MONOBASE 13F, Custom Ht T/n - 24"

1) CVSTENCILING

1) ASSEMBLY REQUIRED

3) 96" - Conseal CS-102 1.00"

1) 24" - Conseal CS-102 1.00"

3) Hole - 36

0 lb

10015 lb

8819 lb

21710 lb

17113 lb

0 lb

0 lb

0 lb

0 lb

0 lb

57657 lb

Structure Notes:

4" CASTING BY OTHERS

LIFT ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE

ICAST TO INSTALL THE INTERNALS

CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE

Structure Total:

57657 lb

Rim: 841.96'

Rim to Invert: 8'


Slack: 1.044"

Sump: 82.044"


Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)




UPSIDE-DOWN VIEW (int. dimenions)



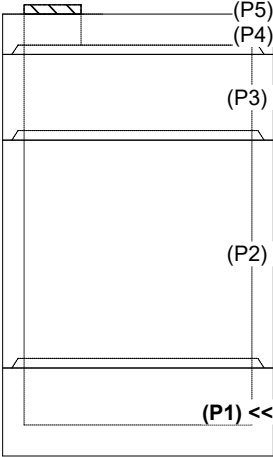

INSIDE WALL DIMENSIONS



Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 9"

Floor Height: 13"

Height (Int): 24"

Height (Ext): 37"

Weight (Net): 17113 lb

Volume (Net): 4.37cu.yd
