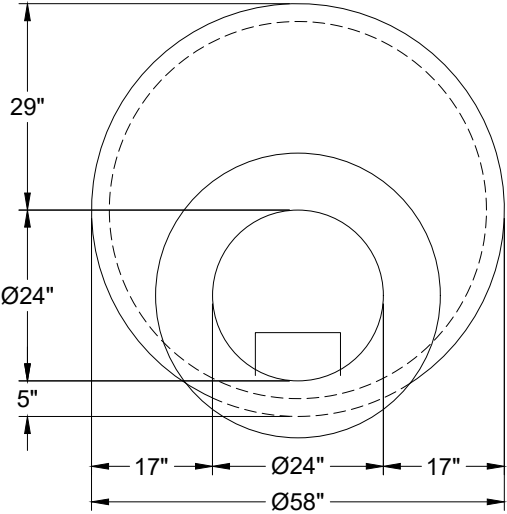


Job Name: 26-2478B - Marcelina Site Improvements San. Job Location: Clarksville, TN 37043 Contractor: Core & Main LP		Plant: Beaver Dam 9/14/2026 1:47:14 PM	Tech: J. Coppage PC: T. Lewis	
Structure ID: FS2 SS-MH				
P4 MH048CN42CDARED		ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G		
P6) 24" - CASTING HEIGHT - 6" P5) 24" - GRADE RING w/ConBlock-CDA Red F/F - 3" P4) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42" P3) 48" - MH RISER w/ConBlock-CDA Red T/G - 72" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 72" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 3) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 16Y NYLO 18) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 3116 lb 5030 lb 5030 lb 2835 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 16 lb 0 lb ----- 17670 lb	<u>Structure Notes:</u> . 1. (6" TALL CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = CONBLOCK CDA RED. 5. REINFORCING PER ASTM A615 (GRADE 60)	
				
48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42" - (P4) 				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3116 lb Volume (Net): 0.8cu.yd
