



Job Name: 26-2478B - Marcelina Site Improvements San. Job Location: Clarksville, TN 37043 Contractor: Core & Main LP					Plant: Beaver Dam 9/14/2026 1:46:44 PM		Tech: J. Coppage PC: T. Lewis						
Structure ID: FS4 SS-MH													
P3 MH060RS72SCDR			MH RISER SPECIAL w/ConBlock-CDA Red T/G										
P5) 24" - CASTING HEIGHT - 6" P4) 60" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G - 13" P3) 60" - MH RISER SPECIAL w/ConBlock-CDA Red T/G - 72" P2) 60" - MH RISER w/ConBlock-CDA Red T/G - 72" P1) 60" - MH BASE Custom Ht, w/ConBlock-CDA Red T/n - 50" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 60" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 3) 60" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 16Y NYLO 16) MH Step ML-10-TDS-NCR - 10"						0 lb 2800 lb 7414 lb 7516 lb 7748 lb 0 lb 0 lb 2962 lb 0 lb 0 lb 24 lb 0 lb ----- 28464 lb		Structure Notes: . 1. (6" TALL CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = CONBLOCK CDA RED. 5. REINFORCING PER ASTM A615 (GRADE 60). 6. INTERNAL DROP PROVIDED BY OTHERS - ICAST TO SUPPLY OPENINGS & BOOTS					
Rim: 462.7' Rim to Invert: 17.52' Slack: 0.24' Sump: 3' Step Position: 78.5°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3	457'	254°	159.625"	10" PVC SDR26	10.5"	PSX 16Y NYLO	16"	16.196"	15.125"	0"			
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													

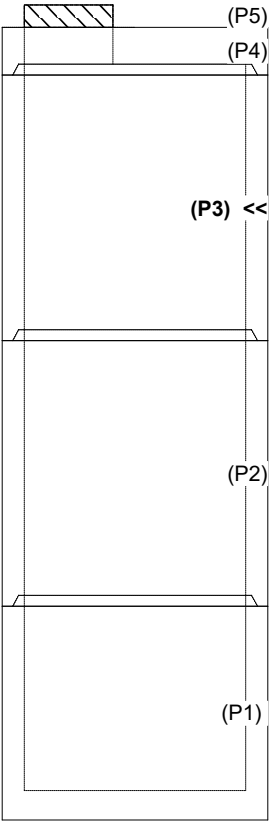

(P5)
(P4)
(P3) <<
(P2)
(P1)


RIGHT-SIDE UP VIEW (int. dimensions)



Step: 78.5°
Horz: 41.125"

Invert: 3
Degree: 254°
Horz: 133"
Hole: 16"
Up(): 15.125"

INSIDE WALL DIMENSIONS

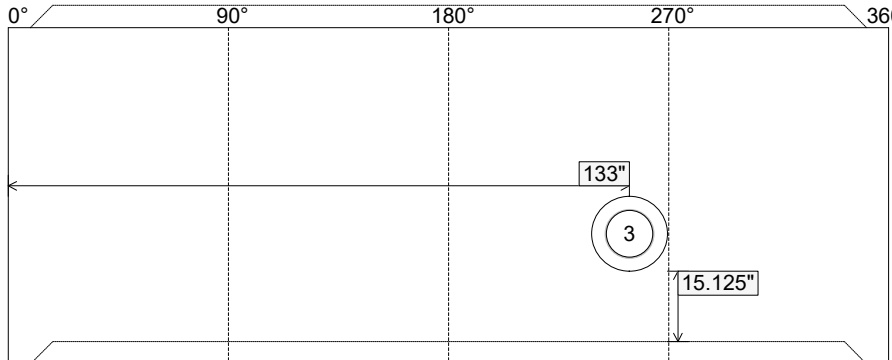

(P3)

133"

3

15.125"

EXT

72"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6" Floor Height: 0"	Height (Int): 72" Height (Ext): 72"	Weight (Net): 7414 lb Volume (Net): 1.89cu.yd
----------------------------------	------------------------------------	--	--	--
