

Job Name: 26-2478B - Marcelina Site Improvements San.
Job Location: Clarksville, TN 37043
Contractor: Core & Main LP

Plant: Beaver Dam

Tech: J. Coppage

9/14/2026 4:53:44 PM

PC: T. Lewis



Structure ID: FS8 SS-MH

P4 MH060LD13CDARED

MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G



- P5) 24" - CASTING HEIGHT - 6"
P4) 60" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G - 13"
P3) 60" - MH RISER w/ConBlock-CDA Red T/G - 48"
P2) 60" - MH RISER w/ConBlock-CDA Red T/G - 48"
P1) 60" - MH BASE Custom Ht, w/ConBlock-CDA Red T/n - 26"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 60" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
3) 60" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
2) PSX - 16Y NYLO
10) MH Step ML-10-TDS-NCR - 10"

0 lb
2800 lb
5011 lb
5011 lb
5243 lb
0 lb
0 lb
2962 lb
0 lb
0 lb
16 lb
0 lb

Structure Total: 21043 lb

Structure Notes:

1. (6" TALL CASTING PROVIDED BY OTHERS)
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. ADMIXTURE = CONBLOCK CDA RED.
5. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
6. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING

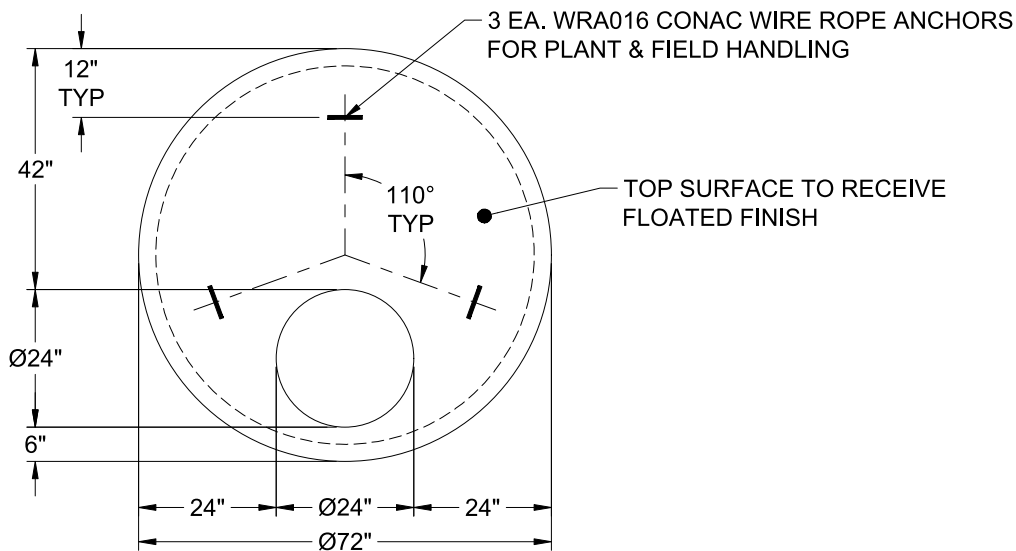

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 6"

Height (Ext): 13"

Weight (Net): 2800 lb
Volume (Net): 0.69cu.yd
