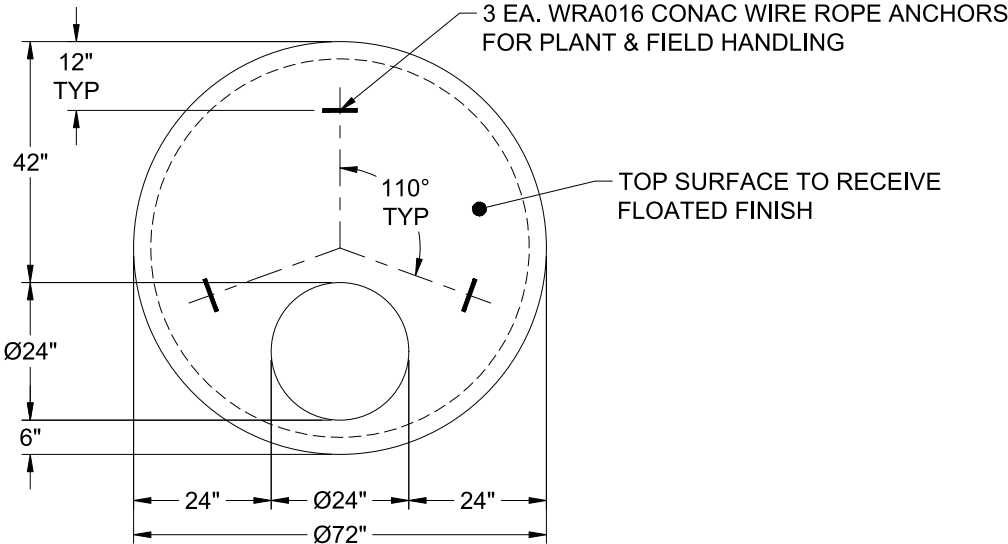



Job Name: 26-2478B - Marcelina Site Improvements San. Job Location: Clarksville, TN 37043 Contractor: Core & Main LP		Plant: Beaver Dam 9/14/2026 4:53:44 PM	Tech: J. Coppage PC: T. Lewis		
Structure ID: FS9 SS-MH					
P4 MH060LD13CDARED		MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G			
P6) 24" - CASTING HEIGHT - 6" P5) 24" - GRADE RING w/ConBlock-CDA Red F/F - 6" P4) 60" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G - 13" P3) 60" - MH RISER w/ConBlock-CDA Red T/G - 72" P2) 60" - MH RISER w/ConBlock-CDA Red T/G - 60" P1) 60" - MH BASE Custom Ht. w/ConBlock-CDA Red T/n - 32" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 60" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 3) 60" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 16Y NYLO 1) PSX - 12-08 NYLO 13) MH Step ML-10-TDS-NCR - 10"		0 lb 405 lb 2800 lb 7459 lb 6264 lb 5869 lb 0 lb 0 lb 2962 lb 0 lb 0 lb 16 lb 8 lb 0 lb Structure Total: 25783 lb	Structure Notes: . 1. (6" TALL CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = CONBLOCK CDA RED. 5. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 6. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING		
					
					
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 6"	Height (Ext): 13"	Weight (Net): 2800 lb Volume (Net): 0.69cu.yd	
