


Job Name: 26-2478B - Marcelina Site Improvements San.
Job Location: Clarksville, TN 37043
Contractor: Core & Main LP

Plant: Beaver Dam

Tech: J. Coppage

9/14/2026 4:53:48 PM

PC: T. Lewis



Structure ID: FV1 SS-MH

P5 GR4CDARED

GRADE RING w/ConBlock-CDA Red F/F

P6) 24" - CASTING HEIGHT - 6"
P5) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4"
P4) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 24"
P3) 48" - MH RISER w/ConBlock-CDA Red T/G - 36"
P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 48"
P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
3) 48" - Conseal CS-102 1.00" (Double)
2) 24" - Conseal CS-102 1.00" (Double)
2) PSX - 12-08 NYLO
11) MH Step ML-10-TDS-NCR - 10"


0 lb
270 lb
1738 lb
2515 lb
3353 lb
2911 lb
0 lb
0 lb
1440 lb
0 lb
0 lb
16 lb
0 lb

Structure Total:


12243 lb

Structure Notes:


1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: (1) #3 HOOP CENTERED (GRADE 60)
4. CONBLOCK CDA RED ADMIXTURE REQUIRED

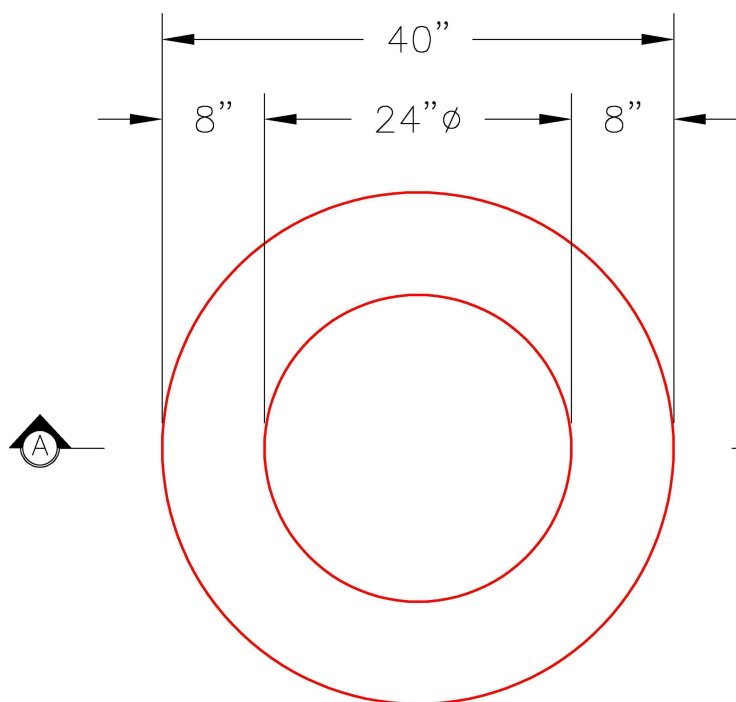

PLAN VIEW



ISOMETRIC VIEW

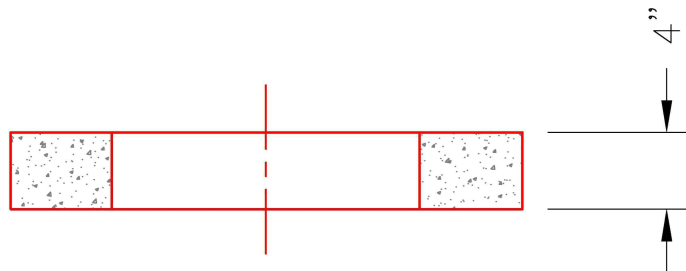

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 4"

Weight (Net): 270 lb
Volume (Net): 0.07cu.yd
