




Job Name: 26-2478B - Marcelina Site Improvements San. Job Location: Clarksville, TN 37043 Contractor: Core & Main LP					Plant: Beaver Dam 9/14/2026 4:48:09 PM		Tech: J. Coppage PC: T. Lewis				
Structure ID: FX1 SS-MH											
P1 MH048BA24CDARED					MH BASE w/ConBlock-CDA Red T/n						
P5) 24" - CASTING HEIGHT - 6" P4) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" P3) 48" - MH RISER w/ConBlock-CDA Red T/G - 48" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 48" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 13) MH Step ML-10-TDS-NCR - 10"					0 lb 1961 lb 3353 lb 3353 lb 2863 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 24 lb 0 lb		Structure Notes: . 1. (6" TALL CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = CONBLOCK CDA RED. 5. REINFORCING PER ASTM A615 (GRADE 60).				
Structure Total:					12995 lb						
Rim: 520' Rim to Invert: 12.93' Slack: 1.16" Sump: 2" Step Position: 263°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌋)	Offset	
Invert 1	507.07'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	507.17'	90°	45.5"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"	
Invert 3	507.17'	166°	84"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

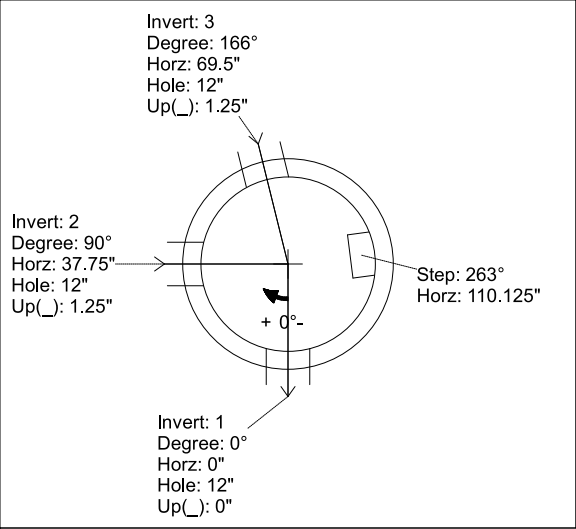

RIGHT-SIDE UP VIEW (int. dimensions)

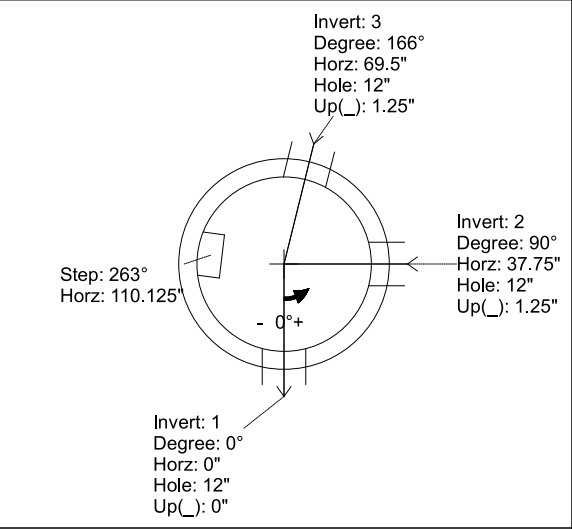


UPSIDE-DOWN VIEW (int. dimensions)

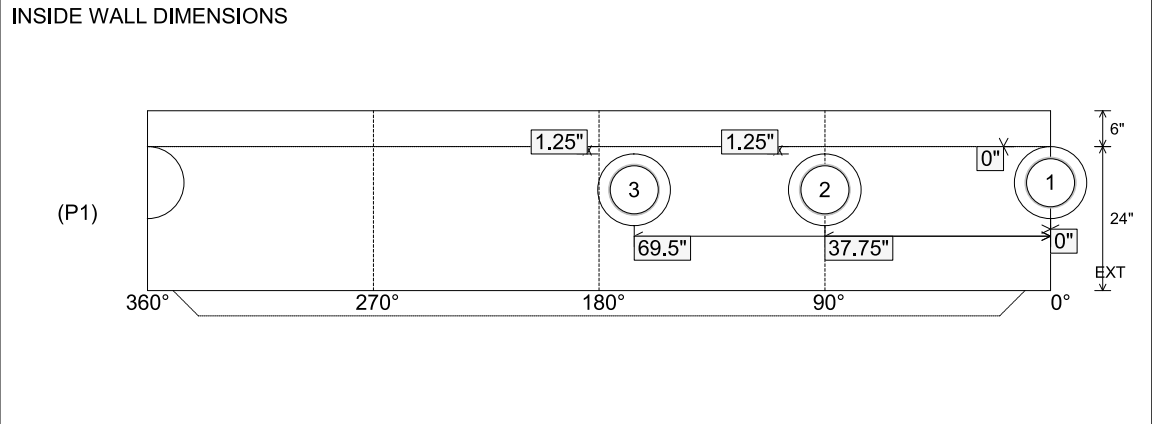


INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2863 lb Volume (Net): 0.73cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-2478B - Marcelina Site Improvements San. Job Location: Clarksville, TN 37043 Contractor: Core & Main LP					Plant: Beaver Dam 9/14/2026 4:48:09 PM		Tech: J. Coppage PC: T. Lewis				
Structure ID: FX1 SS-MH											
P1 MH048BA24CDARED					MH BASE w/ConBlock-CDA Red T/n						
P5) 24" - CASTING HEIGHT - 6" P4) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" P3) 48" - MH RISER w/ConBlock-CDA Red T/G - 48" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 48" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 13) MH Step ML-10-TDS-NCR - 10"					0 lb 1961 lb 3353 lb 3353 lb 2863 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 24 lb 0 lb Structure Total: 12995 lb		Structure Notes: . 1. (6" TALL CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = CONBLOCK CDA RED. 5. REINFORCING PER ASTM A615 (GRADE 60).				
Rim: 520' Rim to Invert: 12.93' Slack: 1.16" Sump: 2" Step Position: 263"											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	507.07'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	507.17'	90°	45.5"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"	
Invert 3	507.17'	166°	84"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

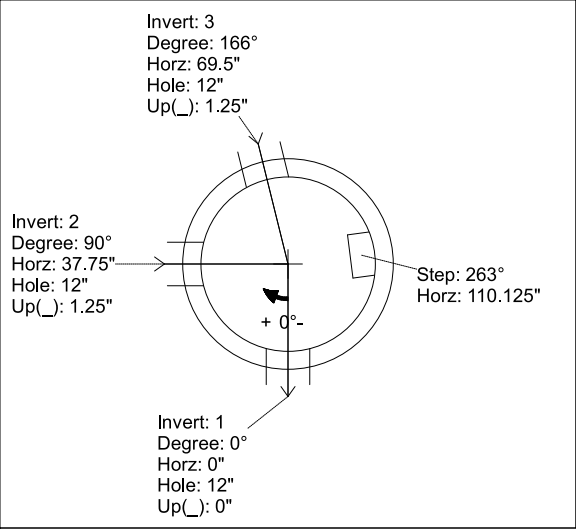

RIGHT-SIDE UP VIEW (int. dimensions)

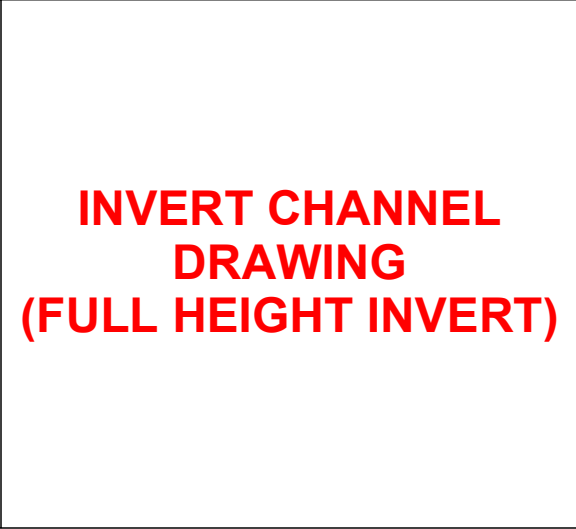

UPSIDE-DOWN VIEW (int. dimenions)


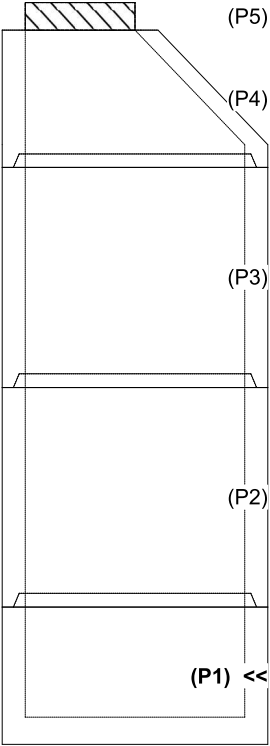


Diagram showing structure components (P1) through (P5) and internal dimensions.

INVERT CHANNEL DRAWING (FULL HEIGHT INVERT)

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2863 lb Volume (Net): 0.73cu.yd
----------------------------------	---------------------------------	--	--	--
