



Job Name: 26-2484 Bass Pro Shops Outpost Paducah Job Location: Paducah, KY Contractor: Central Paving Co. of Paducah, Inc.					Plant: Beaver Dam 6/16/2026 8:02:27 AM		Tech: S. Felletter PC: A. Chambers				
Structure ID: X3 ST-CI											
P1 MH060BA60		MH BASE T/n									
P4) 24" x 24" - CASTING HEIGHT - 5" P3) 24" x 24" - GRADE RING F/F - 3" P2) 60" - MH FLAT TOP w/24"x24" Hole F/G - 13" P1) 60" - MH BASE T/n - 60" 1) CASTING - HOE KY-465 SET (CBI TY F) 1) 60" - Conseal CS-102 1.00" 2) 24" x 24" - Conseal CS-102 1.00" 3) Hole - 30"						0 lb 258 lb 2619 lb 7887 lb 465 lb 0 lb 0 lb 0 lb ----- Structure Total: 11229 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 465 F/G/H). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.			
Rim: 369.19' Rim to Invert: 6.79' Slack: 2.38" Sump: 1.9" Step Position: 270°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	362.4'	0°	0"	24" HDPE	27.8"	Hole 30	30"	31.416"	0"	0"	
Invert 2	363.8'	90°	56.549"	24" HDPE	27.8"	Hole 30	30"	31.416"	16.8"	0"	
Invert 3	362.4'	270°	169.646"	24" HDPE	27.8"	Hole 30	30"	31.416"	0"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

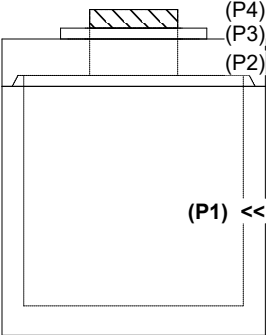

(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

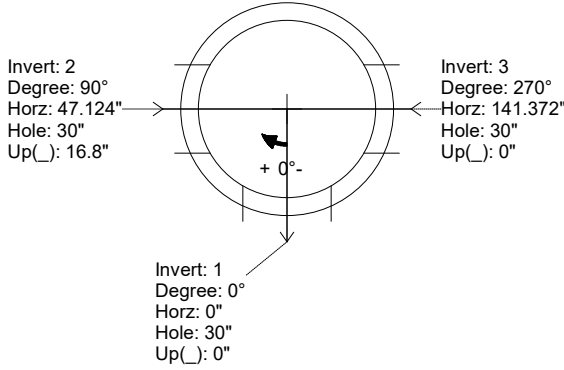


Invert: 2
Degree: 90°
Horz: 47.124"
Hole: 30"
Up(): 16.8"

Invert: 3
Degree: 270°
Horz: 141.372"
Hole: 30"
Up(): 0"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 30"
Up(): 0"

UPSIDE-DOWN VIEW (int. dimensions)

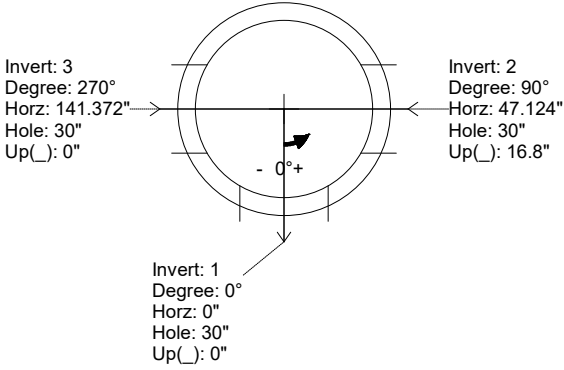


Invert: 3
Degree: 270°
Horz: 141.372"
Hole: 30"
Up(): 0"

Invert: 2
Degree: 90°
Horz: 47.124"
Hole: 30"
Up(): 16.8"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 30"
Up(): 0"

INSIDE WALL DIMENSIONS

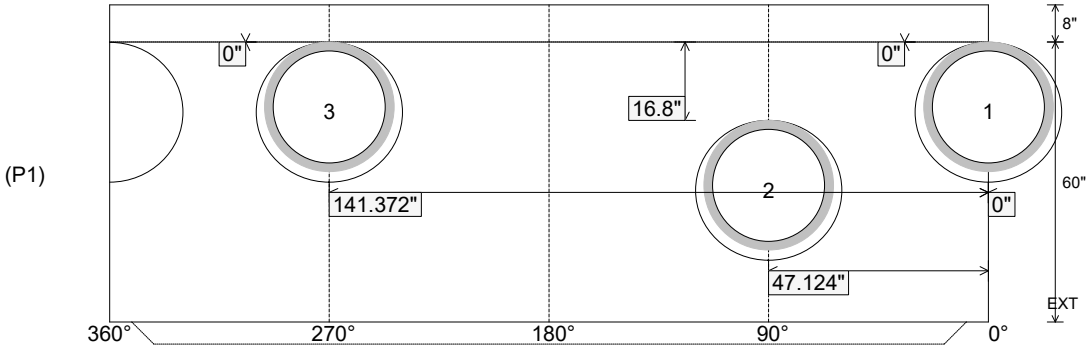

(P1)

Horizontal dimensions: 0", 141.372", 16.8", 47.124", 0"

Vertical dimensions: 8", 60", EXT

Angles: 360°, 270°, 180°, 90°, 0°

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 60" Height (Ext): 68"	Weight (Net): 7887 lb Volume (Net): 2.02cu.yd
----------------------------------	---------------------------------	--	--	--
