

Job Name: 26-2484 Bass Pro Shops Outpost Paducah
Job Location: Paducah, KY
Contractor: Central Paving Co. of Paducah, Inc.

Plant: Beaver Dam
6/16/2026 8:03:41 AM

Tech: S. Felletter
PC: A. Chambers



Structure ID: X3 ST-CI

P2 MH060LD13-24SQ

MH FLAT TOP w/24"x24" Hole F/G



- P4) 24" x 24" - CASTING HEIGHT - 5"
P3) 24" x 24" - GRADE RING F/F - 3"
P2) 60" - MH FLAT TOP w/24"x24" Hole F/G - 13"
P1) 60" - MH BASE T/n - 60"
1) CASTING - HOE KY-465 SET (CBI TY F)
1) 60" - Con seal CS-102 1.00"
2) 24" x 24" - Con seal CS-102 1.00"
3) Hole - 30

0 lb
258 lb
2619 lb
7887 lb
465 lb
0 lb
0 lb
0 lb
Structure Total: 11229 lb

- Structure Notes:**
1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. CASTING BY ICAST (HOE 465 F/G/H).
- REINFORCING PER ASTM A615 (GRADE 60).**
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .18)
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

GENERAL NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 @ 6" C.C. E.W. PER ASTM A615 (GRADE 60)

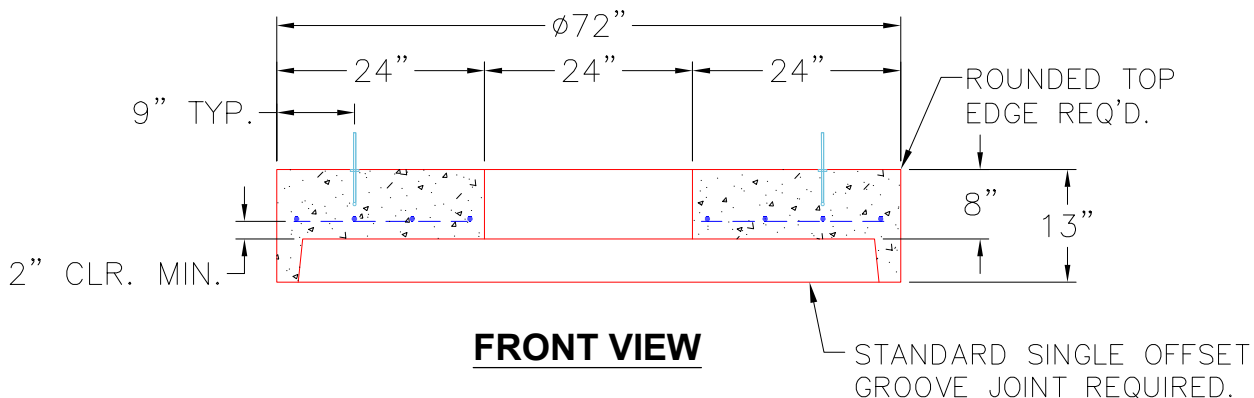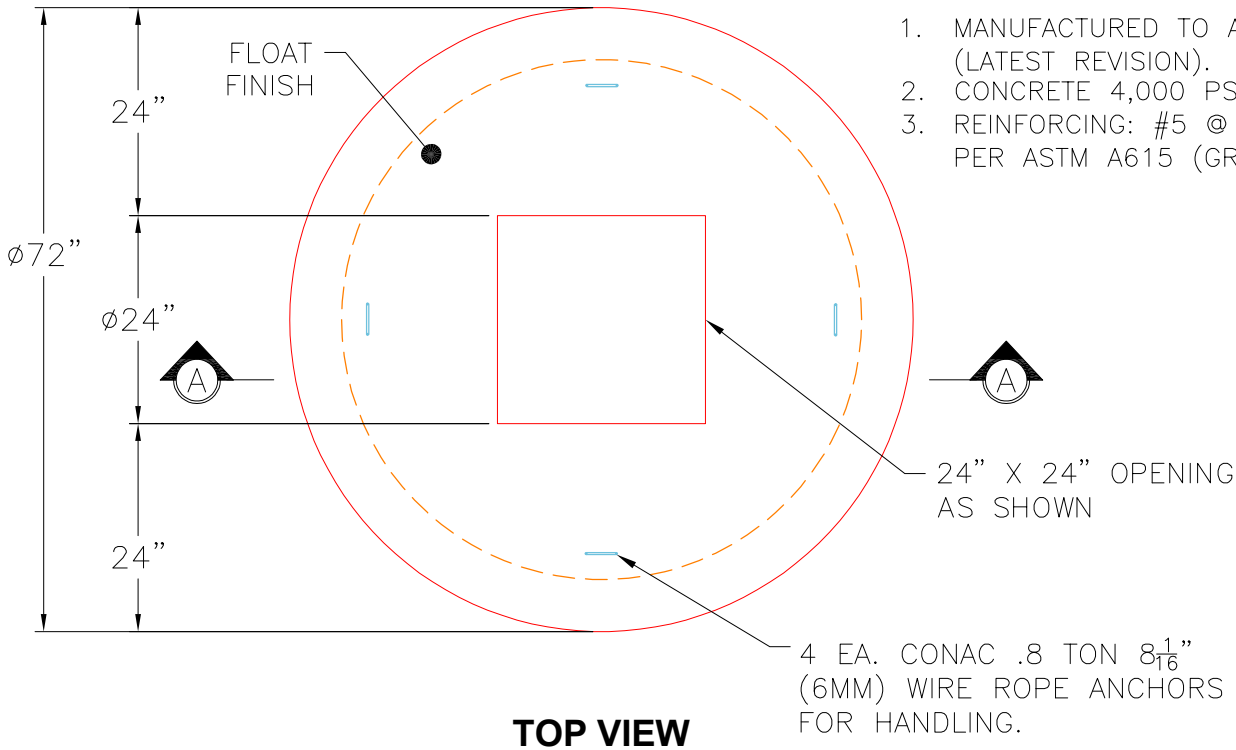

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 6"

Height (Ext): 13"

Weight (Net): 2619 lb
Volume (Net): 0.67cu.yd
