

Contractor: Central Paving Co. of Paducah, Inc.

Plant: Beaver Dam



Slack: 2.38"


REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .18)
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

P4) 24" x 24" - CASTING HEIGHT - 5"
P3) 24" x 24" - GRADE RING F/F - 3"
P2) 60" - MH FLAT TOP w/24"x24" Hole F/G - 13"
P1) 60" - MH BASE T/n - 60"


- 1) CASTING - HOE KY-465 SET (CBI TY F)
- 1) 60" - Conseal CS-102 1.00"
- 2) 24" x 24" - Conseal CS-102 1.00"
- 3) Hole - 30

0 lb
258 lb
2619 lb
7887 lb
465 lb
0 lb
0 lb
0 lb


Structure Total: 11229 lb

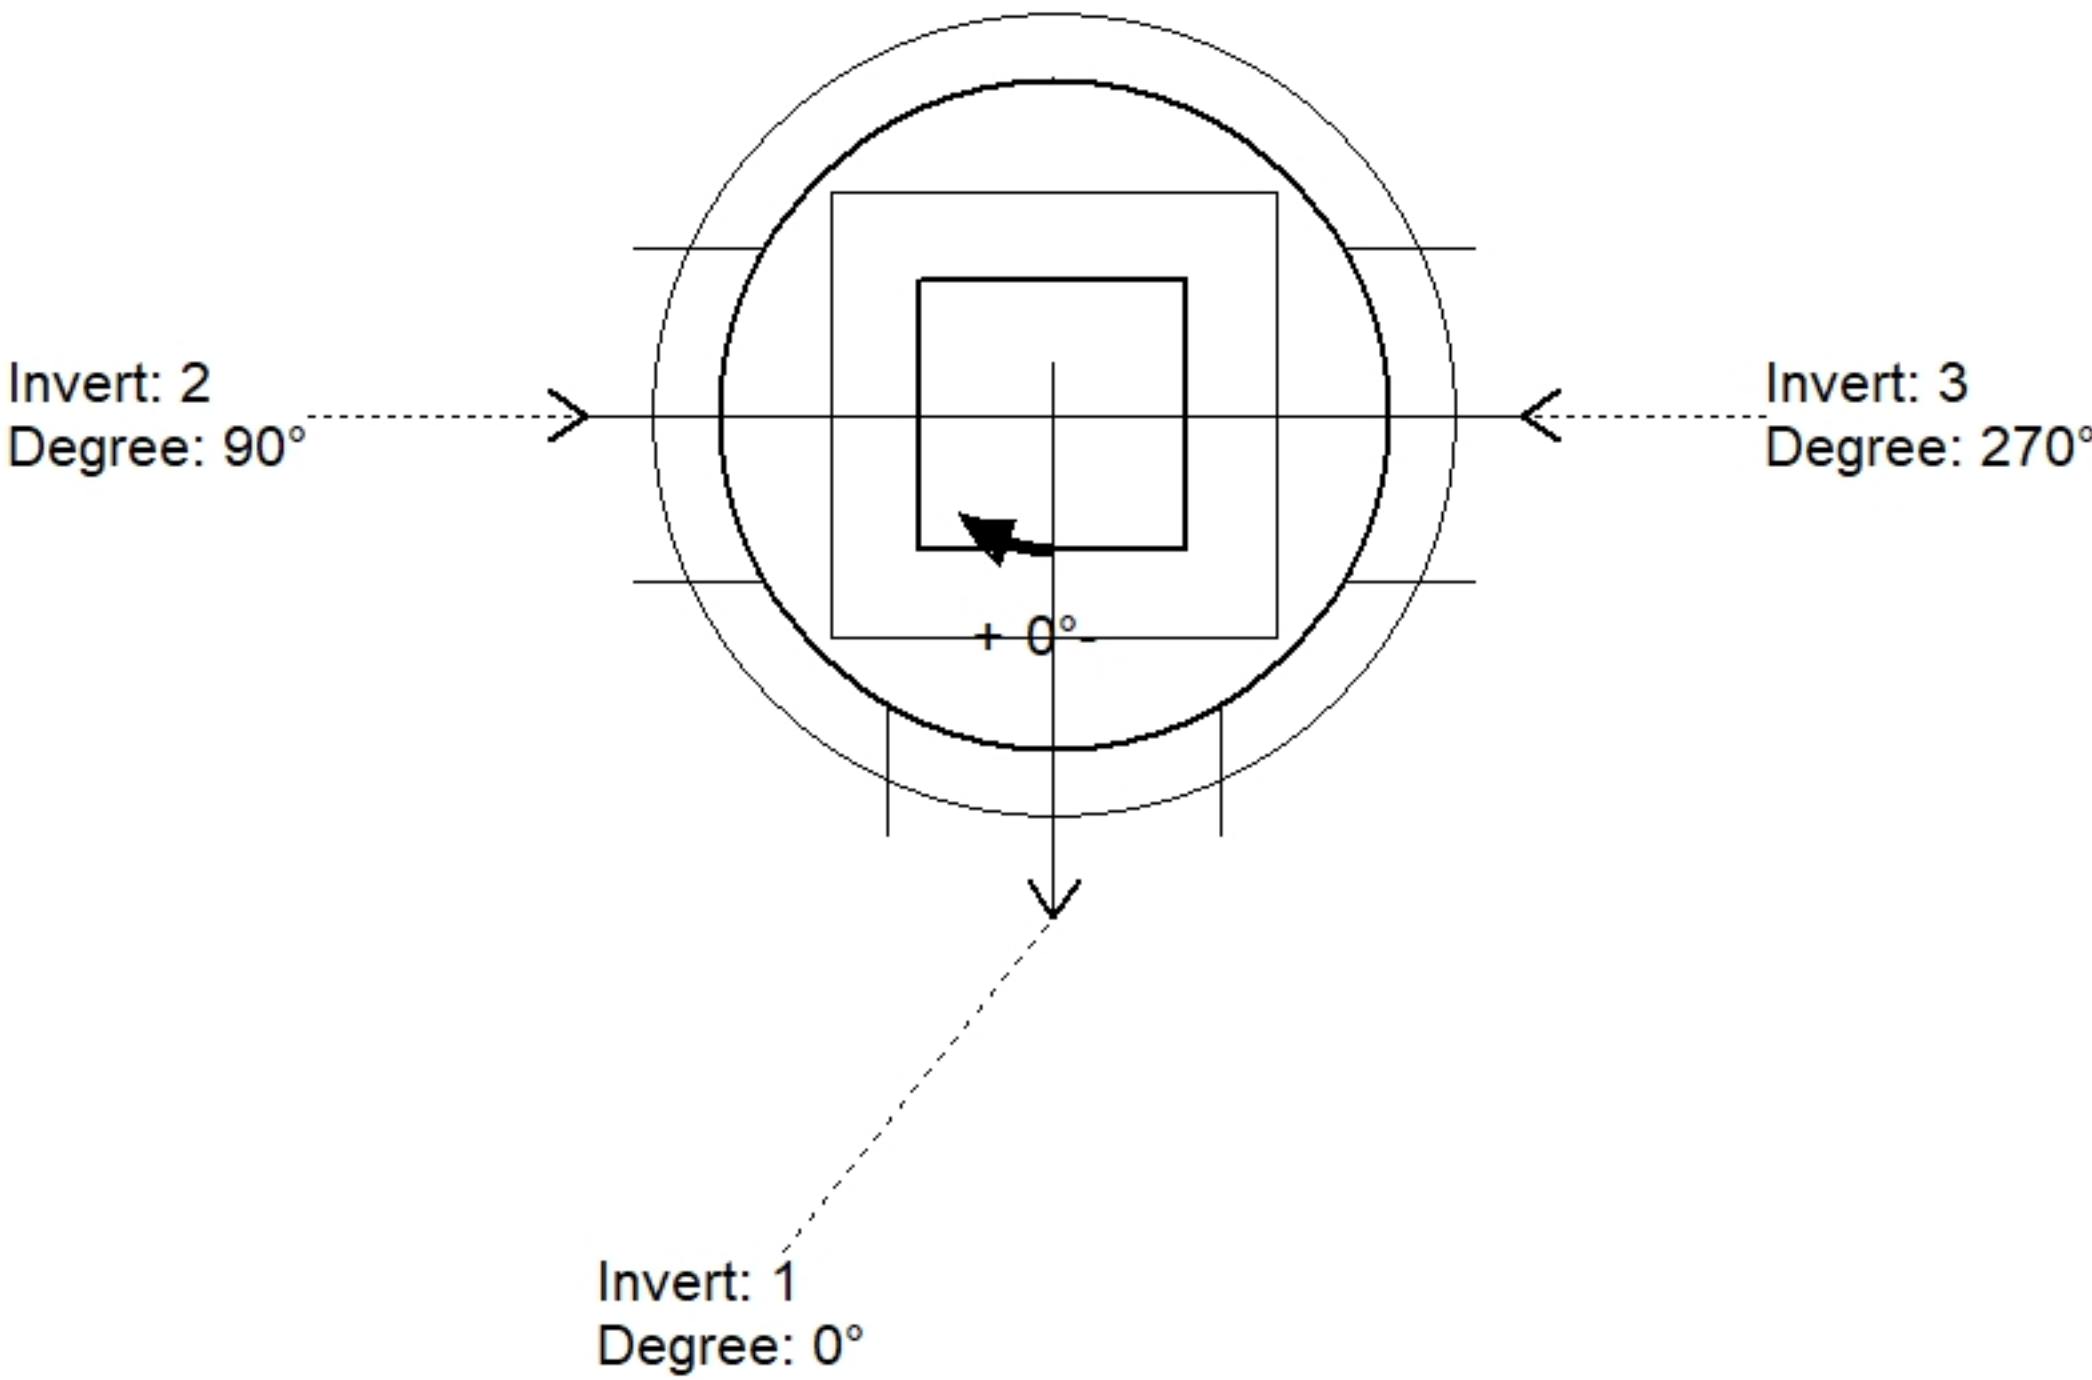

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	369.19'							
Reducer								
Invert 1	362.4'	0°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 2	363.8'	90°	24" HDPE	27.8"	30"	Hole 30	16.8"	P1
Invert 3	362.4'	270°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

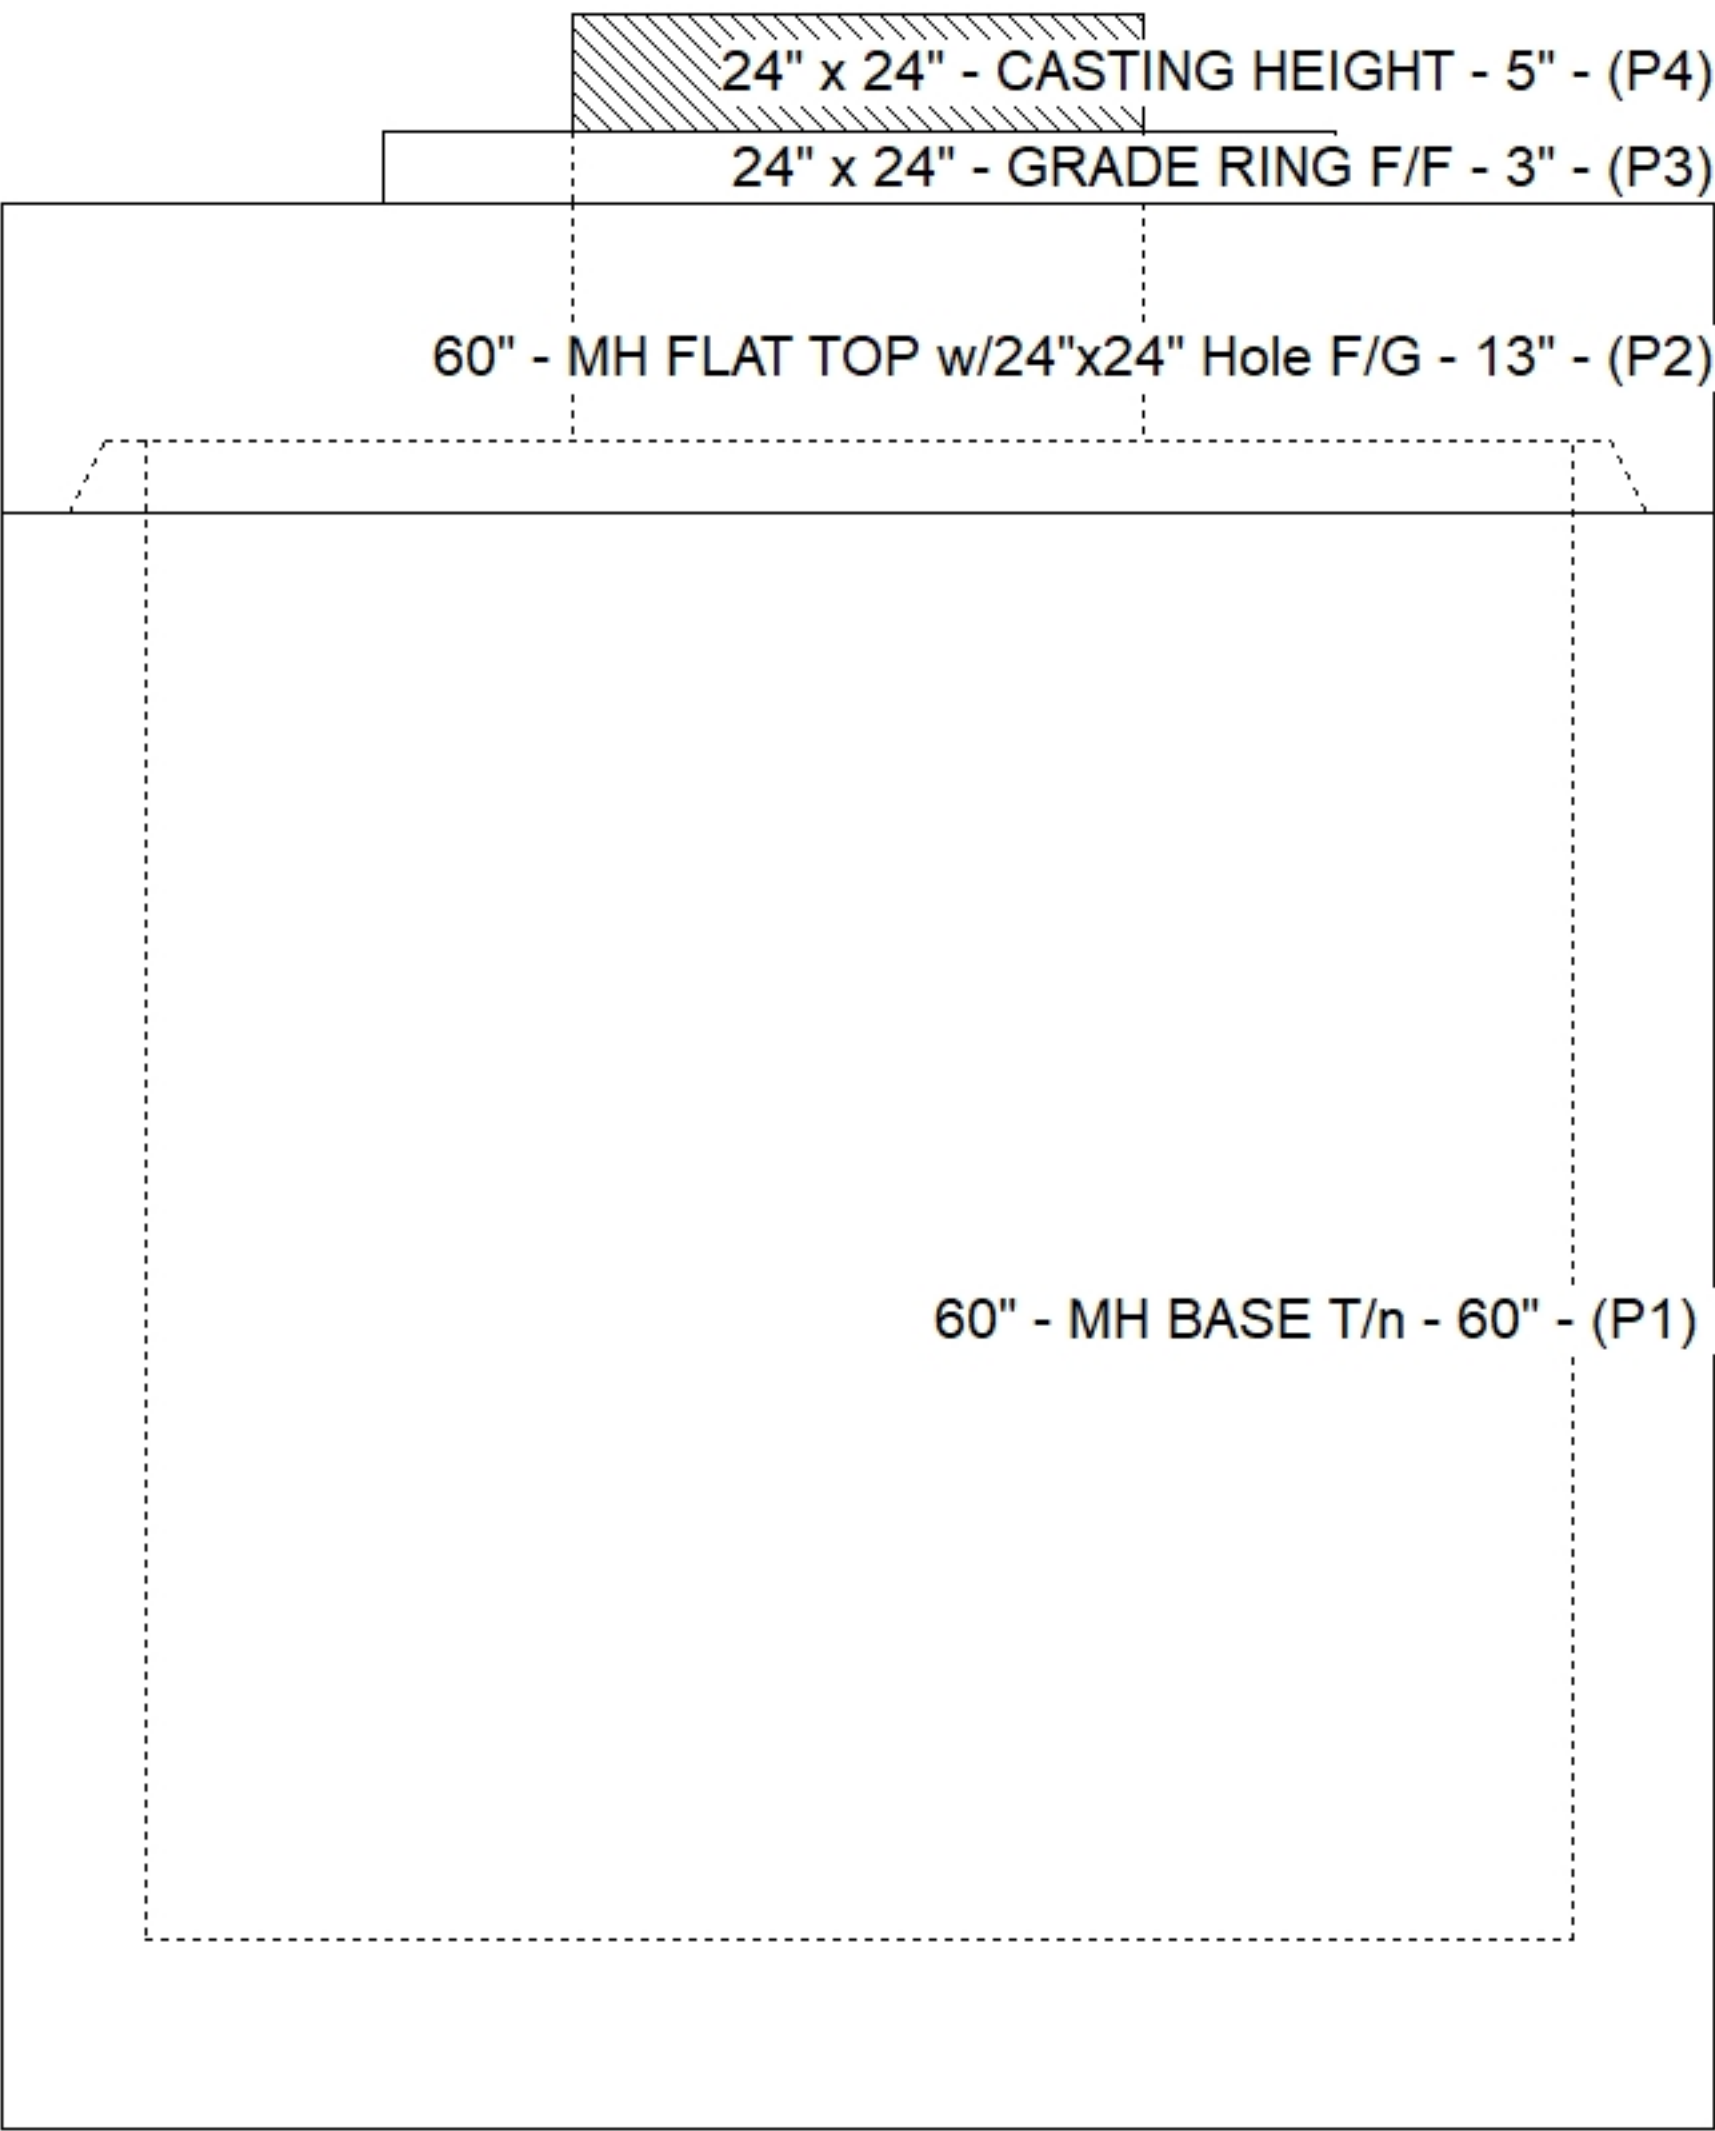

Default - Interior Dimensions

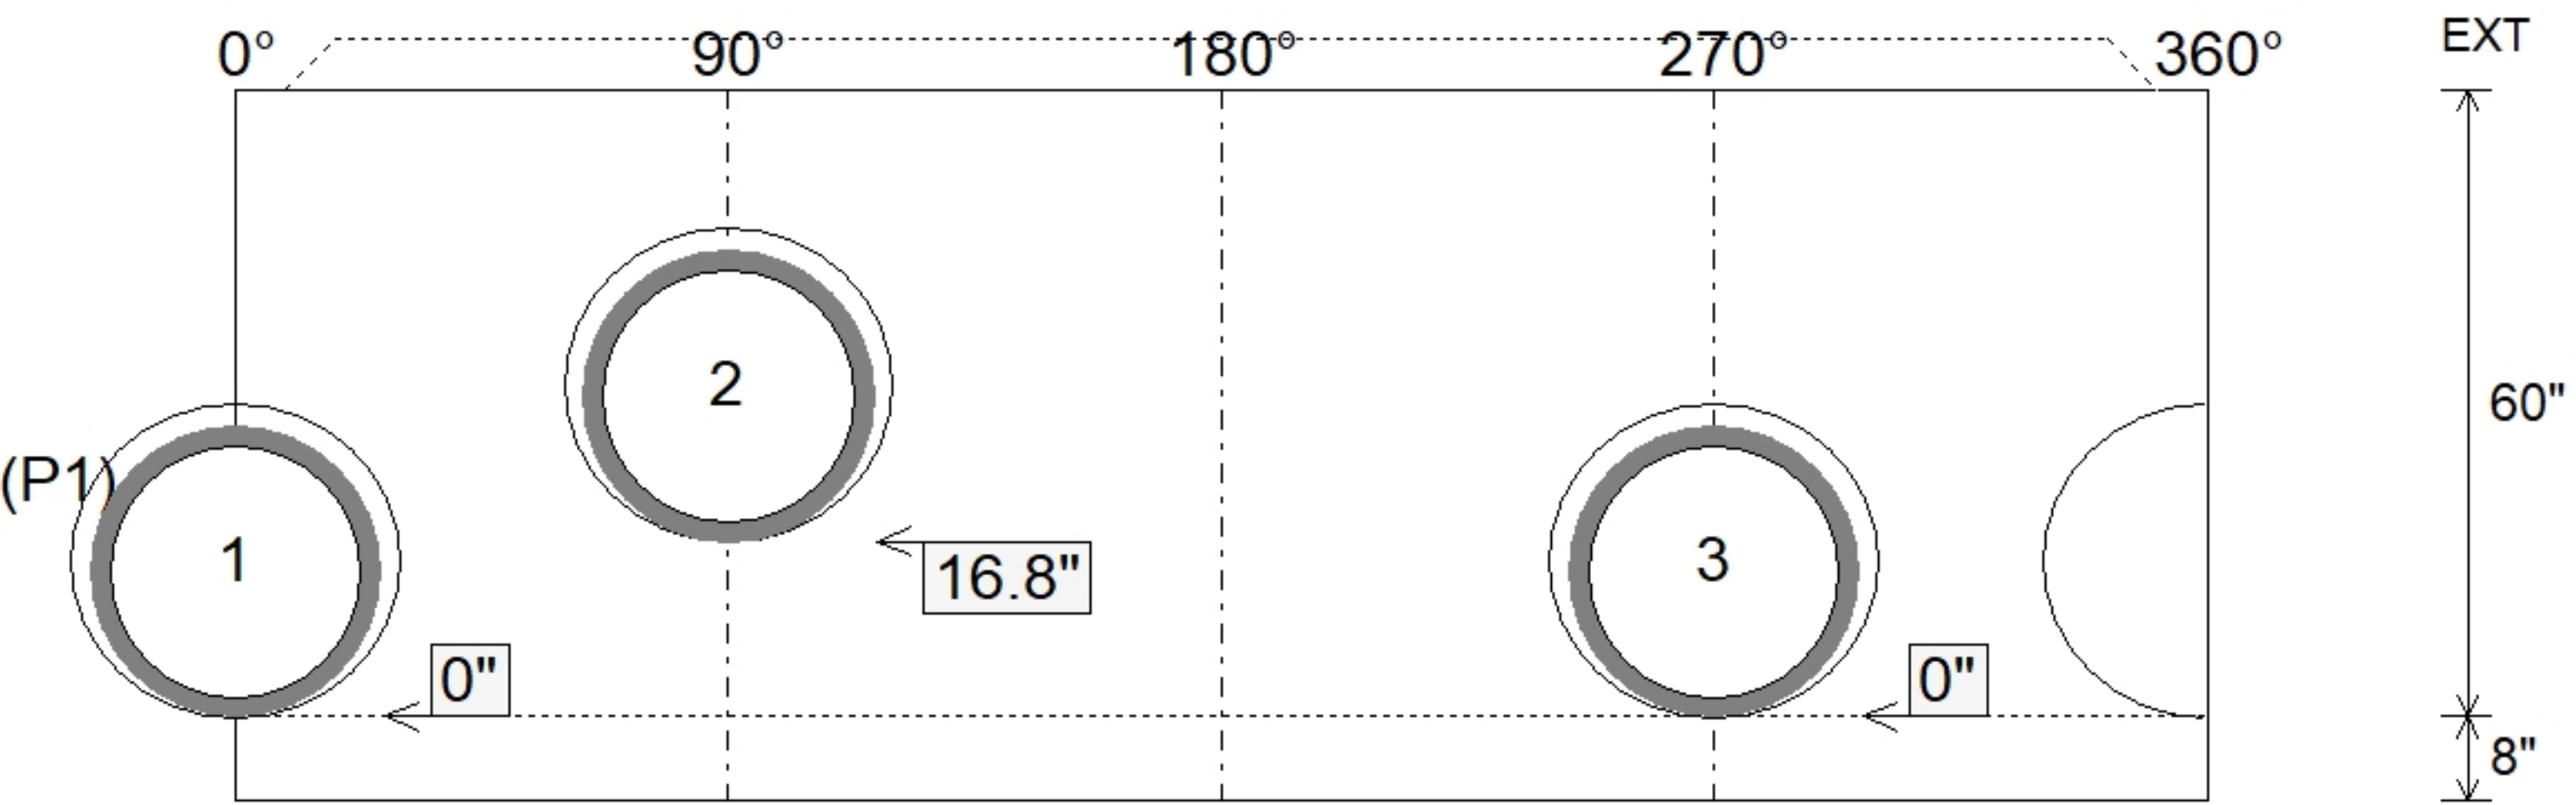

Submittal Drawing
6/16/2026 2:29:53 PM

SUBMITTAL
APPROVED BY:
