

Contractor: Central Paving Co. of Paducah, Inc.

Plant: Beaver Dam



Slack: 0.3"

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 24" x 24" - CASTING HEIGHT - 5"
P2) 48" - MH FLAT TOP w/24"x24" Hole F/F - 7"
P1) 48" - MH BASE Custom Ht F/n - 34"
1) CASTING - HOE KY-465 SET (CBI TY F)
1) 48" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
2) Hole - 30



0 lb
1214 lb
3073 lb
465 lb
0 lb
0 lb
0 lb

Structure Total: 4752 lb

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	368.7'							
Reducer								
Invert 1	365'	0°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 2	365'	135°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

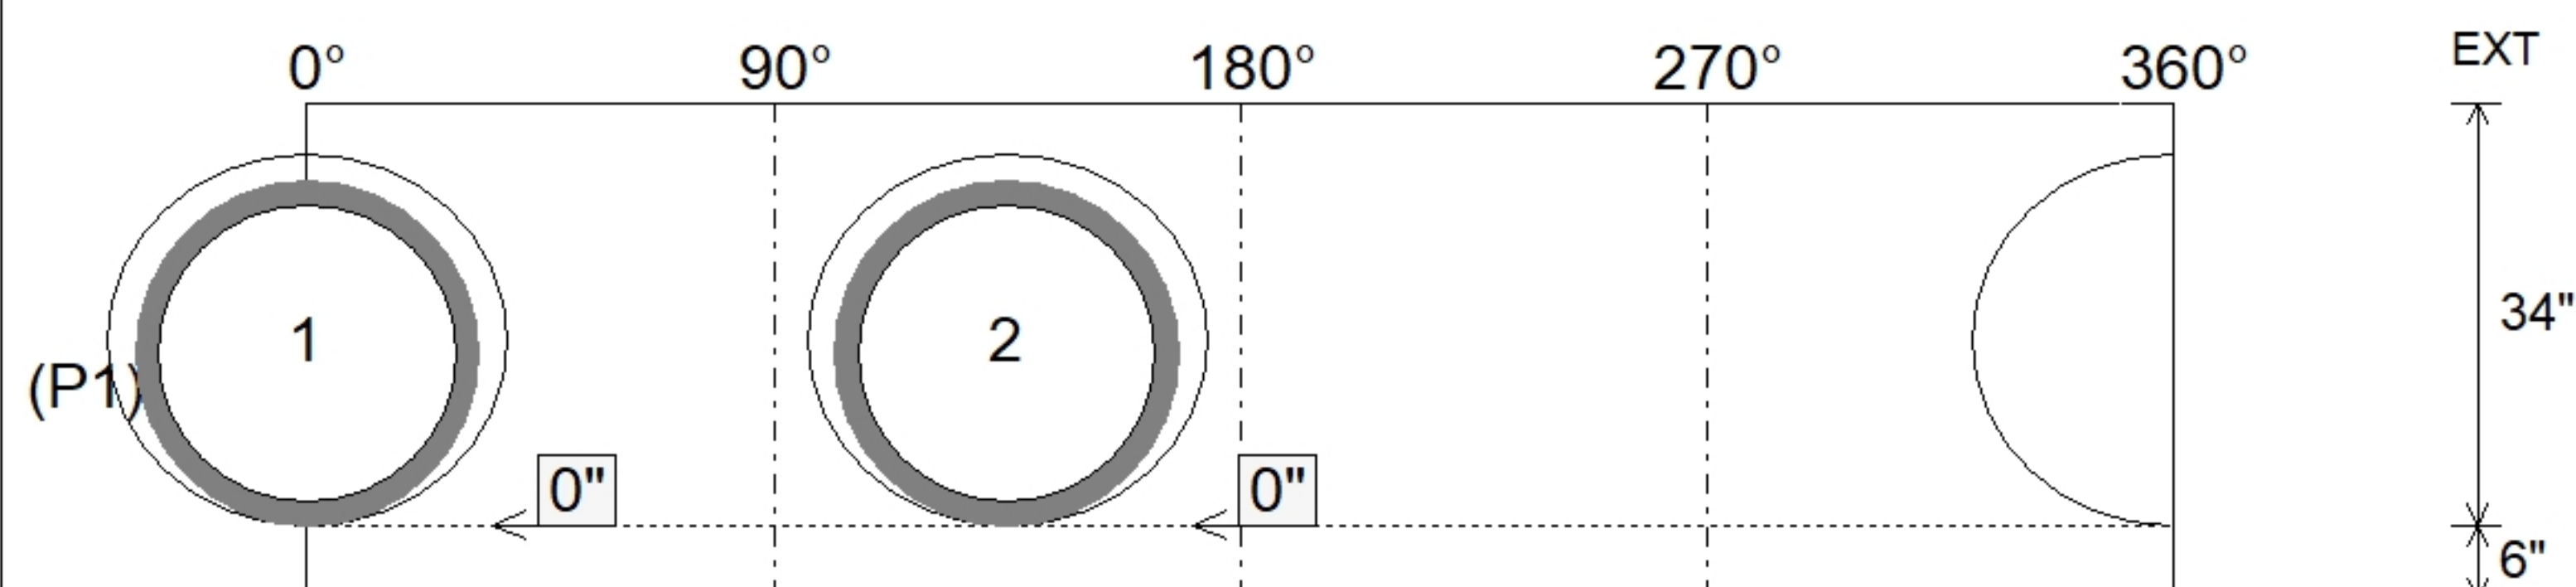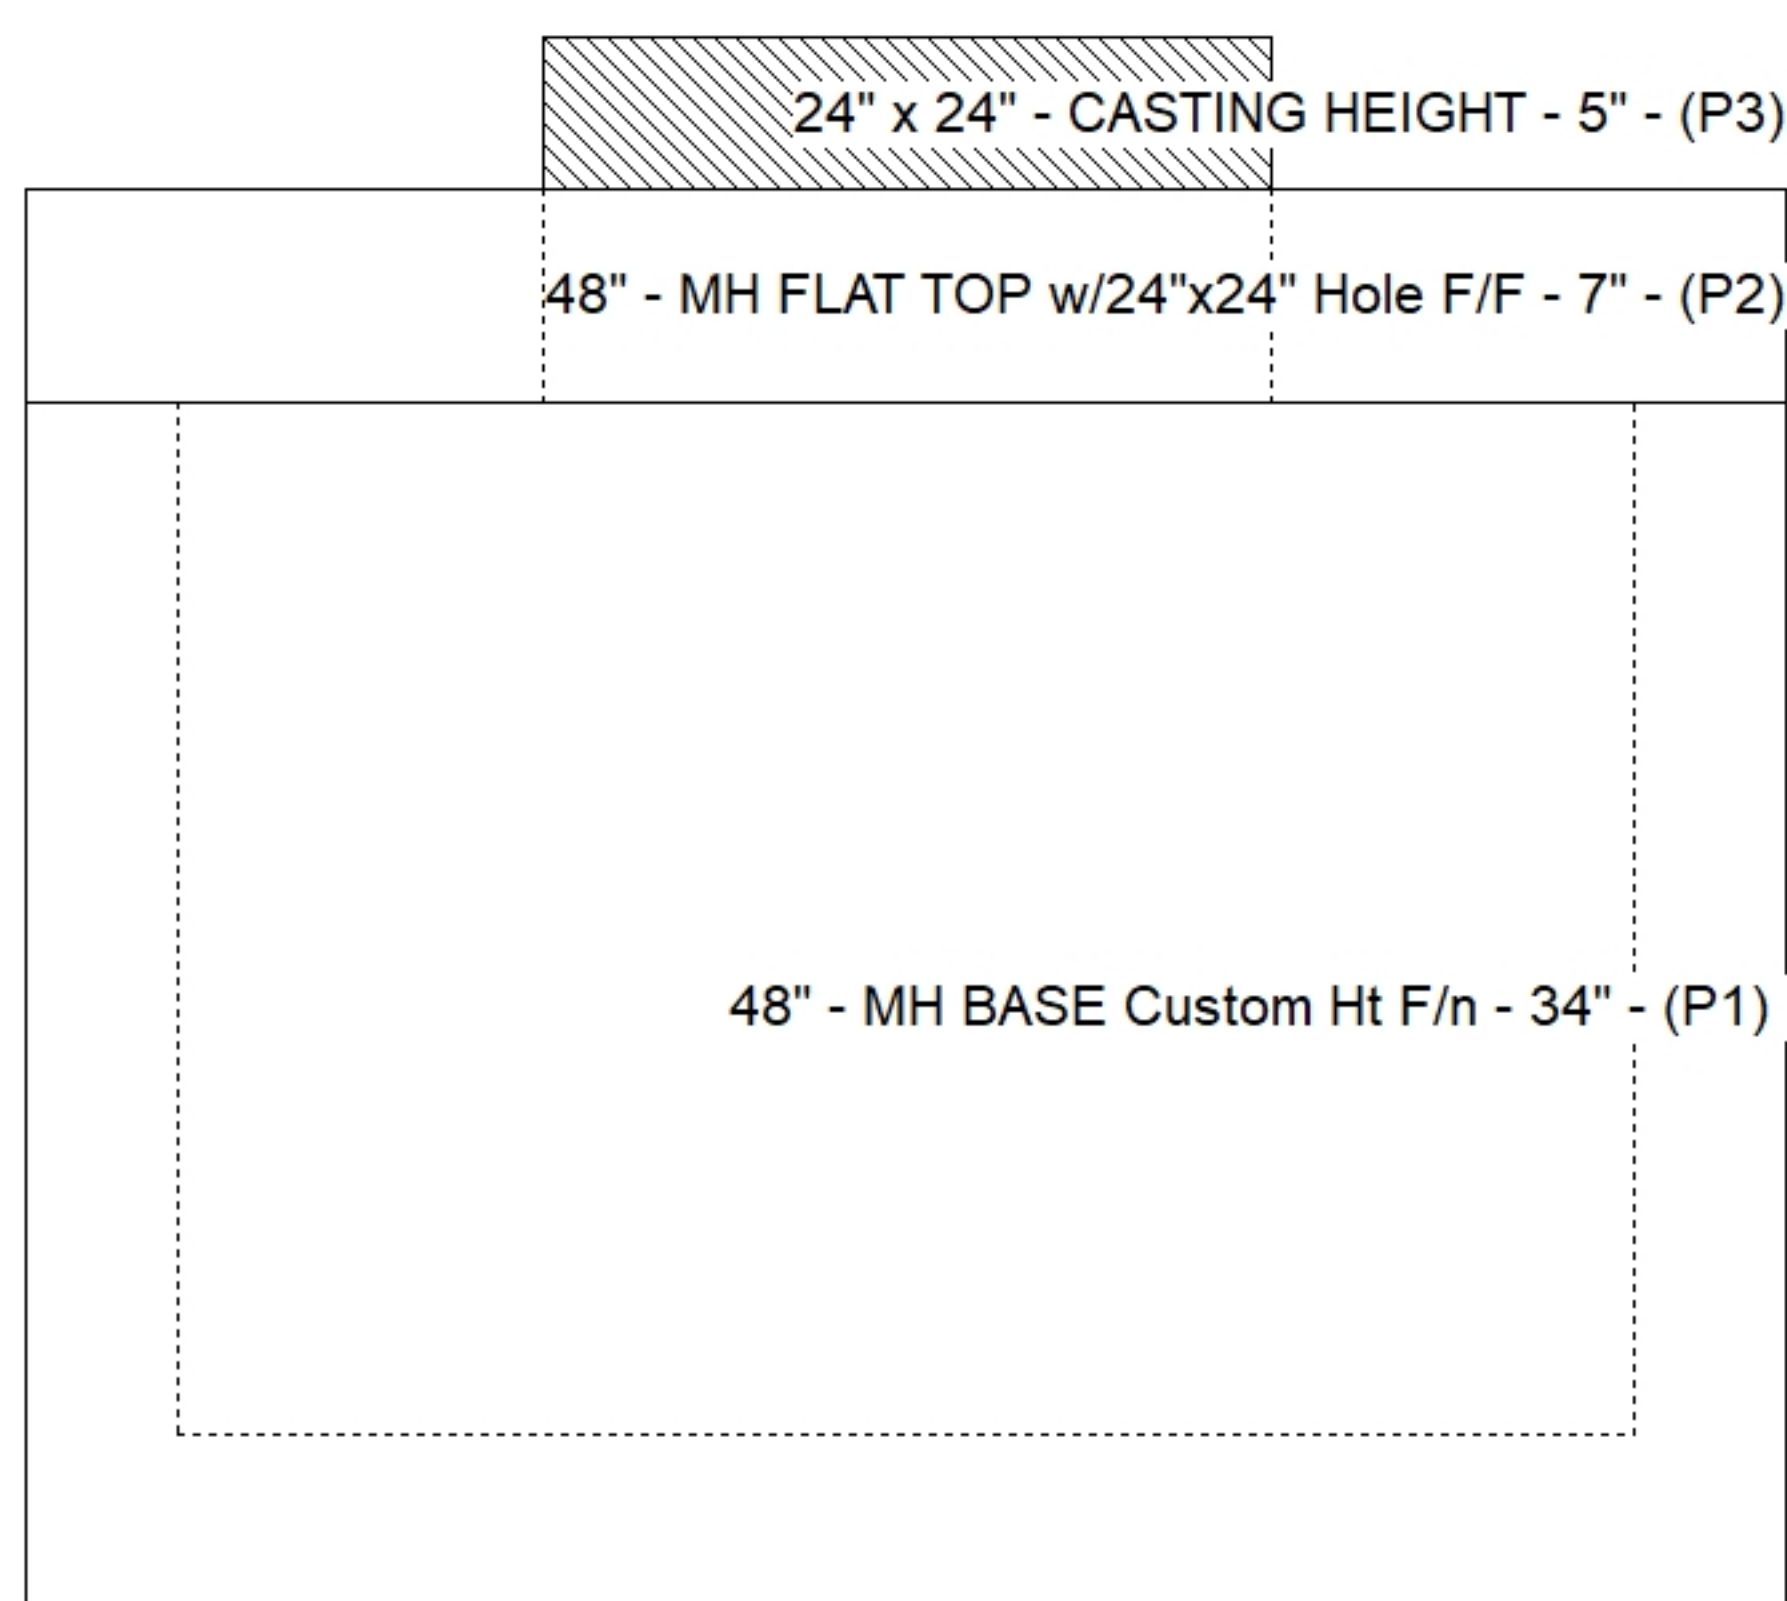

SUBMITTAL
APPROVED BY:
