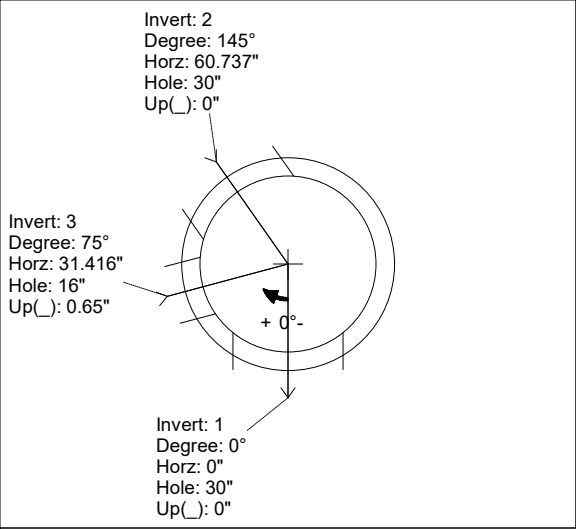
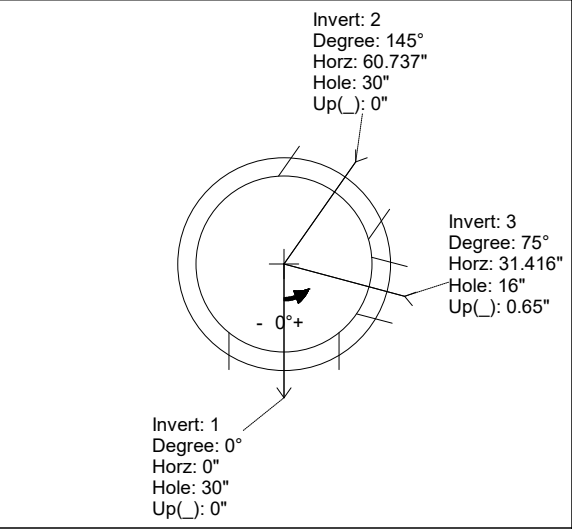
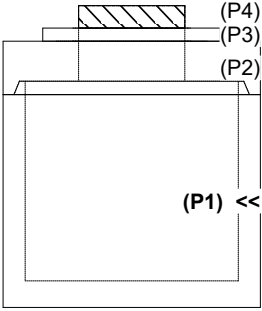
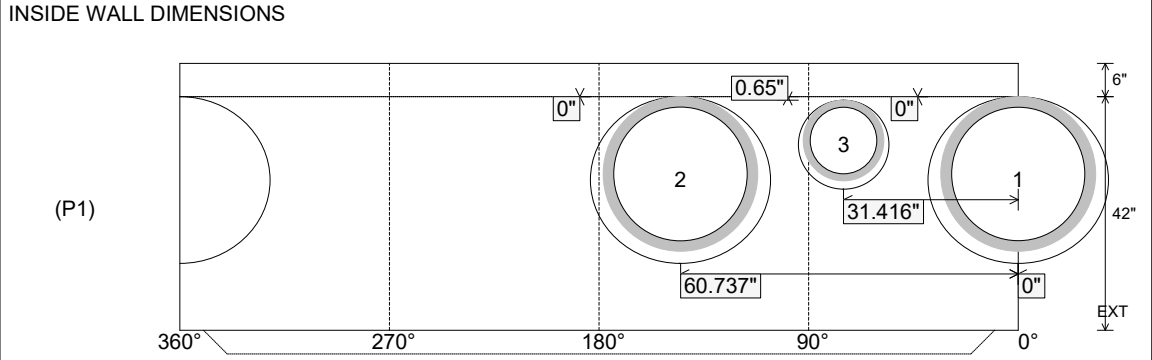


Job Name: 26-2484 Bass Pro Shops Outpost Paducah Job Location: Paducah, KY Contractor: Central Paving Co. of Paducah, Inc.					Plant: Beaver Dam 6/16/2026 8:02:30 AM		Tech: S. Felletter PC: A. Chambers				
Structure ID: X5 ST-CI											
P1 MH048BA42		MH BASE T/n									
P4) 24" x 24" - CASTING HEIGHT - 5" P3) 24" x 24" - GRADE RING F/F - 3" P2) 48" - MH FLAT TOP w/24"x24" Hole F/G - 12" P1) 48" - MH BASE T/n - 42" 1) CASTING - HOE KY-465 SET (CBI TY F) 1) 48" - Conseal CS-102 1.00" 2) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 30 1) Hole - 16					0 lb 258 lb 1500 lb 3546 lb 465 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5769 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 465 F/G/H). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 370.6'		Rim to Invert: 5.05'		Slack: 0.5"		Sump: 1.9"		Step Position: 0°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	365.55'	0°	0"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"	
Invert 2	365.55'	145°	73.391"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"	
Invert 3	365.55'	75°	37.961"	12" HDPE	14.5"	Hole 16	16"	16.312"	0.65"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)   INSIDE WALL DIMENSIONS  Coating (Int): Coating (Ext): Seam Up: Tongue Seam Dn: n/a Wall Thickness: 5" Floor Height: 6" Height (Int): 42" Height (Ext): 48" Weight (Net): 3546 lb Volume (Net): 0.91cu.yd											
