


Job Name: 26-2484 Bass Pro Shops Outpost Paducah Job Location: Paducah, KY Contractor: Central Paving Co. of Paducah, Inc.					Plant: Beaver Dam 6/16/2026 8:02:31 AM		Tech: S. Felletter PC: A. Chambers				
Structure ID: X6 ST-CI											
P1 MH048BAVF		MH BASE Custom Ht F/n									
P3) 24" x 24" - CASTING HEIGHT - 5" P2) 48" - MH FLAT TOP w/24"x24" Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 37" 1) CASTING - HOE KY-465 SET (CBI TY F) 1) 48" - Conseal CS-102 1.00" 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 30 1) Hole - 24						0 lb 1214 lb 3402 lb 465 lb 0 lb 0 lb 0 lb 0 lb ----- 5080 lb Structure Total:		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 465 F/G/H). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 370.5'		Rim to Invert: 4'		Slack: 0.9"		Sump: 1.9"		Step Position: 0°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	366.5'	0°	0"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"	
Invert 2	366.5'	180°	91.106"	18" HDPE	21.2"	Hole 24	24"	25.133"	0.3"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

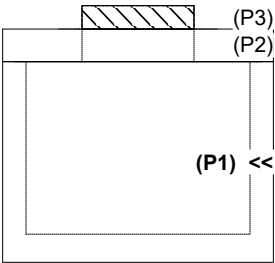

(P1) <<


(P2)

(P3)

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

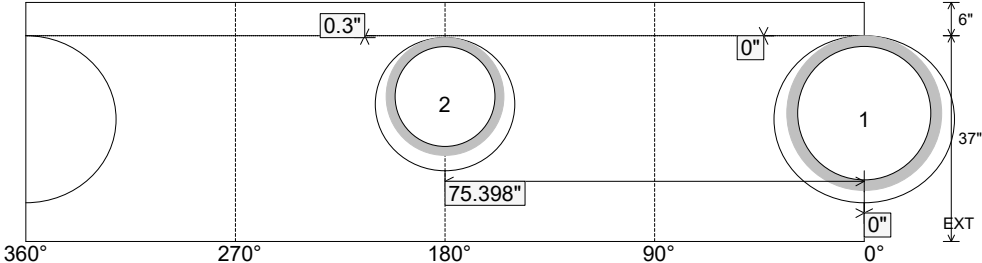

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 37" Height (Ext): 43"	Weight (Net): 3402 lb Volume (Net): 0.87cu.yd
----------------------------------	-------------------------------	--	--	--
