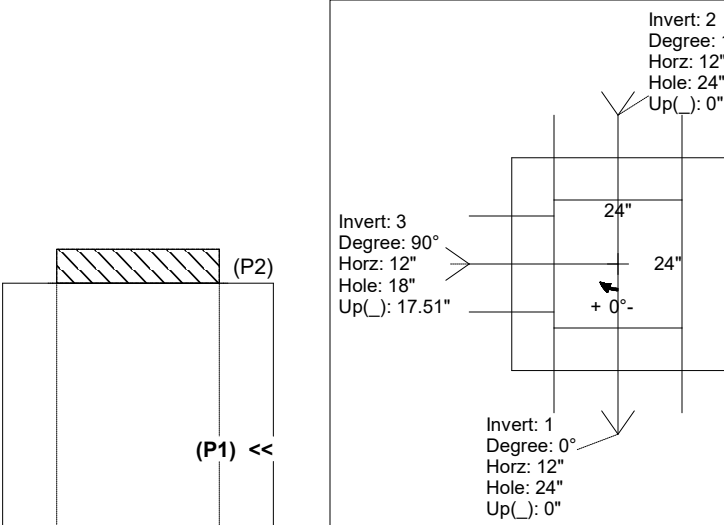
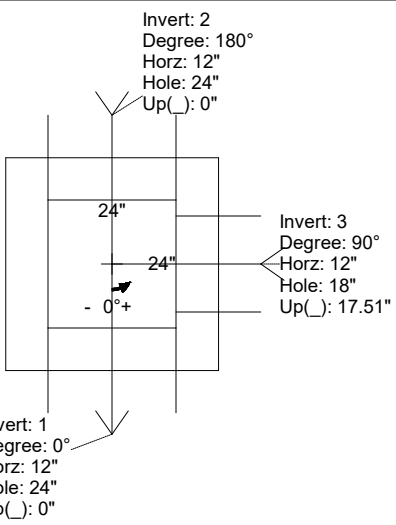
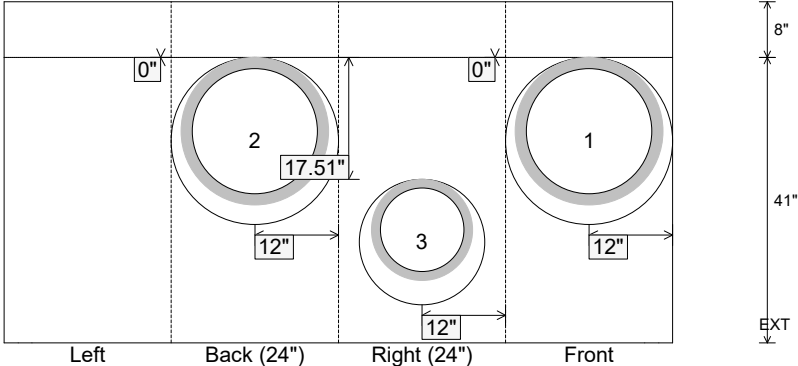


Job Name: 26-2484 Bass Pro Shops Outpost Paducah Job Location: Paducah, KY Contractor: Central Paving Co. of Paducah, Inc.					Plant: Beaver Dam 6/16/2026 8:02:32 AM		Tech: S. Felletter PC: A. Chambers					
Structure ID: X7 ST-CI												
P1 BX2424-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n										
P2) 24" x 24" - CASTING HEIGHT - 5" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 41" 1) CASTING - HOE KY-465 SET (CBI TY F) 1) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 24 1) Hole - 18					0 lb 3971 lb 465 lb 0 lb 0 lb 0 lb ----- Structure Total: 4436 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 465 F/G/H). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.					
Rim: 370.9'					Rim to Invert: 3.7'		Slack: 0"		Sump: 1.6"		Step Position: 0°	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	367.2'	0°	20"	18" HDPE	21.2"	Hole 24	24"	24"	0"	0"		
Invert 2	367.2'	180°	20"	18" HDPE	21.2"	Hole 24	24"	24"	0"	0"		
Invert 3	368.63'	90°	20"	12" HDPE	14.5"	Hole 18	18"	18"	17.51"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions) INSIDE WALL DIMENSIONS												
  												
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 41" Height (Ext): 49"		Weight (Net): 3971 lb Volume (Net): 1.01cu.yd			
