

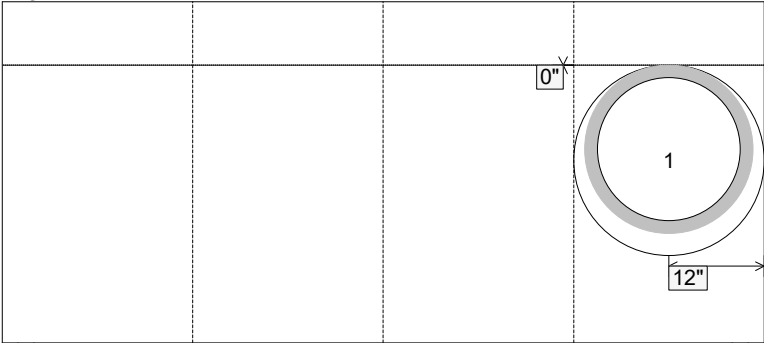


Job Name: 26-2484 Bass Pro Shops Outpost Paducah Job Location: Paducah, KY Contractor: Central Paving Co. of Paducah, Inc.					Plant: Beaver Dam 6/16/2026 8:02:33 AM		Tech: S. Felletter PC: A. Chambers				
Structure ID: X8 ST-CI											
P1 BX2424-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n									
P2) 24" x 24" - CASTING HEIGHT - 5" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 35" 1) CASTING - HOE KY-465 SET (CBI TY F) 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 24						0 lb 3854 lb 465 lb 0 lb 0 lb ----- Structure Total: 4319 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 465 F/G/H). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 370.9'		Rim to Invert: 3.2'		Slack: 0"		Sump: 1.6"		Step Position: 0°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	367.7'	0°	20"	18" HDPE	21.2"	Hole 24	24"	24"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  Invert: 1 Degree: 0° Horz: 12" Hole: 24" Up(_): 0" UPSIDE-DOWN VIEW (int. dimensions)  Invert: 1 Degree: 0° Horz: 12" Hole: 24" Up(_): 0"											
INSIDE WALL DIMENSIONS  Left Back (24") Right (24") Front EXT											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 35" Height (Ext): 43"		Weight (Net): 3854 lb Volume (Net): 0.98cu.yd		
