

Contractor: Central Paving Co. of Paducah, Inc.

Plant: Beaver Dam



Slack: 1.6"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P5) 24" - CASTING HEIGHT - 7"
P4) 24" - GRADE RING F/F - 4"
P3) 48" - ECC CONE w/ 24" HOLE F/G - 30"
P2) 48" - MH RISER T/G - 72"
P1) 48" - MH BASE T/n - 12"
1) CASTING - HOE MC-375 F/C Storm
2) 48" - Conseal CS-102 1.00"
2) 24" - Conseal CS-102 1.00"
3) Hole - 30

0 lb
270 lb
2050 lb
4082 lb
2169 lb
271 lb
0 lb
0 lb
0 lb


Structure Total: 8841 lb

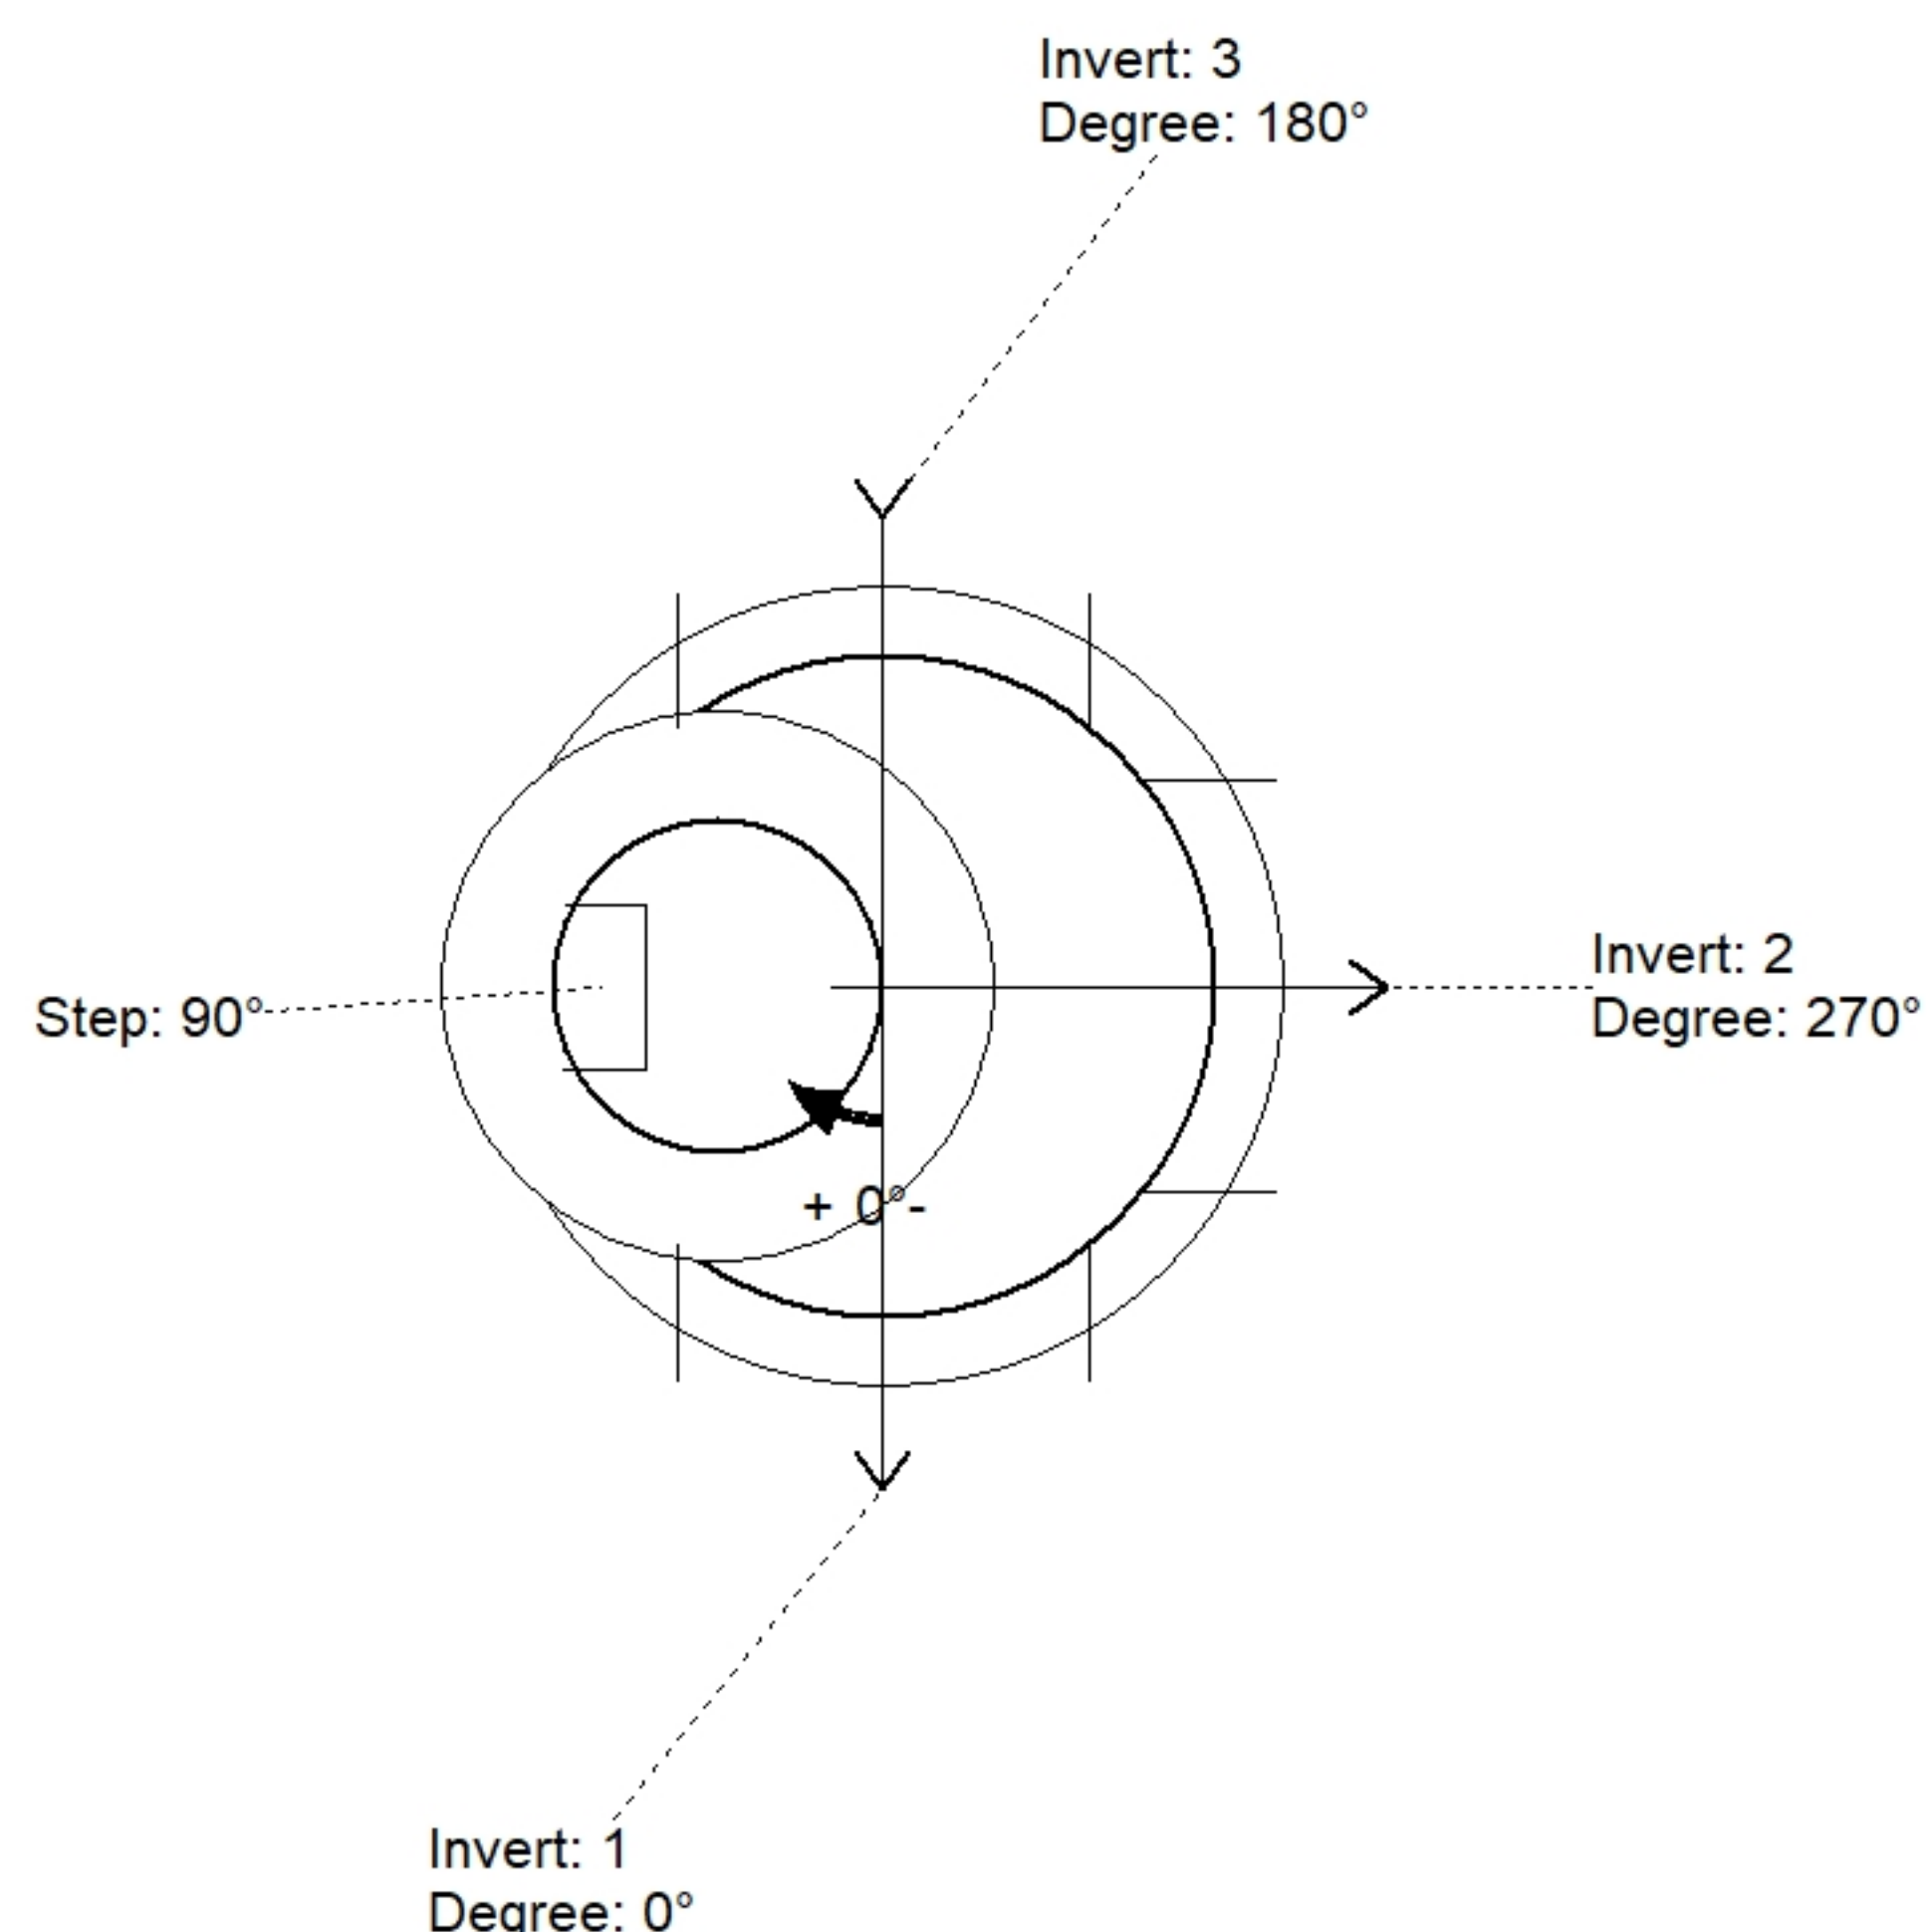

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	370.05'							
Reducer								
Invert 1	361.5'	0°	24" HDPE	27.8"	30"	Hole 30	5.85"	P2
Invert 2	363.23'	270°	24" HDPE	27.8"	30"	Hole 30	26.61"	P2
Invert 3	363.23'	180°	24" HDPE	27.8"	30"	Hole 30	26.61"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

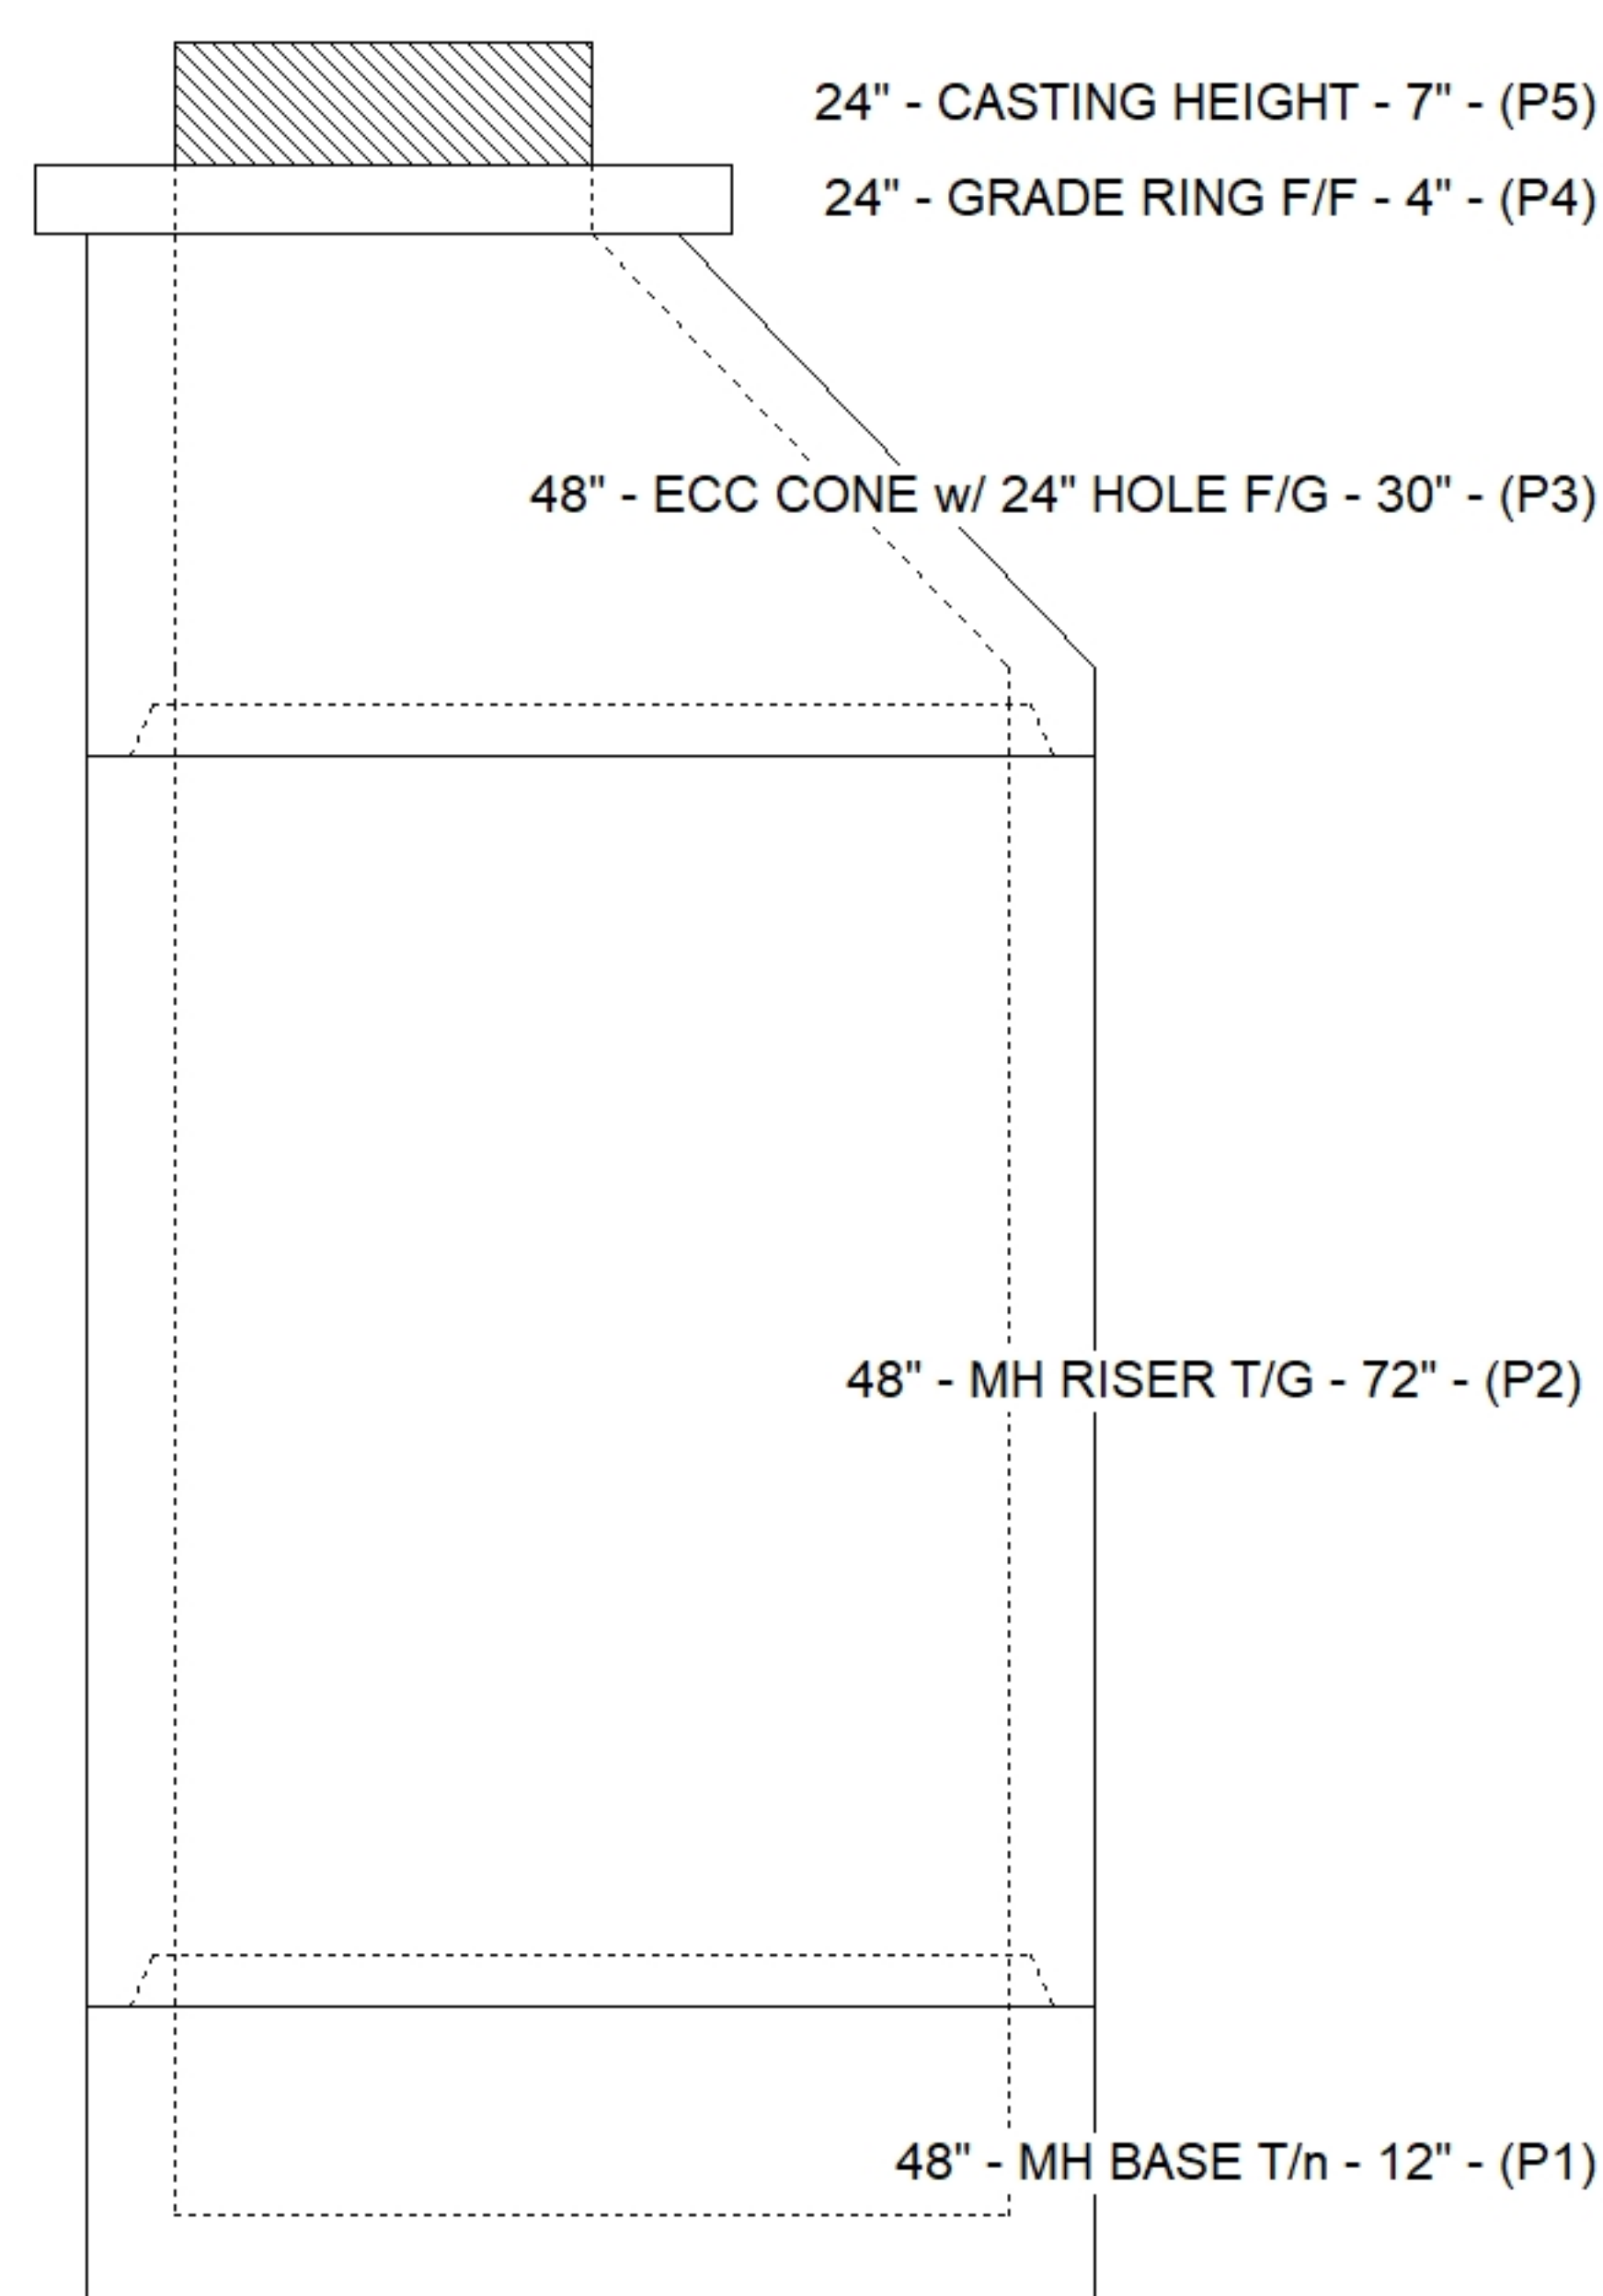

Default - Interior Dimensions

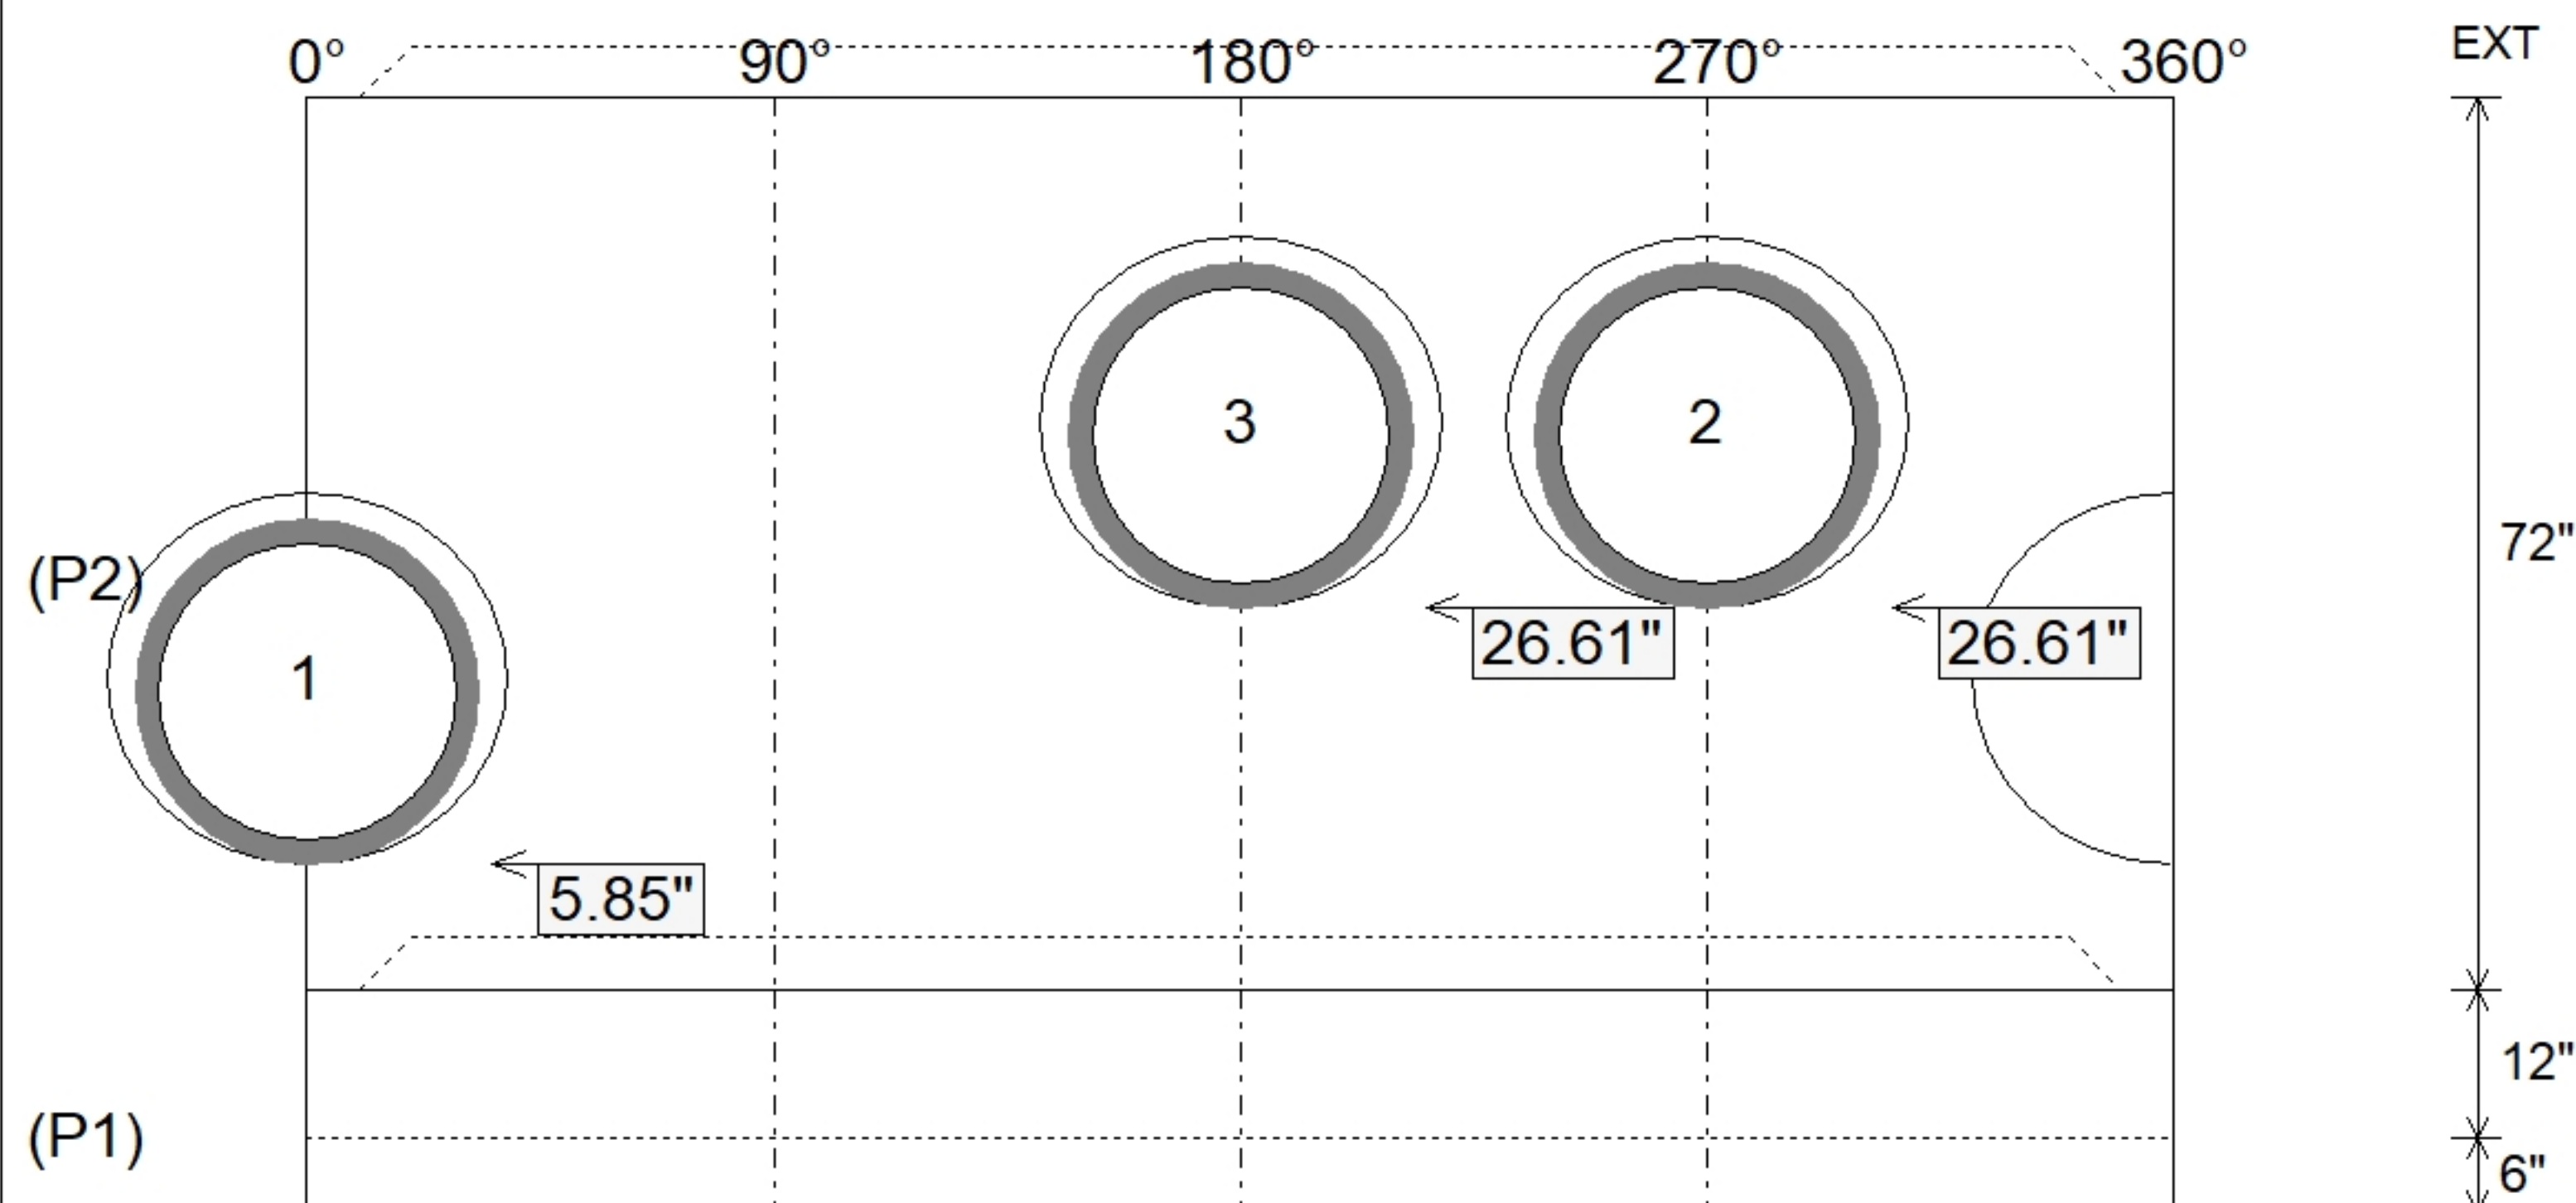

SUBMITTAL
APPROVED BY:
