

Job Name: 26-2484 Bass Pro Shops Outpost Paducah
Job Location: Paducah, KY
Contractor: Central Paving Co. of Paducah, Inc.

Plant: Beaver Dam

Tech: S. Felletter

6/16/2026 8:03:47 AM

PC: A. Chambers



Structure ID: Y5 ST-CI

P2 MH048LD12-24SQ

MH FLAT TOP w/24"x24" Hole F/G

- P3) 24" x 24" - CASTING HEIGHT - 5"
P2) 48" - MH FLAT TOP w/24"x24" Hole F/G - 12"
P1) 48" - MH BASE Custom Ht T/n - 69"
1) CASTING - HOE KY-465 SET (CBI TY F)
1) 48" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 30
1) Hole - 24
1) Hole - 16


0 lb
1500 lb
5551 lb
465 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 7516 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE 465 F/G/H).


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

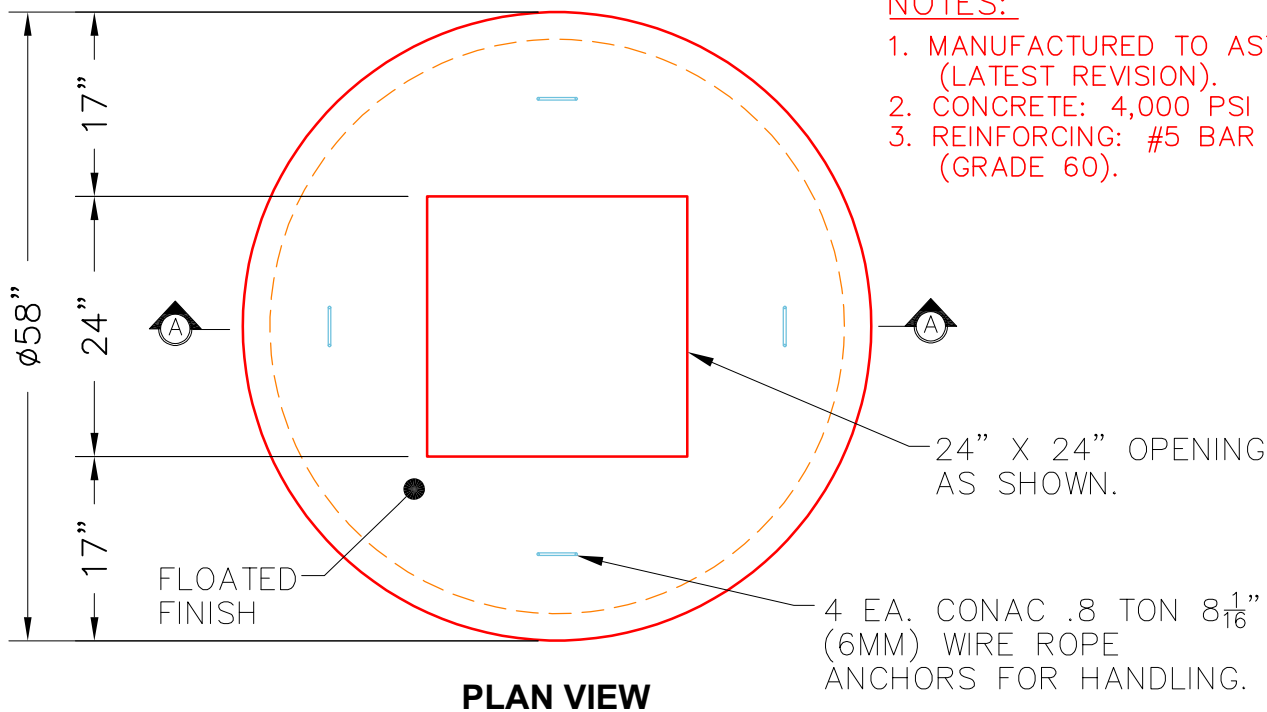

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60).

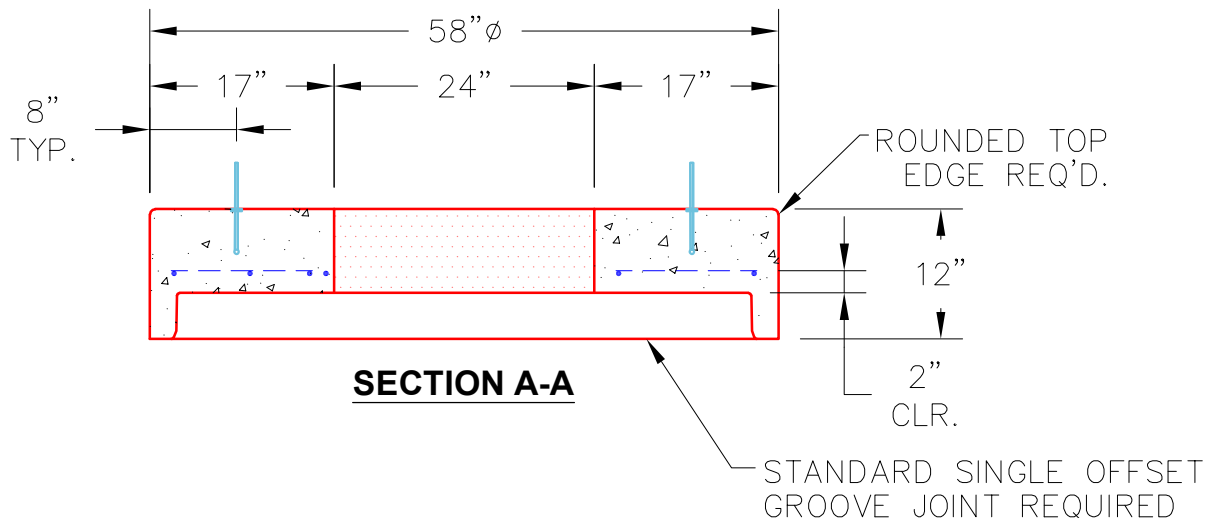

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1500 lb
Volume (Net): 0.37cu.yd
