

Contractor: Central Paving Co. of Paducah, Inc.

Plant: Beaver Dam




Slack: 0.38"

REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 24" x 24" - CASTING HEIGHT - 5"
P2) 48" - MH FLAT TOP w/24"x24" Hole F/G - 12"
P1) 48" - MH BASE Custom Ht T/n - 69"
1) CASTING - HOE KY-465 SET (CBI TY F)
1) 48" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 30
1) Hole - 24
1) Hole - 16

0 lb
1500 lb
5551 lb
465 lb
0 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 7516 lb

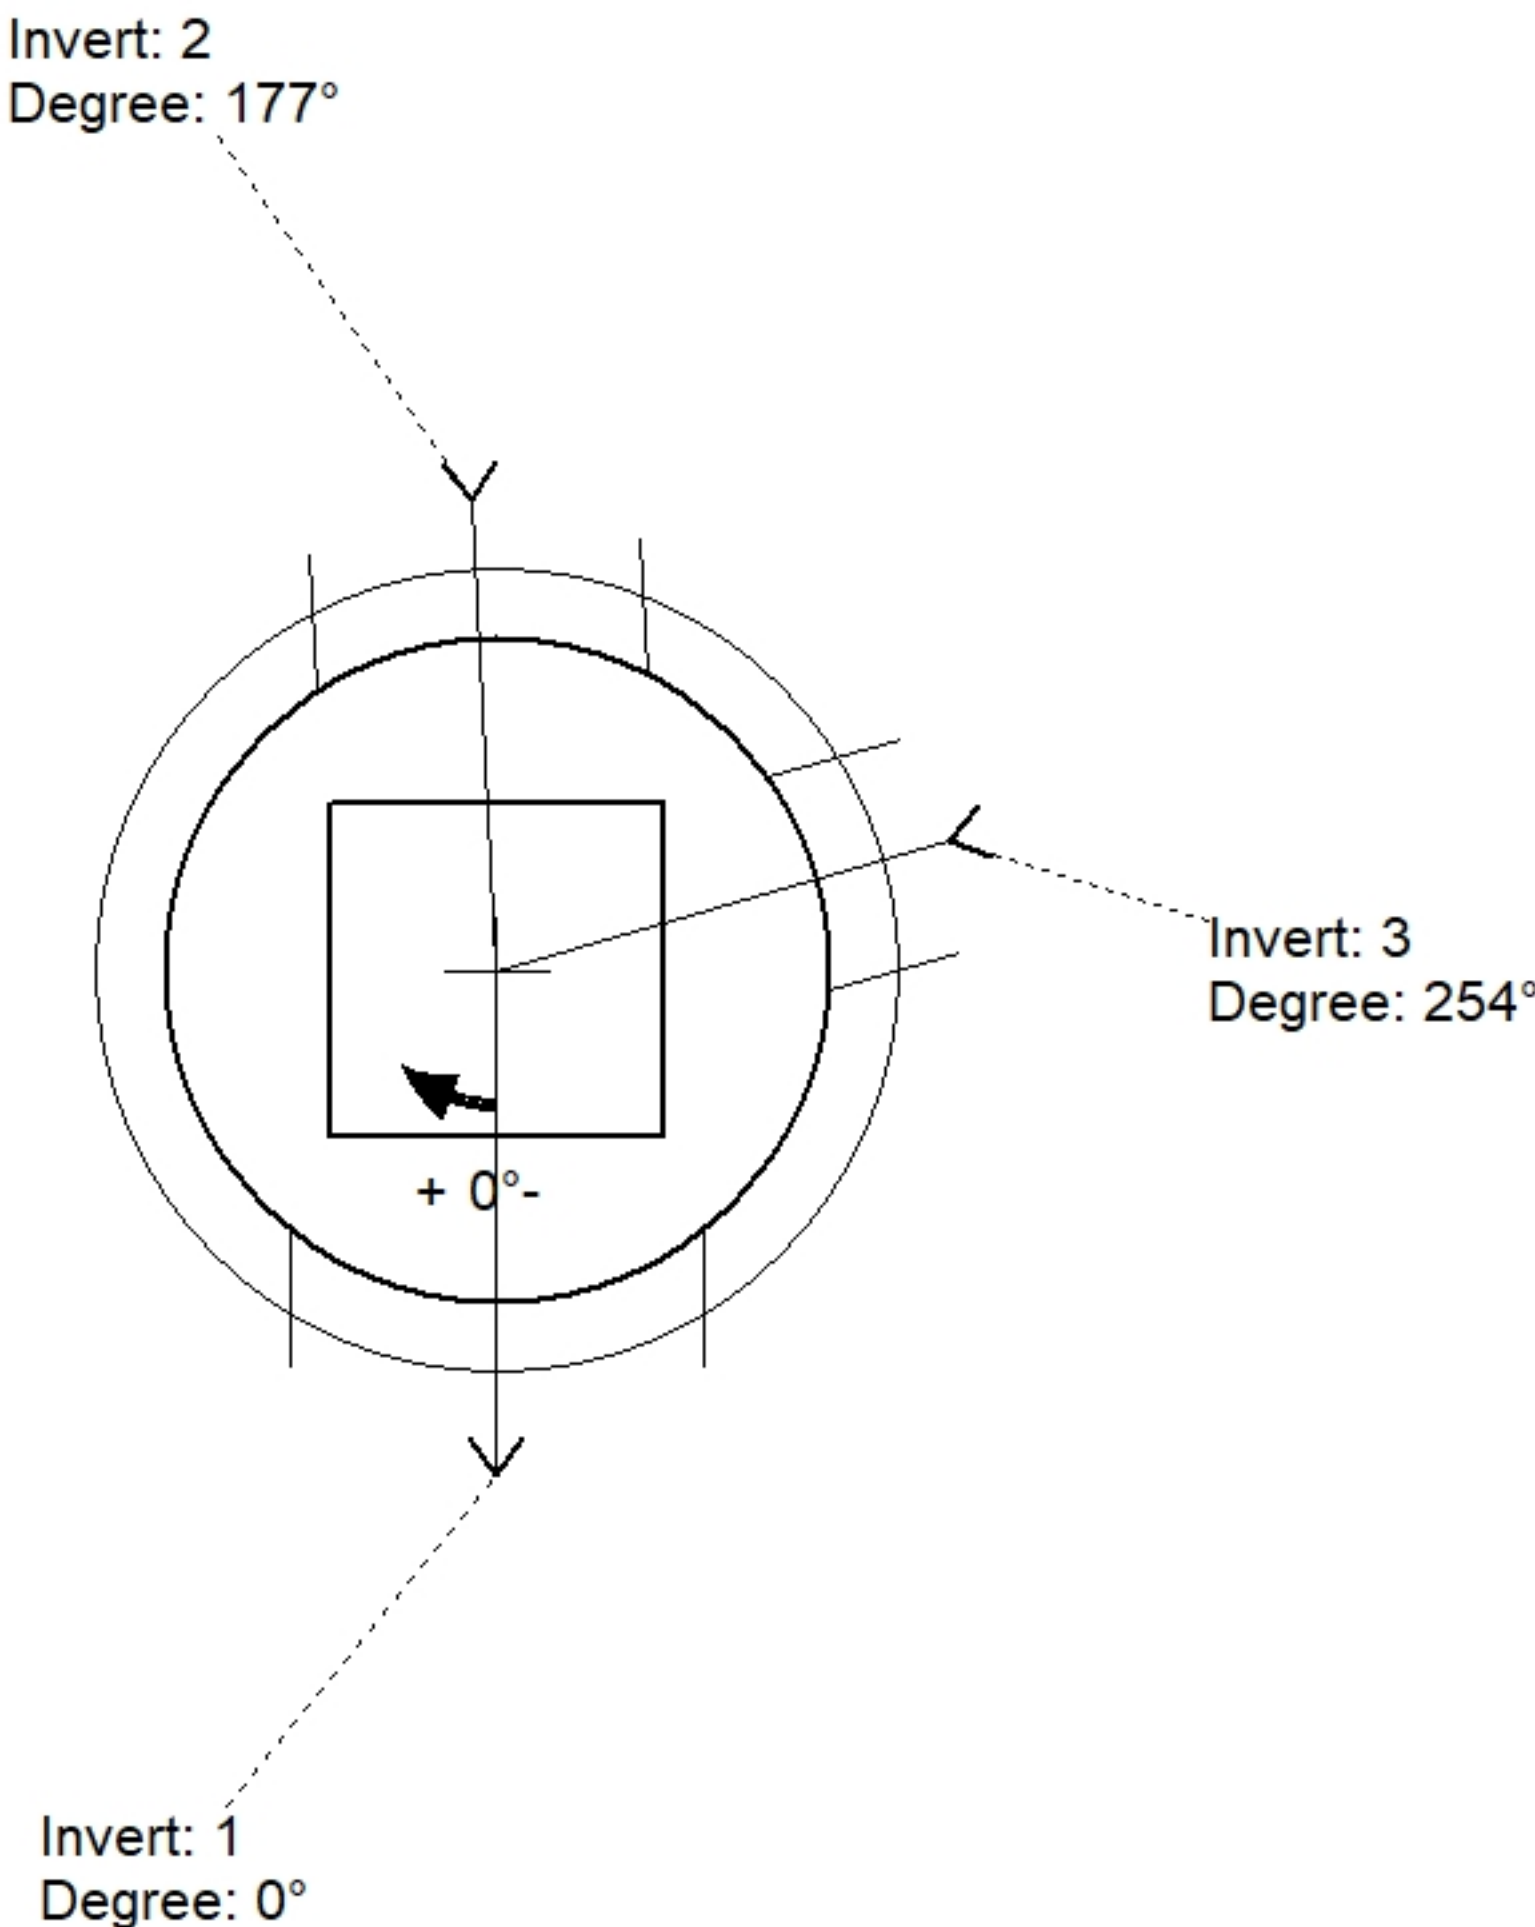

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	369.8'							
Reducer								
Invert 1	362.76'	0°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 2	363.26'	177°	18" HDPE	21.2"	24"	Hole 24	6.3"	P1
Invert 3	363'	254°	12" HDPE	14.5"	16"	Hole 16	3.53"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

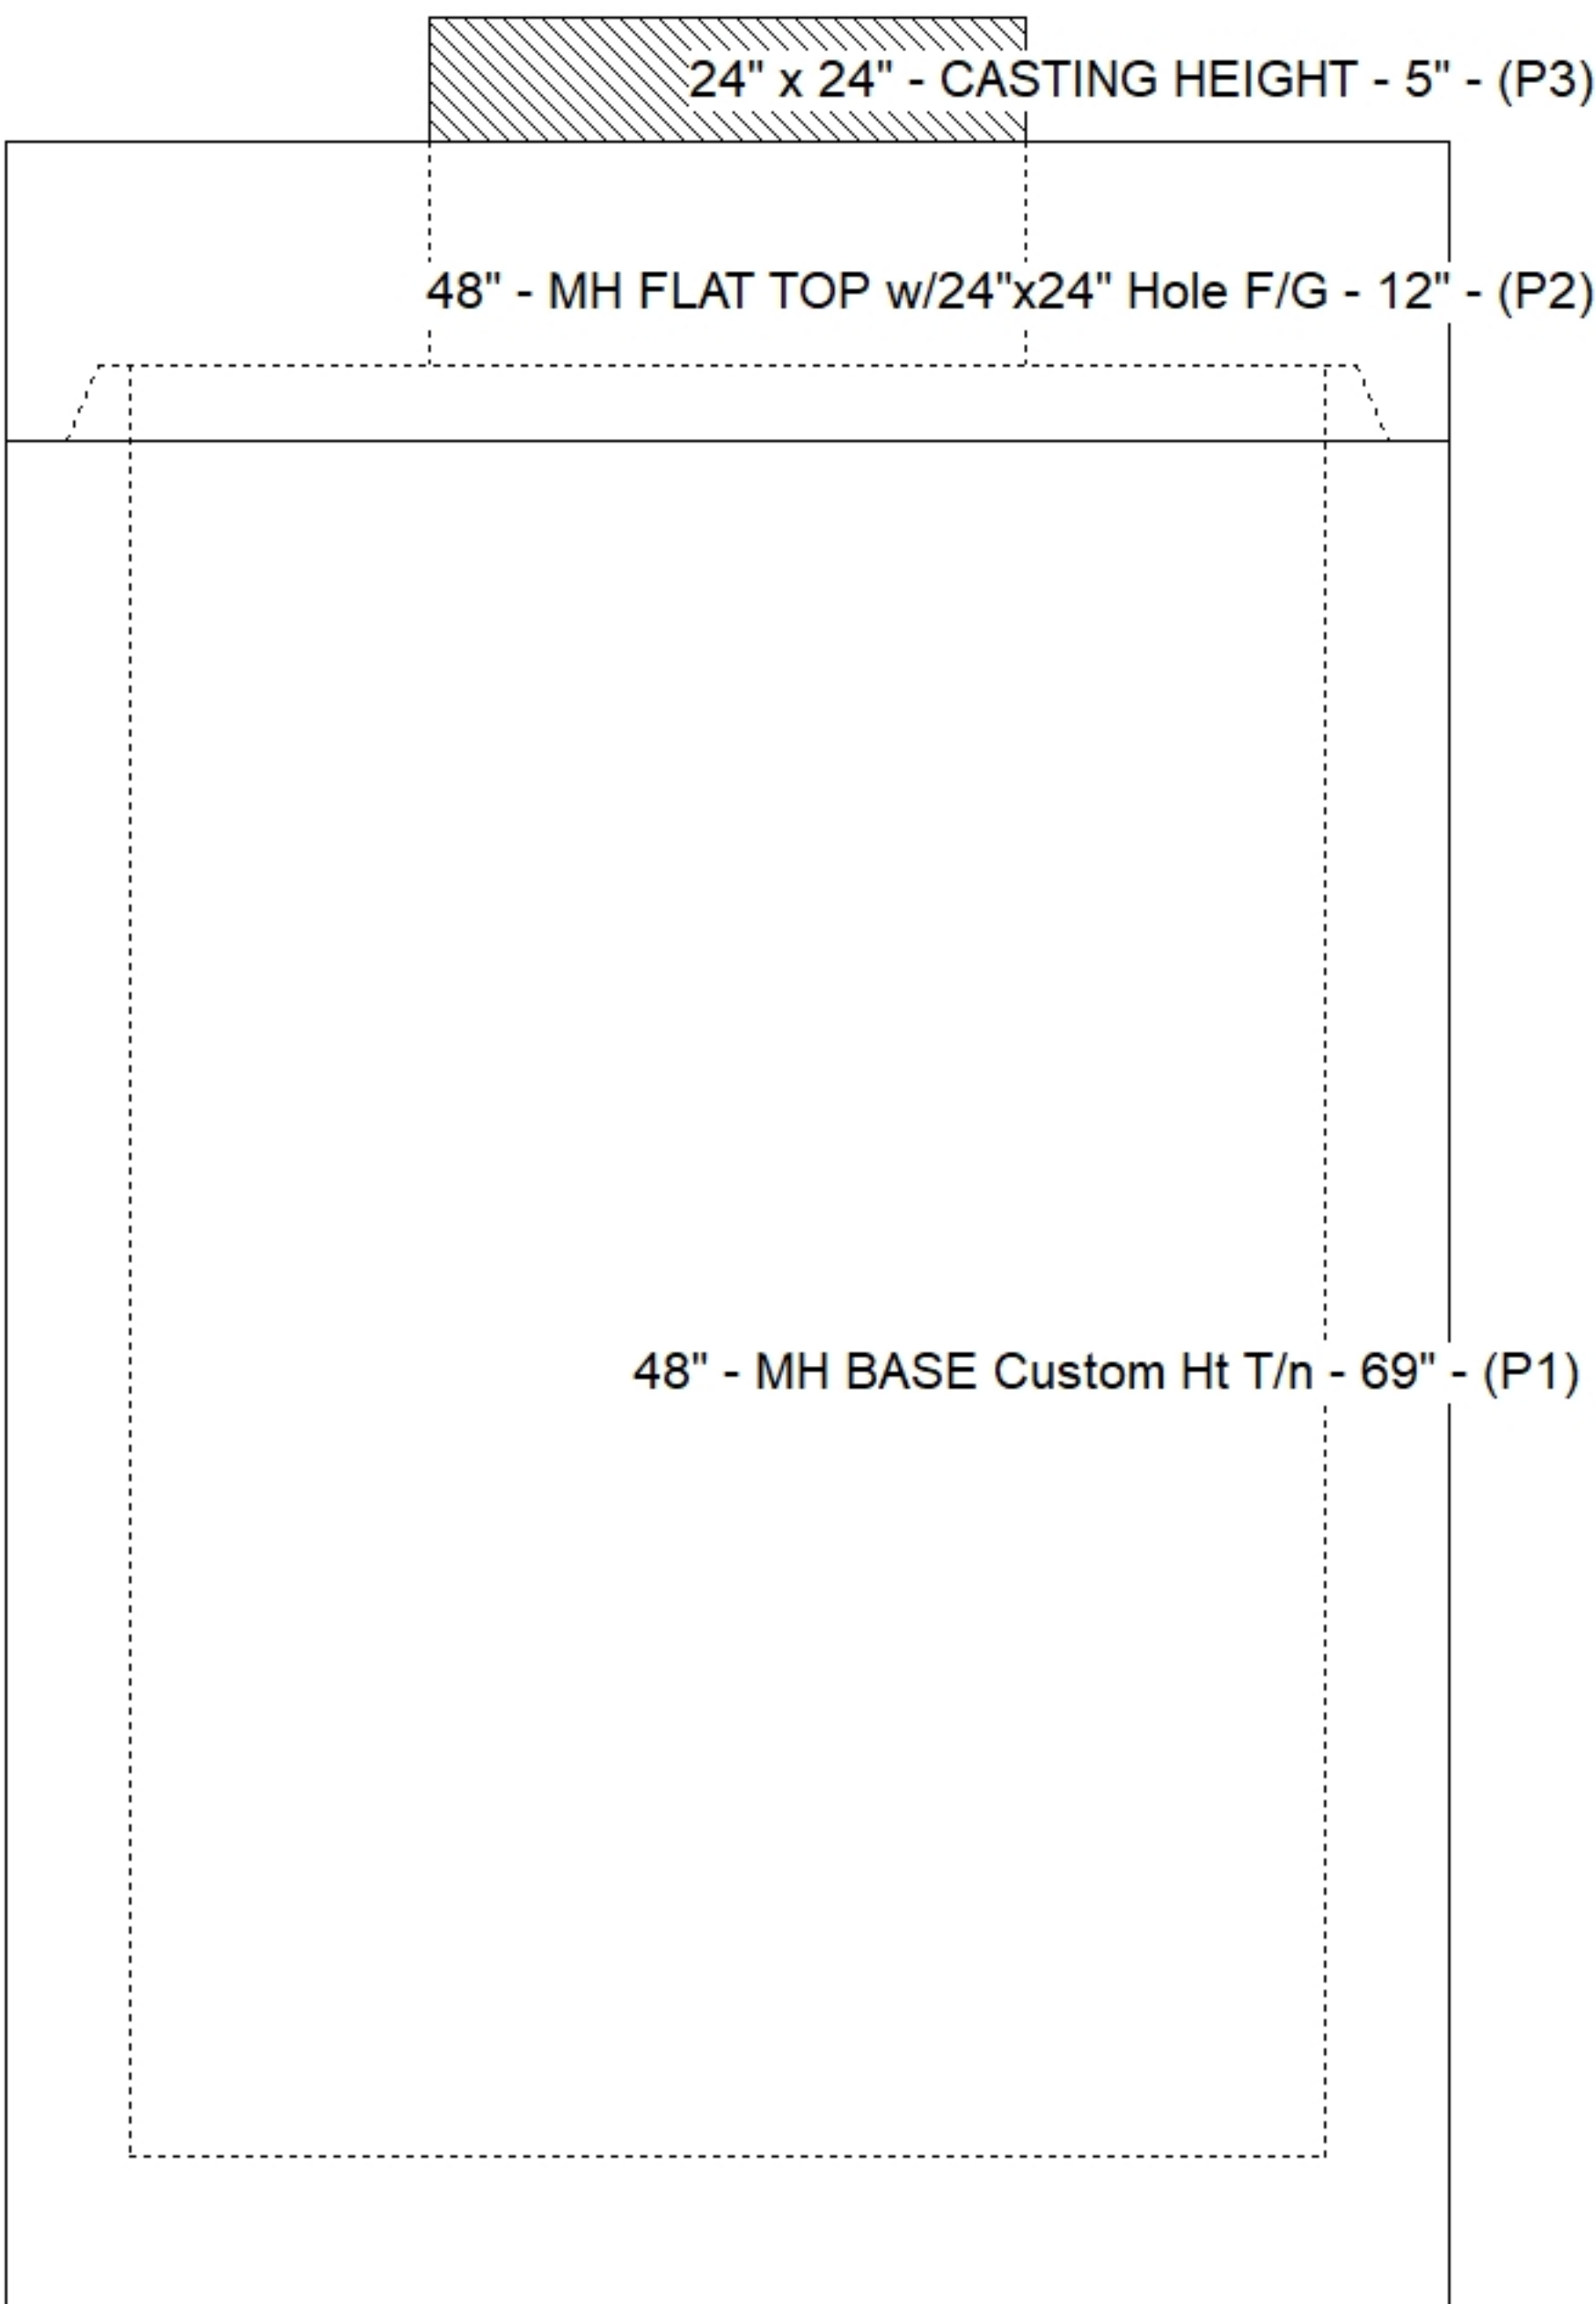

Default - Interior Dimensions

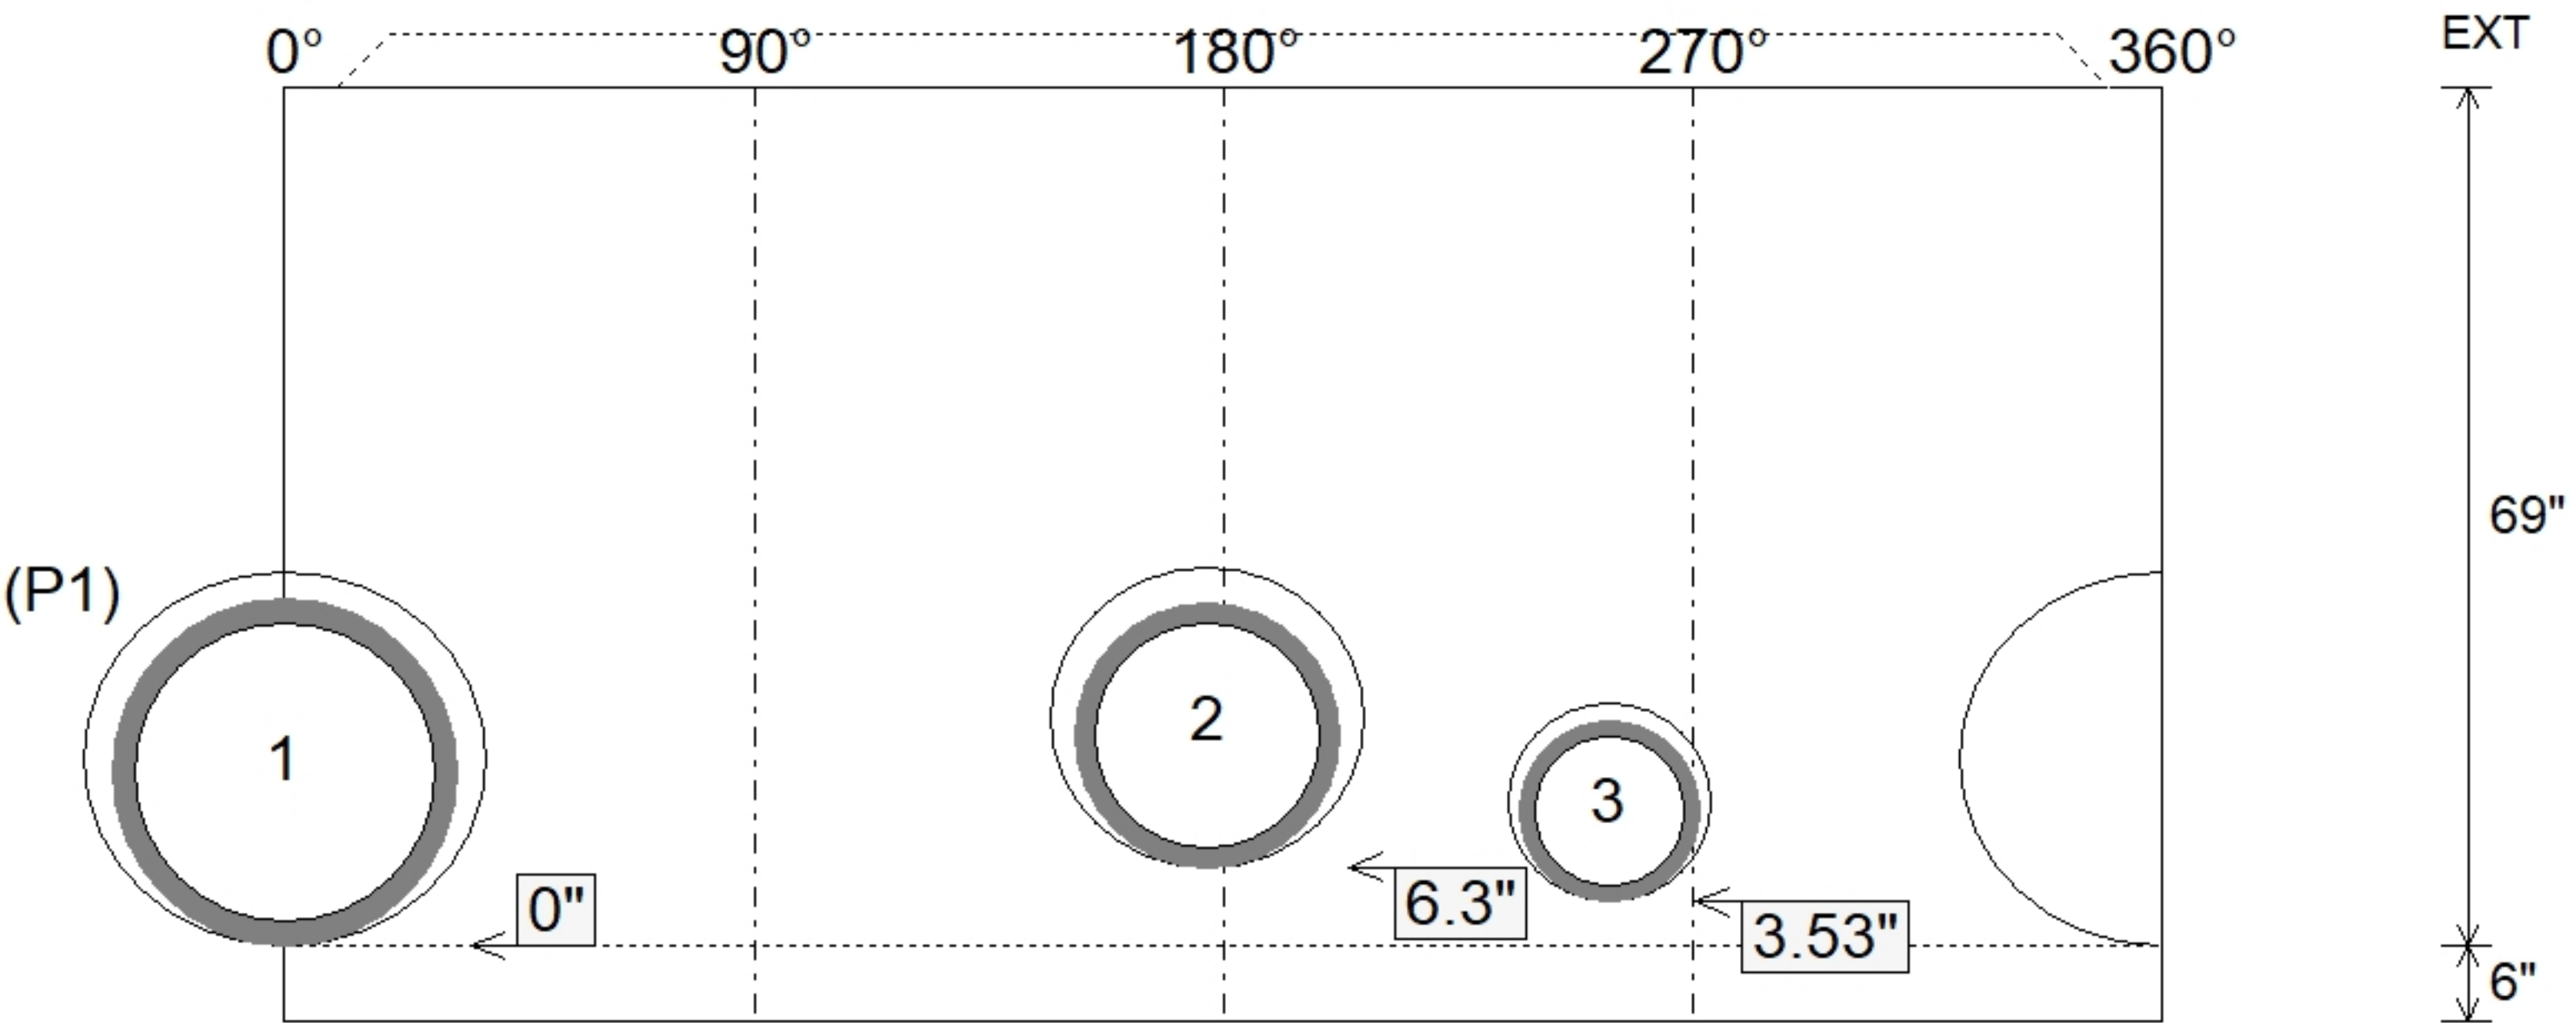

Submittal Drawing
6/16/2026 2:29:58 PM

SUBMITTAL
APPROVED BY:
