

Contractor: Central Paving Co. of Paducah, Inc.

Plant: Beaver Dam




Slack: 0.4"

REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 34" x 34" - CASTING HEIGHT - 3"
P2) 48" - MH FLAT TOP w/34"x34" Hole F/G - 12"
P1) 48" - MH BASE Custom Ht T/n - 51"
1) CASTING - HOE 595 F/G
1) 48" - Conseal CS-102 1.00"
2) Hole - 24
1) Hole - 16

0 lb
1194 lb
4413 lb
376 lb
0 lb
0 lb
0 lb


Structure Total: 5983 lb

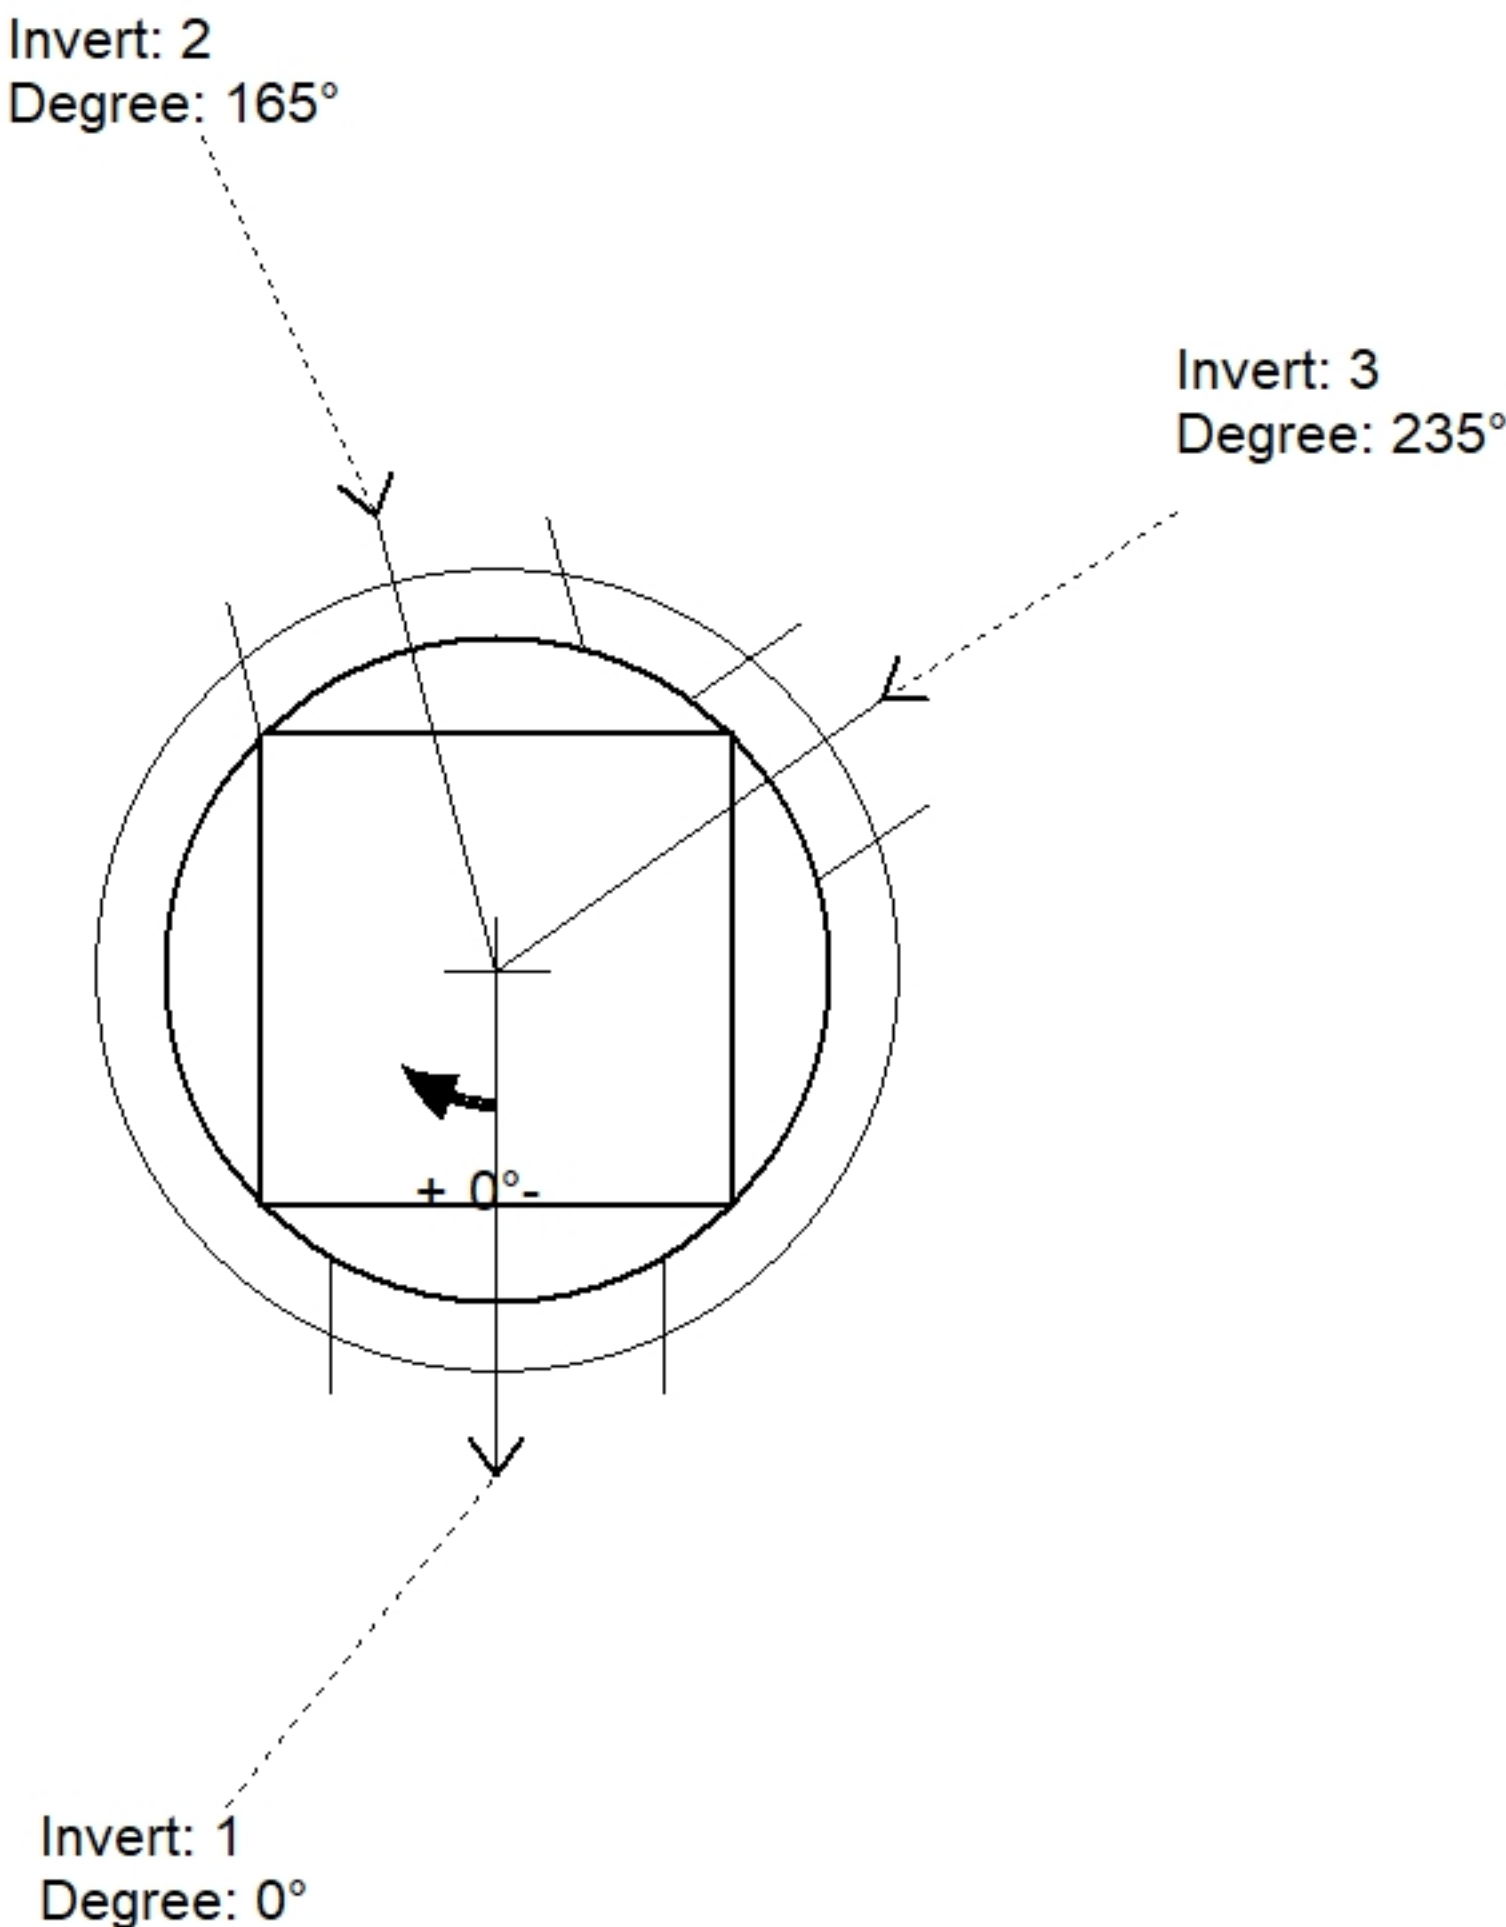

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	370.4'							
Reducer								
Invert 1	365'	0°	18" HDPE	21.2"	24"	Hole 24	0"	P1
Invert 2	365'	165°	18" HDPE	21.2"	24"	Hole 24	0"	P1
Invert 3	365'	235°	12" HDPE	14.5"	16"	Hole 16	0.35"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

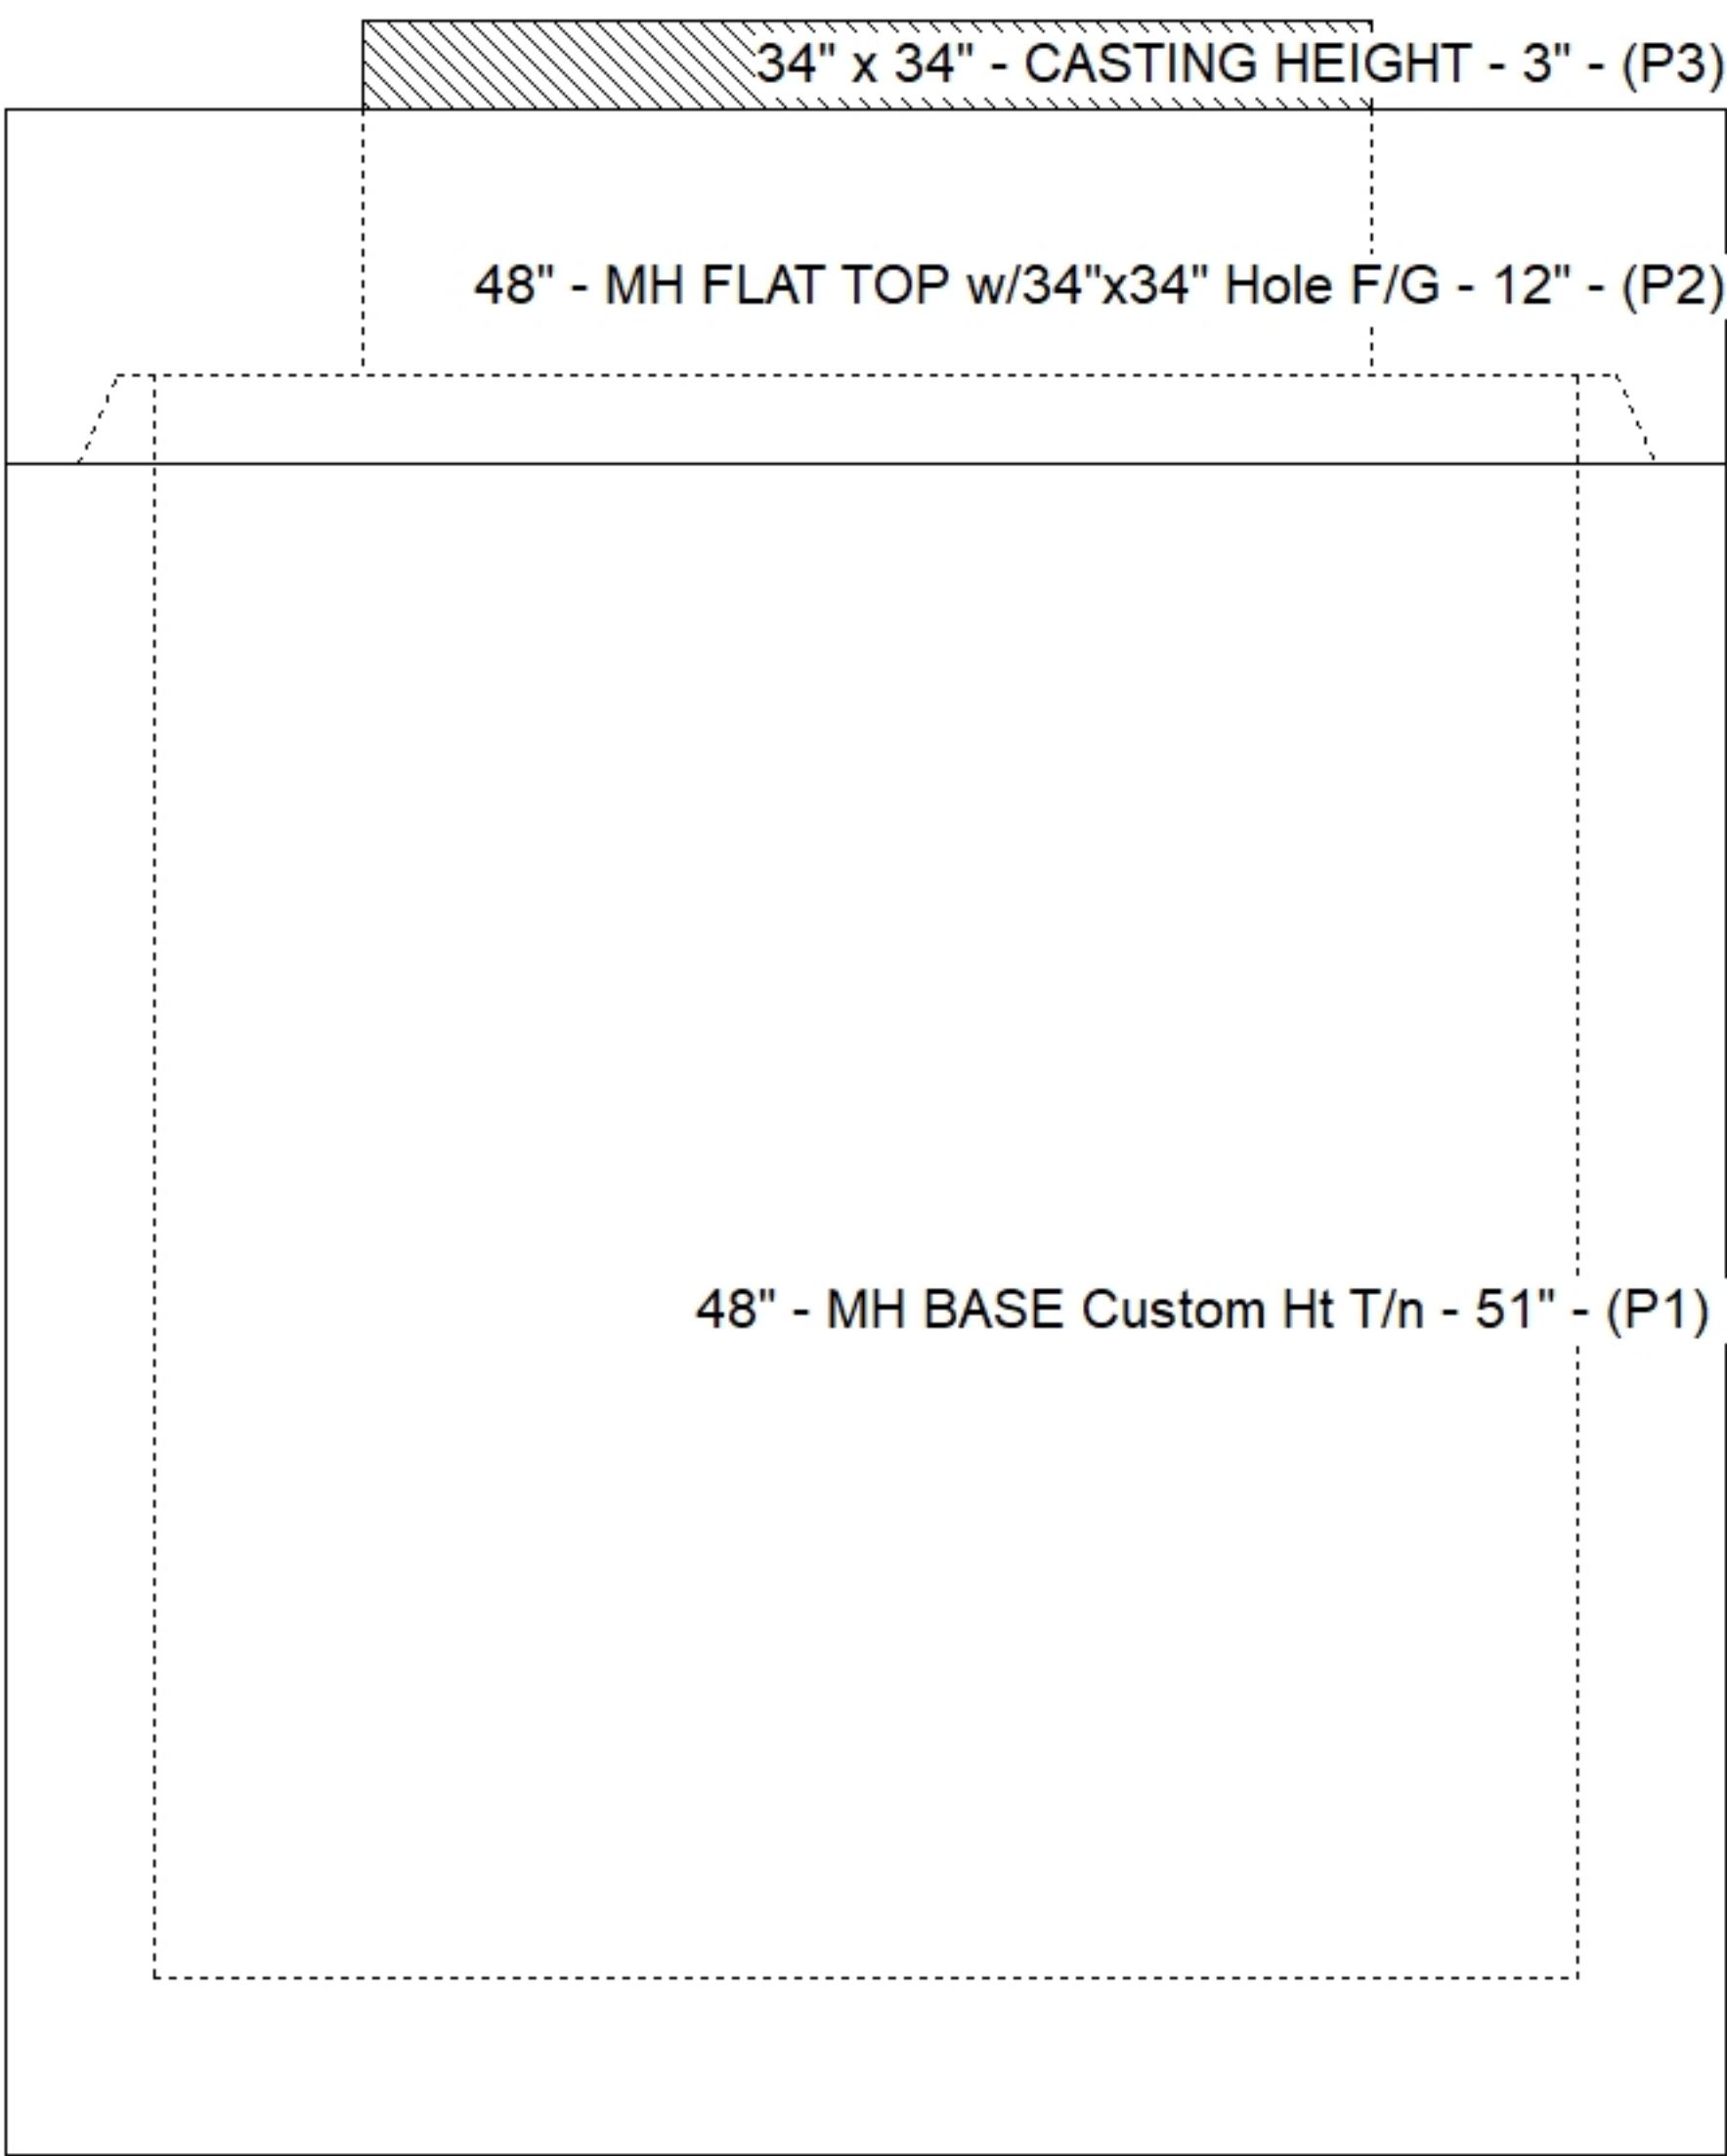

Default - Interior Dimensions

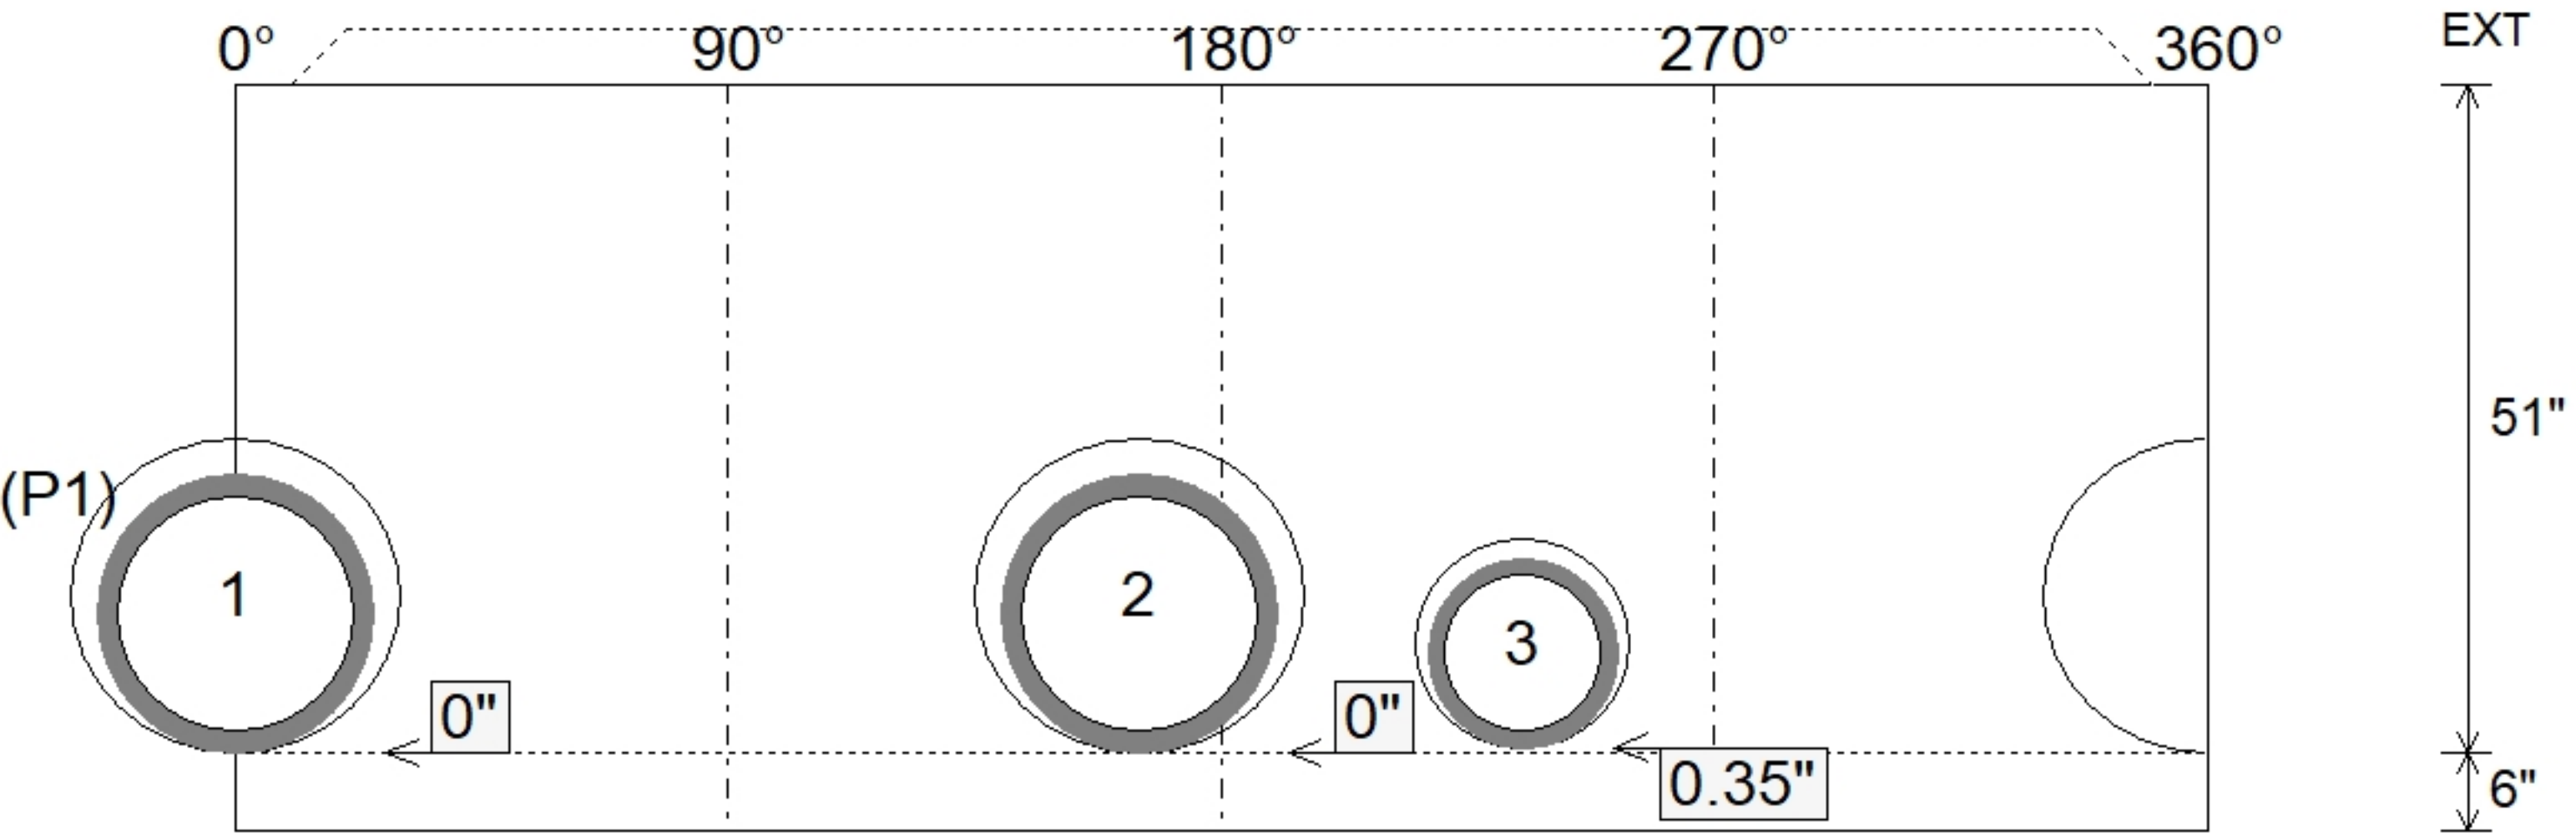

Submittal Drawing
6/16/2026 2:29:59 PM

SUBMITTAL
APPROVED BY:
