



Job Name: 26-2484 Bass Pro Shops Outpost Paducah Job Location: Paducah, KY Contractor: Central Paving Co. of Paducah, Inc.					Plant: Beaver Dam 6/16/2026 8:02:40 AM		Tech: S. Felletter PC: A. Chambers				
Structure ID: Y8.1 ST-CI											
P1 BX2424-08BAVF BOX BASE 8inW, 8inF, Variable Ht F/n											
P2) 24" x 24" - CASTING HEIGHT - 5" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 53" 1) CASTING - HOE KY-465 SET (CBI TY F) 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 24 1) Hole - 8					0 lb 5363 lb 465 lb 0 lb 0 lb 0 lb ----- 5828 lb Structure Total:		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 465 F/G/H). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 371.7' Rim to Invert: 4.7' Slack: 0" Sump: 1.6" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	367'	0°	20"	18" HDPE	21.2"	Hole 24	24"	24"	0"	0"	
Invert 2	367'	205°	23.809"	4" HDPE	4.8"	Hole 8	8"	8.827"	1.2"	-5"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

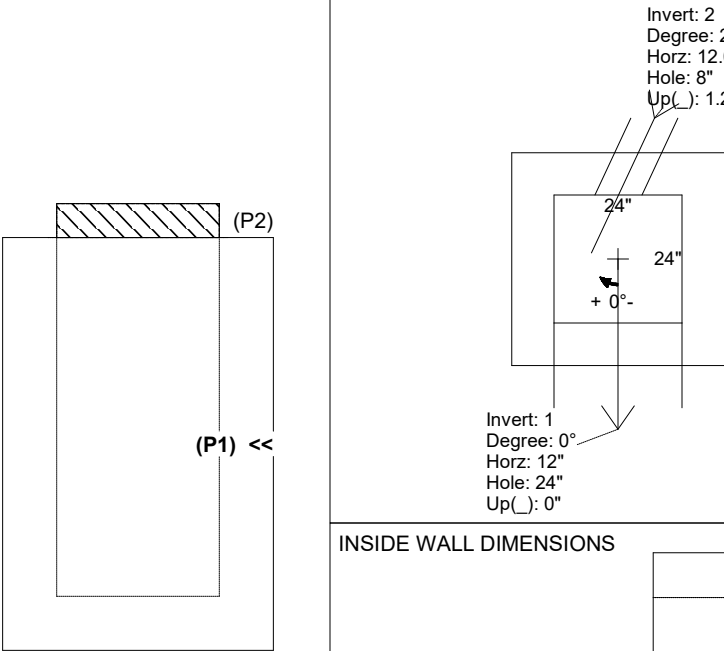

UPSIDE-DOWN VIEW (int. dimensions)

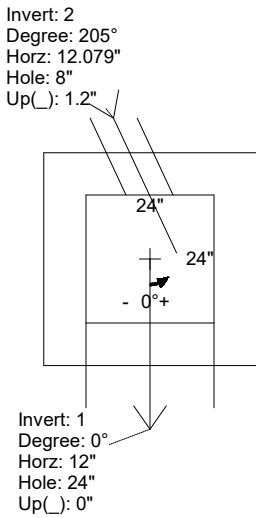

INSIDE WALL DIMENSIONS

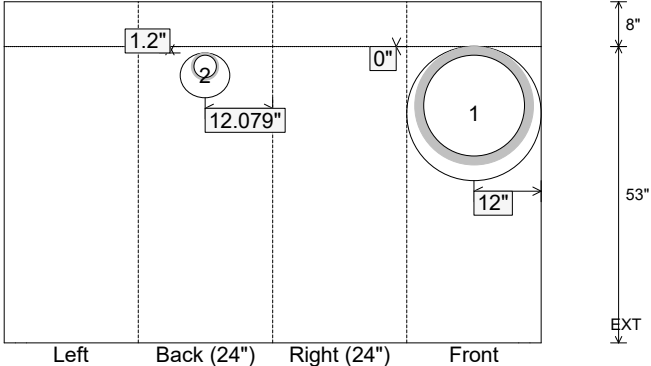

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 53" Height (Ext): 61"	Weight (Net): 5363 lb Volume (Net): 1.37cu.yd
----------------------------------	-------------------------------	--	--	--
