

Job Name: 26-2484 Bass Pro Shops Outpost Paducah
Job Location: Paducah, KY
Contractor: Central Paving Co. of Paducah, Inc.

Plant: Beaver Dam

Tech: S. Felletter

6/16/2026 8:03:48 AM

PC: A. Chambers



Structure ID: Y8.2 ST-MH

P3 GR4

GRADE RING F/F

P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING F/F - 4"
P2) 48" - ECC CONE w/ 24" HOLE F/G - 24"
P1) 48" - MH BASE T/n - 36"
1) CASTING - HOE MC-375 F/C Storm
1) 48" - Con Seal CS-102 1.00"
2) 24" - Con Seal CS-102 1.00"
3) Hole - 24

0 lb
270 lb
1550 lb
3253 lb
271 lb
0 lb
0 lb
0 lb

Structure Total: 5344 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE MC-375 F/C).

REINFORCING PER ASTM A615 (GRADE 60).


- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:


1. GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS:
 - CONCRETE: 4,000 PSI @ 28 DAYS.
 - REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)
2. WEIGHT: 4" 270 Lbs.

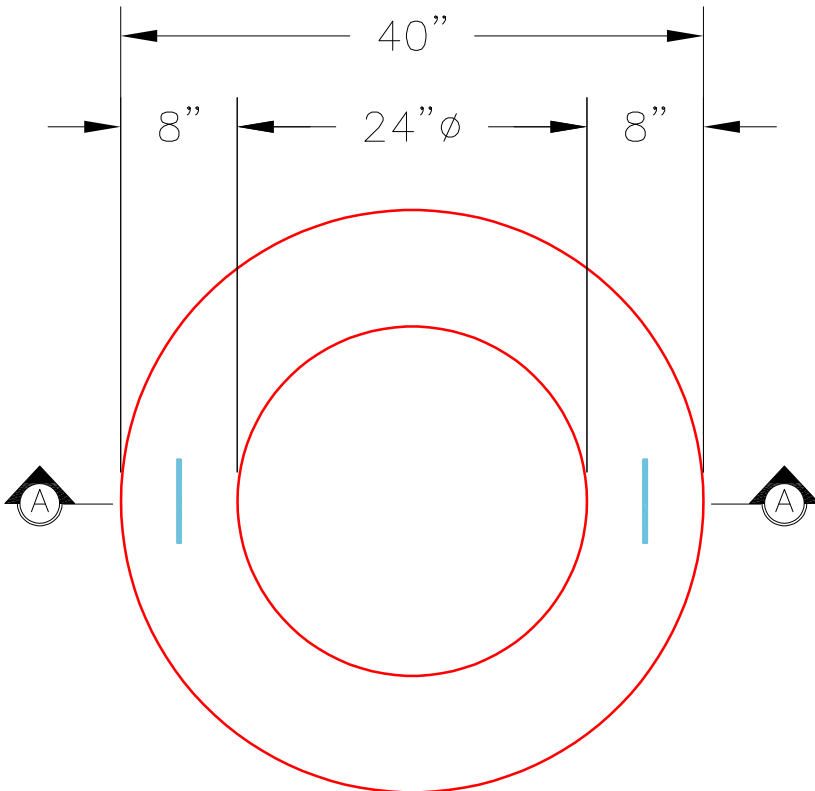

PLAN VIEW

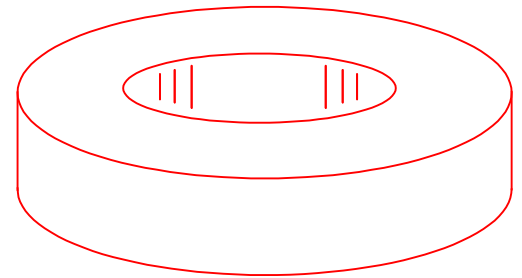

ISOMETRIC VIEW

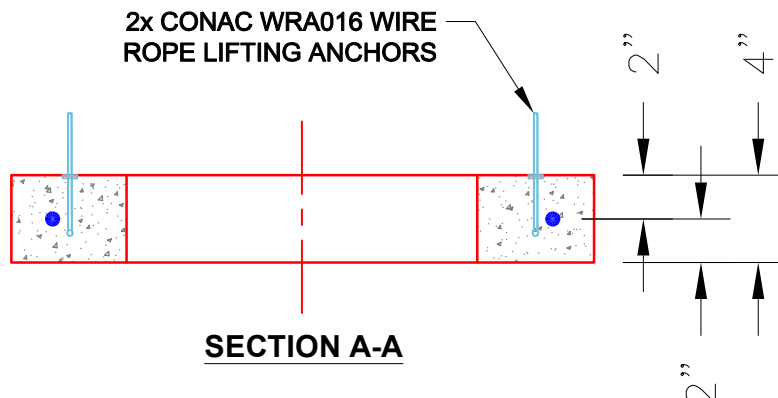

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 4"

Weight (Net): 270 lb
Volume (Net): 0.07cu.yd
