



Job Name: 26-2509 - Airpark Expansion Industrial Subdivision Job Location: Owensboro, KY 42301 Contractor: Koberstein Contracting, Inc.					Plant: 100 7/20/2026 10:55:15 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: Basin A DBI10											
P1 MH048BAVF		MH BASE (08"F) Custom Ht T/n									
P4) 16" x 28" - CASTING HEIGHT - 5" P3) 48" - MH FLAT TOP w/16"x28" Hole F/G - 12" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE (08"F) Custom Ht T/n - 40" 1) CASTING - HOE KY-550 F/G (DBI 10) 2) 48" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 18 7) MH Step ML-10-TDS-NCR - 10"					0 lb 1582 lb 3353 lb 4269 lb 550 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 9754 lb		Structure Notes: . 1. KYTC DBI TYPE 10 / ASTM C-478 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE KY-550 F/G (DBI 10)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 391.25' Rim to Invert: 8.75' Slack: 0" Sump: 0" Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	382.5'	0°	0"	15" HDPE	17.6"	Hole 20	20"	20.629"	-2.5"	0"	
Invert 2	382.5'	180°	91.125"	12" RCP B WALL	16"	Hole 18	18"	18.451", 8.951"	-3"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

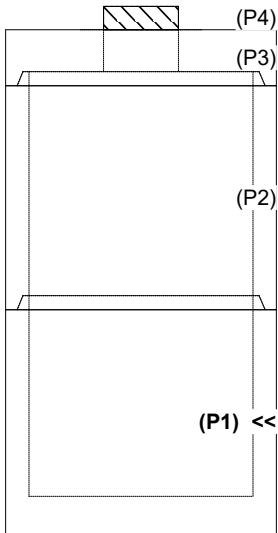

UPSIDE-DOWN VIEW (int. dimensions)

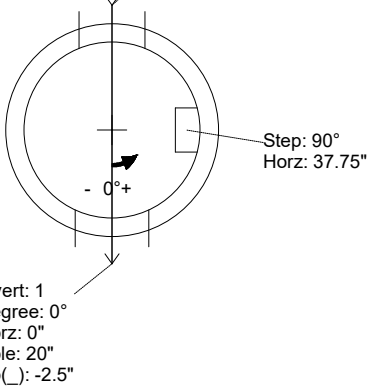

INSIDE WALL DIMENSIONS

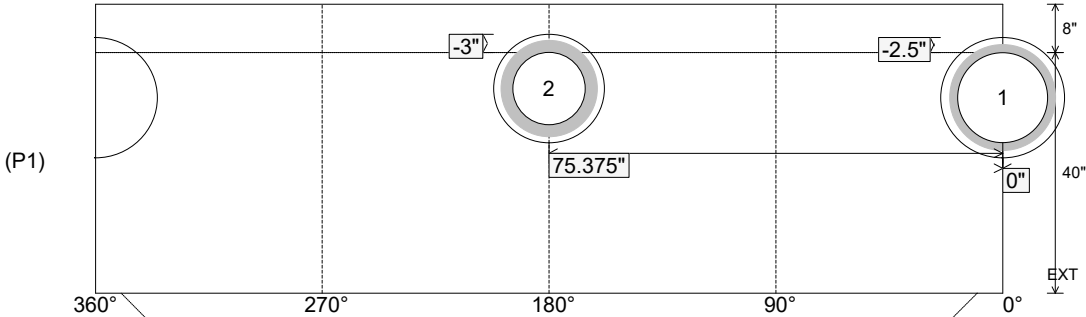

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 8"	Height (Int): 40" Height (Ext): 48"	Weight (Net): 4269 lb Volume (Net): 1.09cu.yd
----------------------------------	---------------------------------	--	--	--
