




Job Name: 26-2509 - Airpark Expansion Industrial Subdivision Job Location: Owensboro, KY 42301 Contractor: Koberstein Contracting, Inc.					Plant: 100 7/20/2026 4:20:48 PM		Tech: Jared - F PC: A. Chambers				
Structure ID: MH A-3 SS-MH											
P1 MH048BA30CDARED			MH BASE w/ConBlock-CDA Red T/n								
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - HOE MC-315 F/C RWRA 1) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-18L 1) PSX - 16M NYLO 6) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 3116 lb 3122 lb 0 lb 0 lb 1440 lb 0 lb 258 lb 0 lb 0 lb 12 lb 8 lb 0 lb ----- 8227 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY ICAST (HOE MC-315 F/C RWRA). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 394.5' Rim to Invert: 6.87' Slack: 1.44' Sump: 2" Step Position: 85°					Structure Total: 8227 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	387.63'	0°	0"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	0.5"	0"	
Invert 2	387.73'	170°	86"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	1.75"	0"	
Invert 3	387.83'	265°	134.125"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	2.375"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

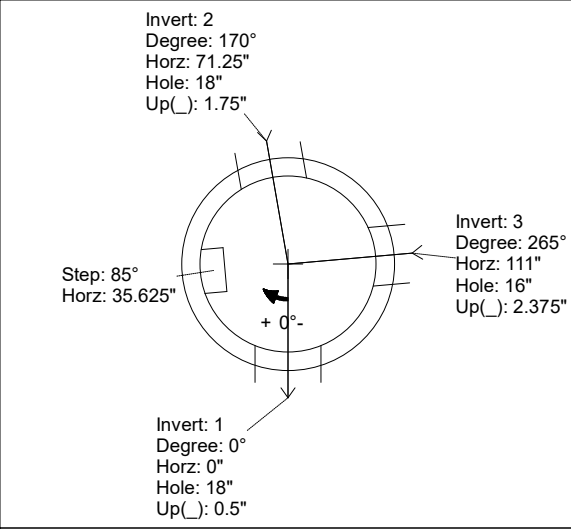


RIGHT-SIDE UP VIEW (int. dimensions)

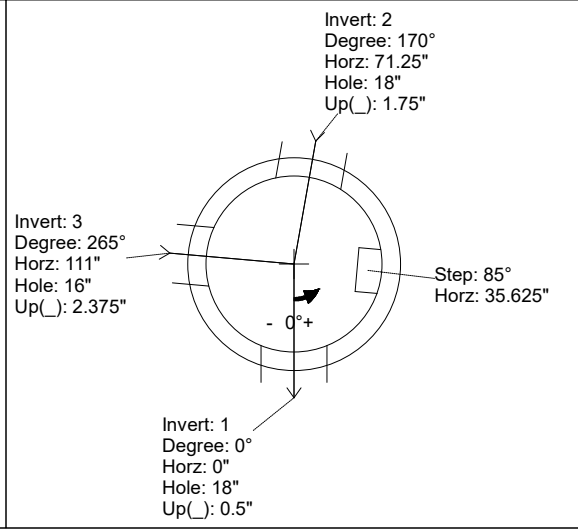

UPSIDE-DOWN VIEW (int. dimensions)

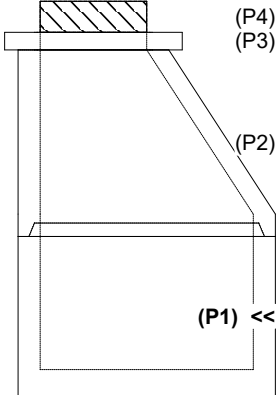

(P1) << (P2) (P3) (P4)

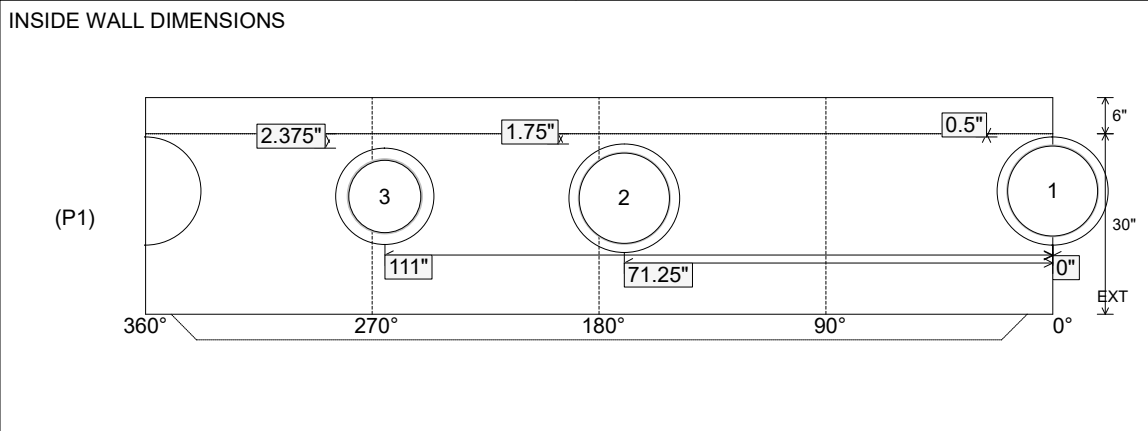

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3122 lb Volume (Net): 0.8cu.yd
----------------------------------	---------------------------------	--	--	---

Job Name: 26-2509 - Airpark Expansion Industrial Subdivision

Job Location: Owensboro, KY 42301

Contractor: Koberstein Contracting, Inc.

Plant: 100

7/20/2026 4:20:48 PM

Tech: Jared - F

PC: A. Chambers

Structure ID: MH A-3 SS-MH

P1 MH048BA30CDARED

MH BASE w/ConBlock-CDA Red T/n

P4) 24" - CASTING HEIGHT - 7"

P3) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4"

P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42"

P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30"

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT

1) ADMIXTURE CONBLOCK CDA RED

1) CASTING - HOE MC-315 F/C RWRA

1) 48" - Conseal CS-102 1.00" (Double)

2) 24" - Conseal CS-102 1.00" (Double)

2) Kor-N-Seal2 - S206-18L

1) PSX - 16M NYLO

6) MH Step ML-10-TDS-NCR - 10"

0 lb

270 lb

3116 lb

3122 lb

0 lb

0 lb

1440 lb

0 lb

258 lb

0 lb

0 lb

12 lb

8 lb

0 lb

8227 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. ADMIXTURE = CONBLOCK CDA RED.

4. CASTING SUPPLIED BY ICAST (HOE MC-315 F/C RWRA).

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 8227 lb

Rim: 394.5'

Rim to Invert: 6.87'

Slack: 1.44"

Sump: 2"

Step Position: 85°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	387.63'	0°	0"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	0.5"	0"
Invert 2	387.73'	170°	86"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	1.75"	0"
Invert 3	387.83'	265°	134.125"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	2.375"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

Invert: 2
Degree: 170°
Horz: 71.25"
Hole: 18"
Up(): 1.75"

Invert: 3
Degree: 265°
Horz: 111"
Hole: 16"
Up(): 2.375"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 18"
Up(): 0.5"

Step: 85°
Horz: 35.625"

FOR INVERT ONLY

UPSIDE-DOWN VIEW (int. dimensions)

Invert: 2
Degree: 170°
Horz: 71.25"
Hole: 18"
Up(): 1.75"

Invert: 3
Degree: 265°
Horz: 111"
Hole: 16"
Up(): 2.375"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 18"
Up(): 0.5"

Step: 85°
Horz: 35.625"

INSIDE WALL DIMENSIONS

2.375"

1.75"

0.5"

111"

71.25"

0"

360°

270°

180°

90°

0°

EXT

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 5"

Floor Height: 6"

Height (Int): 30"

Height (Ext): 36"

Weight (Net): 3122 lb

Volume (Net): 0.8cu.yd
