




Job Name: 26-2509 - Airpark Expansion Industrial Subdivision Job Location: Owensboro, KY 42301 Contractor: Koberstein Contracting, Inc.				Plant: 100 7/20/2026 10:55:14 AM		Tech: Jared - F PC: A. Chambers						
Structure ID: MH A-7 SS-MH												
P1 MH048BA24CDARED				MH BASE w/ConBlock-CDA Red T/n								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - HOE MC-315 F/C RWRA 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) Kor-N-Seal2 - S206-18L 5) MH Step ML-10-TDS-NCR - 10"						0 lb 1961 lb 2898 lb 0 lb 0 lb 1440 lb 0 lb 258 lb 0 lb 0 lb 6 lb 0 lb ----- Structure Total: 6563 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY ICAST (HOE MC-315 F/C RWRA). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 395'				Rim to Invert: 5'		Slack: 1"		Sump: 2"		Step Position: 180°		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	390'	0°	0"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	0.5"	0"		
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

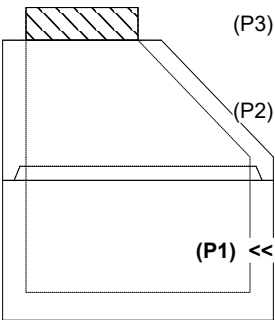


RIGHT-SIDE UP VIEW (int. dimensions)

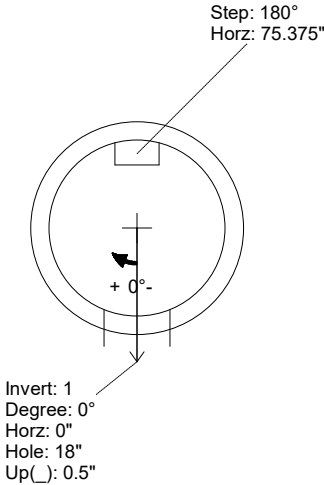

UPSIDE-DOWN VIEW (int. dimensions)

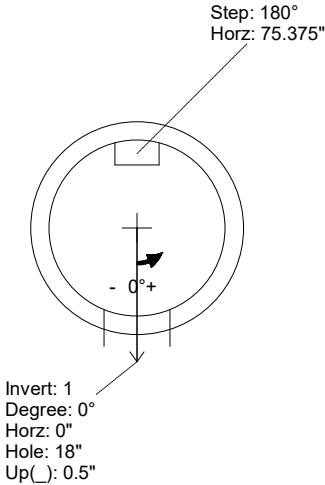

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2898 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-2509 - Airpark Expansion Industrial Subdivision

Job Location: Owensboro, KY 42301

Contractor: Koberstein Contracting, Inc.

Plant: 100

7/20/2026 10:55:14 AM

Tech: Jared - F

PC: A. Chambers



Structure ID: MH A-7 SS-MH

P1 MH048BA24CDARED

MH BASE w/ConBlock-CDA Red T/n

P3) 24" - CASTING HEIGHT - 7"

P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30"

P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24"

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT

1) ADMIXTURE CONBLOCK CDA RED

1) CASTING - HOE MC-315 F/C RWRA

1) 48" - Conseal CS-102 1.00" (Double)

1) 24" - Conseal CS-102 1.00" (Double)

1) Kor-N-Seal2 - S206-18L

5) MH Step ML-10-TDS-NCR - 10"

0 lb

1961 lb

2898 lb

0 lb

0 lb

1440 lb

0 lb

258 lb

0 lb

0 lb

6 lb

0 lb

6563 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. ADMIXTURE = CONBLOCK CDA RED.

4. CASTING SUPPLIED BY ICAST (HOE MC-315 F/C RWRA).

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total:

6563 lb

Rim: 395'

Rim to Invert: 5'


Slack: 1"

Sump: 2"


Step Position: 180°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	390'	0°	0"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	0.5"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

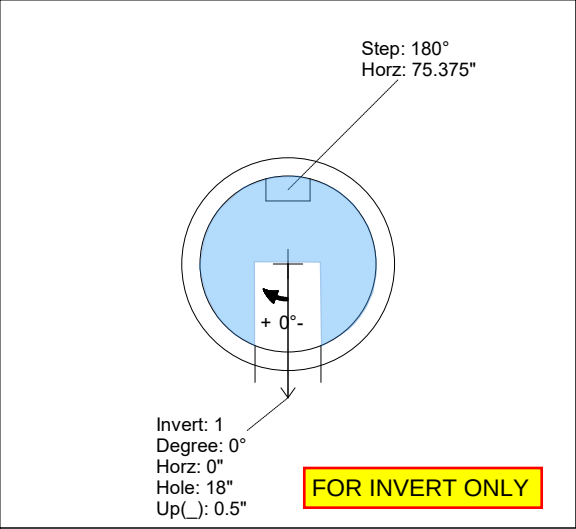

UPSIDE-DOWN VIEW (int. dimensions)

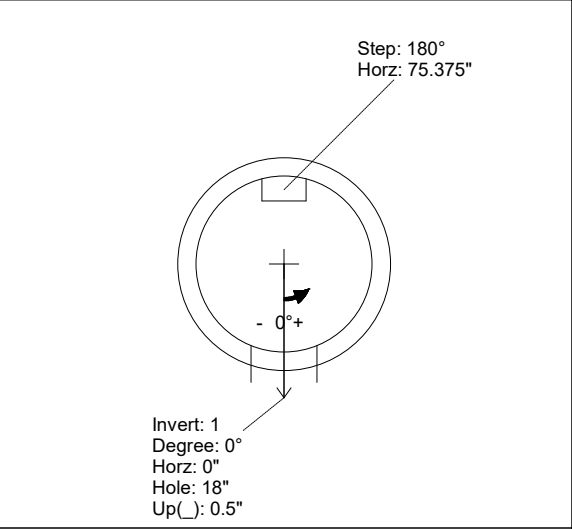

INSIDE WALL DIMENSIONS

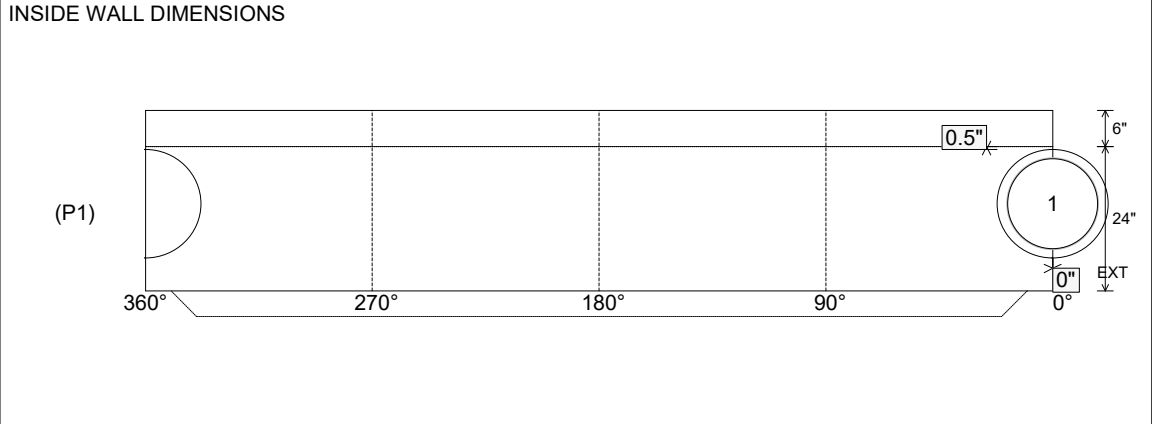

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 5"

Floor Height: 6"

Height (Int): 24"

Height (Ext): 30"

Weight (Net): 2898 lb

Volume (Net): 0.74cu.yd
