

Contractor: Koberstein Contracting, Inc.

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 6.58'

Floor Height: 6"

Slack: 1.96"

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:

P3) 24" - CASTING HEIGHT - 7"

0 lb

P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 42"

3116 lb

P1) 48" - MH BASE w/ConBlock-CDA Red - 30"

3255 lb

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

0 lb

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

0 lb

1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT

1440 lb

1) ADMIXTURE CONBLOCK CDA RED

0 | b

1) CASTING - HOE MC-315 F/C RWRA

258 lb

1) 48" - Conseal CS-102 1.00" (Double)

0 lb

1) 24" - Conseal CS-102 1.00" (Double)

0 lb


2) PSX - 16M NYLO

16 lb


6) MH Step ML-10-TDS-NCR - 10"

0 lb

Structure Total: 8085 lb



Invert: 2
Degree: 225°




24" - CASTING HEIGHT - 7" - (P3)

48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 42" - (P2)

48" - MH BASE w/ConBlock-CDA Red - 30" - (P1)

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	395'							
Reducer								
Invert 1	388.42'	0°	12" PVC SDR35	12.5"	16"	PSX 16M NYLO	0"	P1
Invert 2	388.52'	225°	12" PVC SDR35	12.5"	16"	PSX 16M NYLO	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

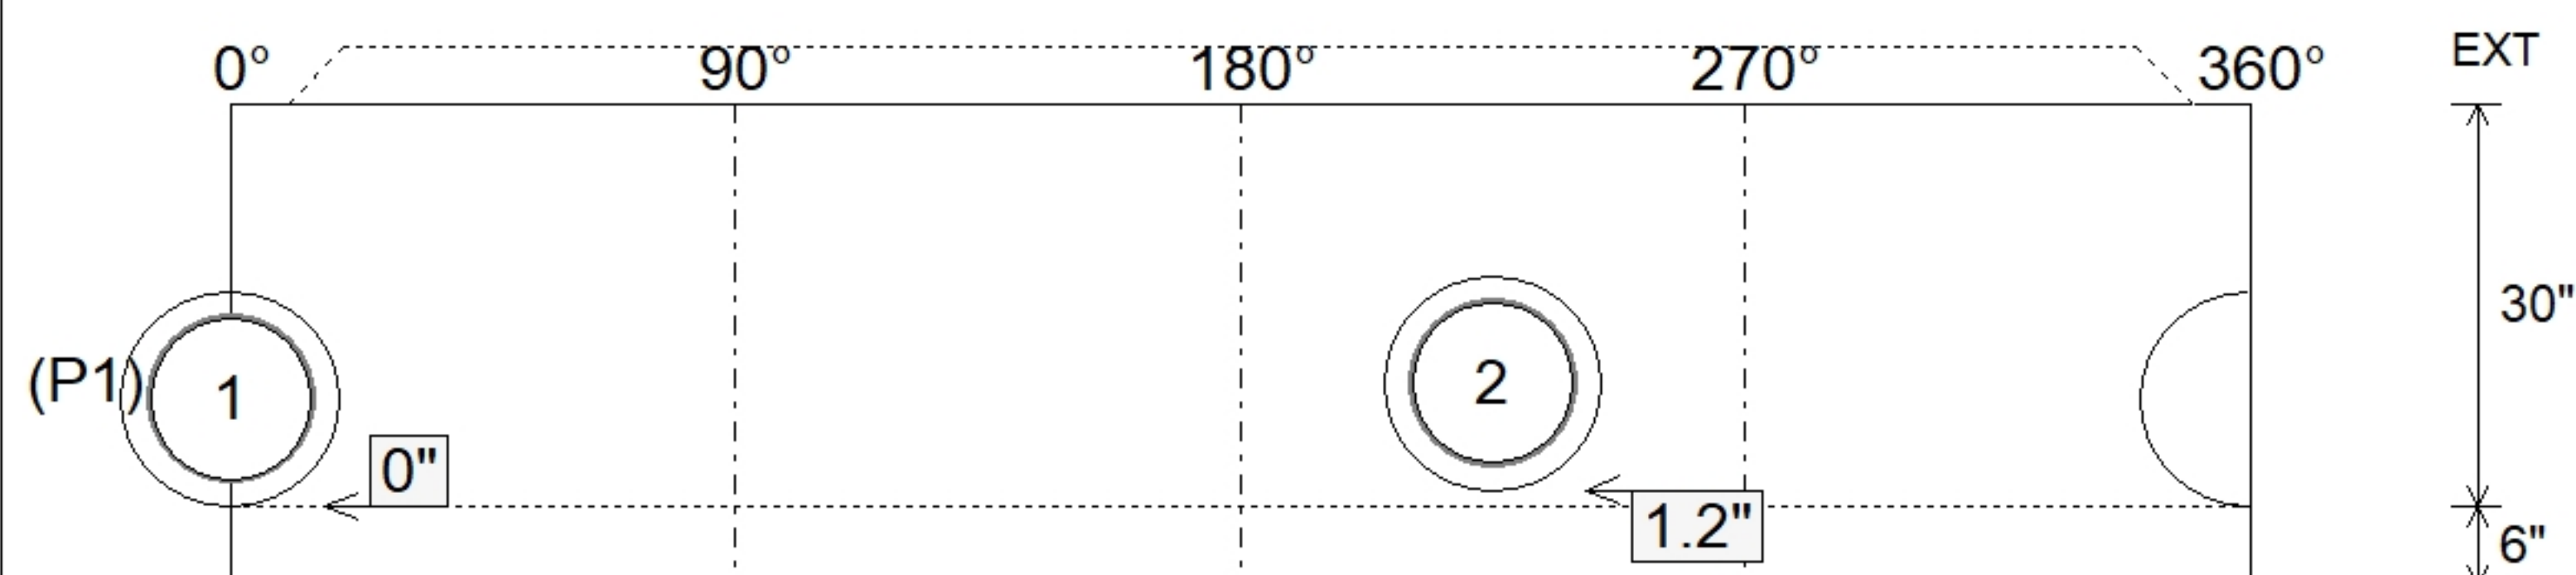

Submittal Drawing
7/22/2026 9:08:31 AM

SUBMITTAL
APPROVED BY:
