


Job Name: 26-2513- Stagner Farms Subdivision Sec. 2 Job Location: Bowling Green, KY Contractor: R.A. Alexander & Sons, Inc.		Plant: 100 8/7/2026 10:22:03 AM	Tech: Jared - A PC: Trevor Lewis	


Structure ID: AA1 SS-MH

P3 MH048CN30

ECC CONE w/ 24" HOLE

P4) 24" - CASTING HEIGHT - 7"	0 lb	Structure Notes: 1. HOE MC-375 F/C SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
P3) 48" - ECC CONE w/ 24" HOLE - 30"	2050 lb	
P2) 48" - MH RISER - 48"	3353 lb	
P1) 48" - MH BASE Custom Ht - 32"	3471 lb	
1) JOINT WRAP - 12" WD x 048" MAC WRAP	0 lb	
1) 48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb	
1) CASTING - HOE MC-375 F/C Sanitary	271 lb	
2) 48" - Conseal CS-102 1.00" (Double)	0 lb	
1) 24" - Conseal CS-102 1.00" (Double)	0 lb	
3) A-Lok - 0285	3 lb	
9) MH Step ML-10-TDS-NCR - 10"	0 lb	
Structure Total:		10588 lb

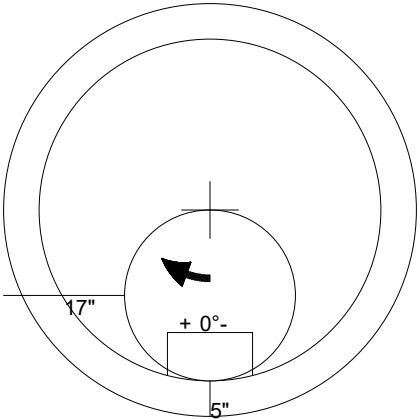



48" - ECC CONE w/ 24" HOLE - 30" - (P3)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 2050 lb Volume (Net): 0.41cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	--
