



Job Name: 26-2513- Stagner Farms Subdivision Sec. 2 Job Location: Bowling Green, KY Contractor: R.A. Alexander & Sons, Inc.					Plant: 100 9/22/2026 8:17:05 AM		Tech: Jared - A PC: Trevor Lewis			
Structure ID: D2 ST-CI										
P1 BX2436-08BA36 BOX BASE 8inW, 8inF										
P2) 24" x 36" - CASTING HEIGHT - 6.25" P1) 24" x 36" - BOX BASE 8inW, 8inF - 36" 1) CASTING - EJ 4510 F/G 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 28					0 lb 4243 lb 445 lb 0 lb 0 lb ----- 0 lb Structure Total: 4688 lb		Structure Notes: 1. EJ 4510 F/G PROVIDED BY ICAST. 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 558.2'					Rim to Invert: 3.49'		Slack: 0.13"		Sump: 0.5"	
Step Position: 180°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	554.71'	90°	26"	24" CMP	25"	Hole 28	28"	28"	0"	0"
Invert 2	554.71'	270°	26"	24" CMP	25"	Hole 28	28"	28"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

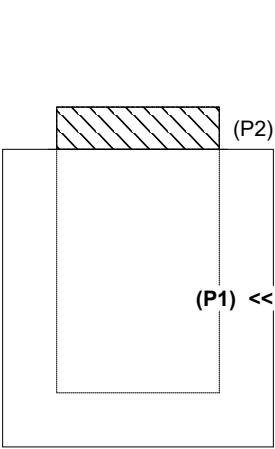

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

INSIDE WALL DIMENSIONS

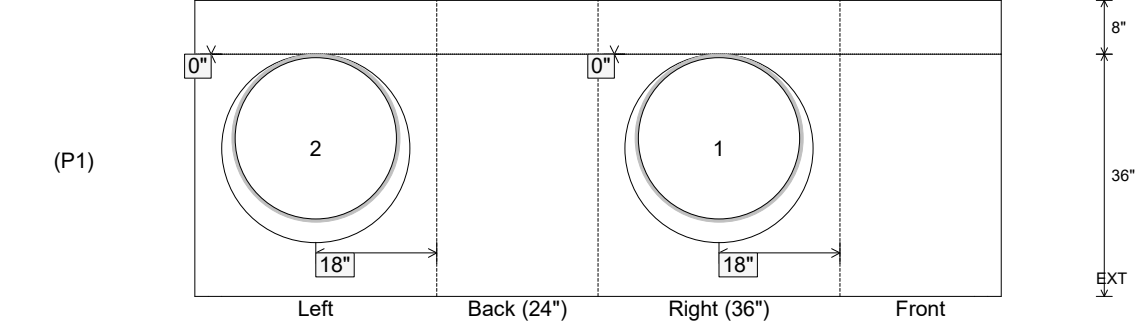

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 4243 lb Volume (Net): 1.08cu.yd
----------------------------------	-------------------------------	--	--	--
