




Job Name: 26-2513- Stagner Farms Subdivision Sec. 2 Job Location: Bowling Green, KY Contractor: R.A. Alexander & Sons, Inc.					Plant: 100 9/22/2026 8:17:17 AM		Tech: Jared - A PC: Trevor Lewis				
Structure ID: D3 ST-CI											
P1 BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht									
P2) 24" x 36" - CASTING HEIGHT - 6.25" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 33" 1) CASTING - EJ 4510 F/G 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 28 1) Hole - 22					0 lb 4095 lb 445 lb 0 lb 0 lb 0 lb ----- Structure Total: 4540 lb		Structure Notes: 1. EJ 4510 F/G PROVIDED BY ICAST. 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 558.2'					Rim to Invert: 3.23'		Slack: 0.01"		Sump: 0.5"		Step Position: 180°
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	554.97'	90°	26"	24" CMP	25"	Hole 28	28"	28"	0"	0"	
Invert 2	554.97'	270°	26"	18" CMP	19"	Hole 22	22"	22"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

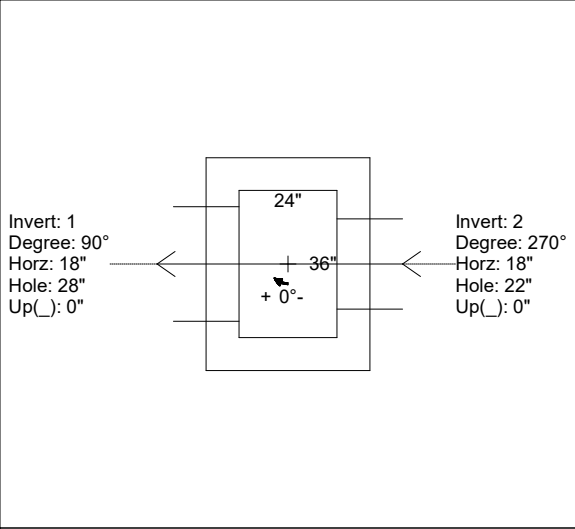

RIGHT-SIDE UP VIEW (int. dimensions)

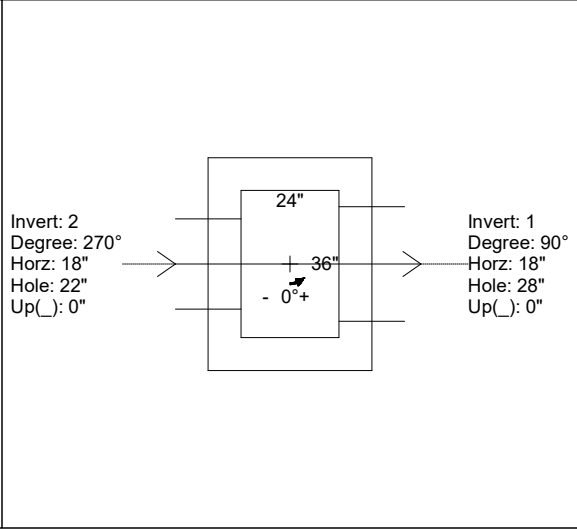


UPSIDE-DOWN VIEW (int. dimensions)

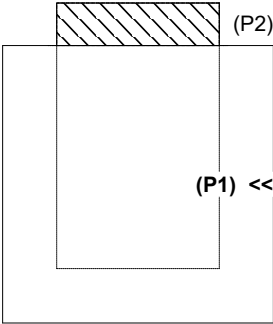

(P2)

(P1) <<

INSIDE WALL DIMENSIONS

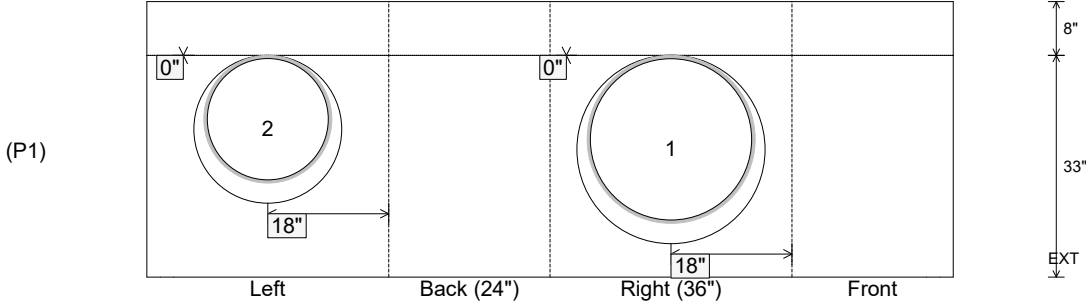

(P1)

Left Back (24") Right (36") Front

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 33" Height (Ext): 41"	Weight (Net): 4095 lb Volume (Net): 1.05cu.yd
----------------------------------	-------------------------------	--	--	--
