



Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1 Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.				Plant: Beaver Dam 8/24/2026 8:08:24 AM		Tech: J. ROSS PC: E. BRADLEY						
Structure ID: A2 SS-MHD												
P1 MH048BA42CDARED				MH BASE w/DROP/ConBlock-CDA Red								
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red - 3" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 36" P2) 48" - MH RISER w/DROP/ConBlock-CDA Red - 72" P1) 48" - MH BASE w/DROP/ConBlock-CDA Red - 42" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) Drop Tee - 8" PVC 1) Drop Elbow - 8" PVC 12) MH Step ML-10-TDS-NCR - 10"						0 lb 202 lb 2251 lb 5006 lb 4192 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 8 lb 0 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 4. CASTING BY OTHERS 5. ADMIXTURE = CONBLOCK-CDA RED				
Rim: 931.36' Rim to Invert: 13.2' Slack: 0.4" Sump: 2"				Structure Total: 13358 lb Step Position: 0"								
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	918.16'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"		
Invert 2												
Invert 3	918.26'	180°	91.106"	8" PVC SDR35	8.5"	Drop Elbow 8" PVC	8.5"	8.545"	2.95"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

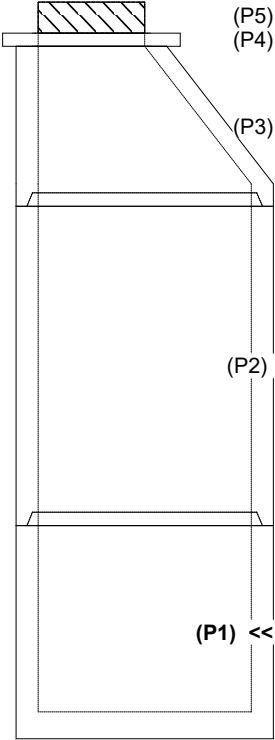

(P5)
(P4)
(P3)
(P2)
(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

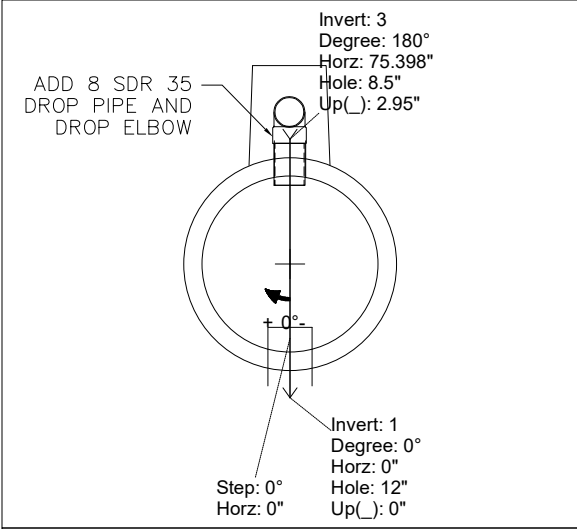


Invert: 3
Degree: 180°
Horz: 75.398"
Hole: 8.5"
Up(): 2.95"

ADD 8 SDR 35
DROP PIPE AND
DROP ELBOW

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"

UPSIDE-DOWN VIEW (int. dimensions)

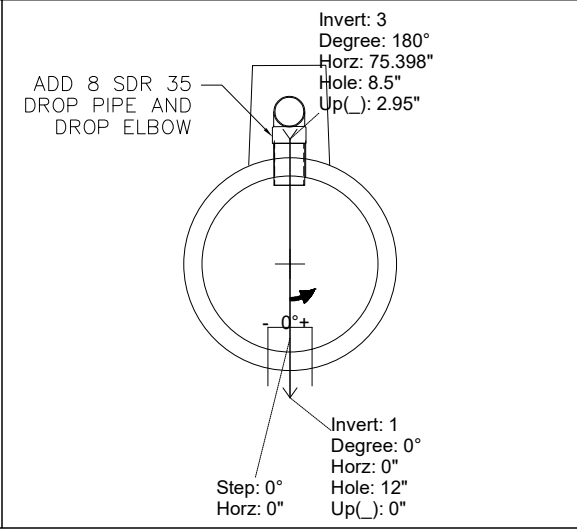


Invert: 3
Degree: 180°
Horz: 75.398"
Hole: 8.5"
Up(): 2.95"

ADD 8 SDR 35
DROP PIPE AND
DROP ELBOW

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"

INSIDE WALL DIMENSIONS

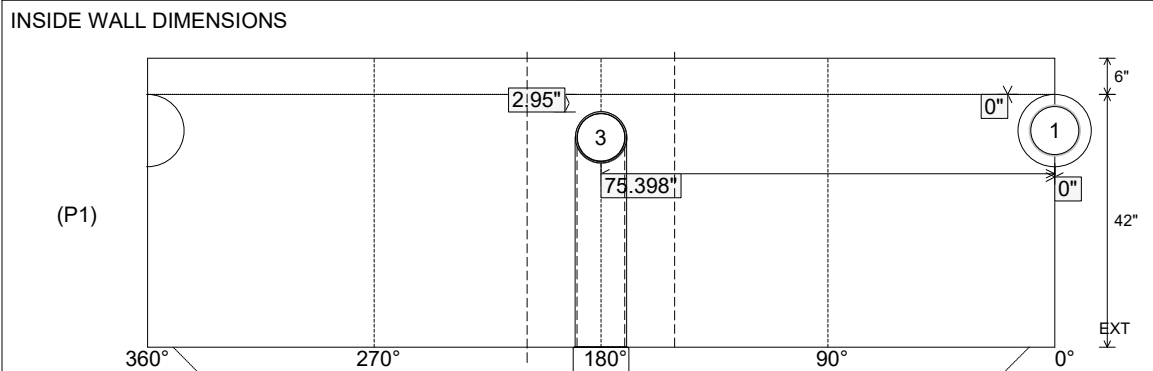

(P1)

360° 270° 180° 90° 0°

2.95" 75.398" 0" 42" 6" EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 42" Height (Ext): 48"	Weight (Net): 4192 lb Volume (Net): 1.07cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1 Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.				Plant: Beaver Dam 8/24/2026 8:08:24 AM		Tech: J. ROSS PC: E. BRADLEY						
Structure ID: A2 SS-MHD												
P1 MH048BA42CDARED				MH BASE w/DROP/ConBlock-CDA Red								
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red - 3" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 36" P2) 48" - MH RISER w/DROP/ConBlock-CDA Red - 72" P1) 48" - MH BASE w/DROP/ConBlock-CDA Red - 42" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) Drop Tee - 8" PVC 1) Drop Elbow - 8" PVC 12) MH Step ML-10-TDS-NCR - 10"						0 lb 202 lb 2251 lb 5006 lb 4192 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 8 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 4. CASTING BY OTHERS 5. ADMIXTURE = CONBLOCK-CDA RED				
Rim: 931.36' Rim to Invert: 13.2' Slack: 0.4" Sump: 2'						Structure Total: 13358 lb Step Position: 0'						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	918.16'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"		
Invert 2												
Invert 3	918.26'	180°	91.106"	8" PVC SDR35	8.5"	Drop Elbow 8" PVC	8.5"	8.545"	2.95"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 42" Height (Ext): 48"	Weight (Net): 4192 lb Volume (Net): 1.07cu.yd
----------------------------------	---------------------------------	--	--	--
