



Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1 Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.	Plant: Beaver Dam 8/24/2026 8:16:56 AM	Tech: J. ROSS PC: E. BRADLEY	
Structure ID: B2 SS-MHD			
P3 MH048RS60SCDARED		MH RISER w/DROP/ConBlock-CDA Red	

P5) 24" - CASTING HEIGHT - 7"	0 lb
P4) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 36"	2251 lb
P3) 48" - MH RISER w/DROP/ConBlock-CDA Red - 60"	4168 lb
P2) 48" - MH RISER w/DROP/ConBlock-CDA Red - 60"	4192 lb
P1) 48" - MH BASE w/DROP/ConBlock-CDA Red - 24"	2935 lb
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT	1440 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) CASTING - HOE MC-315 F/C Sanitary	258 lb
3) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) 24" - Conseal CS-102 1.00" (Double)	0 lb
1) PSX - 12M NYLO	8 lb
1) Drop Tee - 8" PVC	0 lb
1) Drop Elbow - 8" PVC	0 lb
15) MH Step ML-10-TDS-NCR - 10"	0 lb
	15251 lb
Rim: 933.98' Rim to Invert: 15.61' Slack: 2.32" Sump: 2'	Structure Total Step Position: 0


- Structure Notes:**
- PER ASTM C478 SPECIFICATIONS.
 - CONCRETE = 4,000 PSI AT 28 DAYS.
 - REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
 - CASTING BY OTHERS
 - ADMIXTURE = CONBLOCK-CDA RED

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2	928.51'	261°	132.104"	8" PVC SDR35	8.5"	Drop Tee 8" PVC	8.5"	8.545"	35.18"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

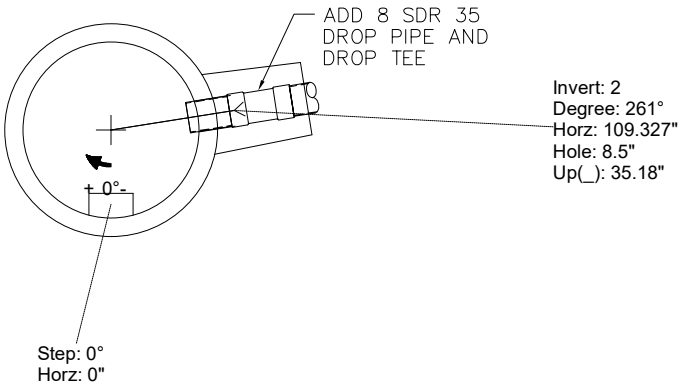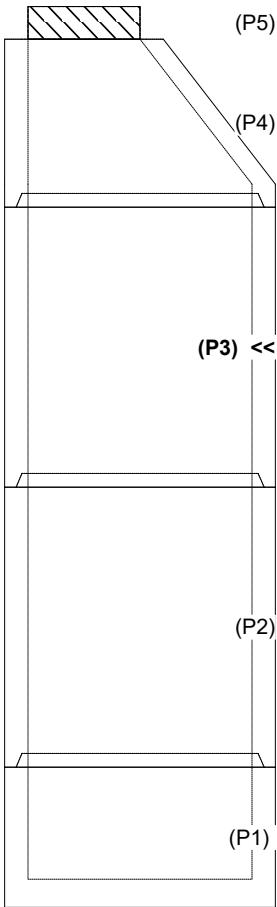

INSIDE WALL DIMENSIONS

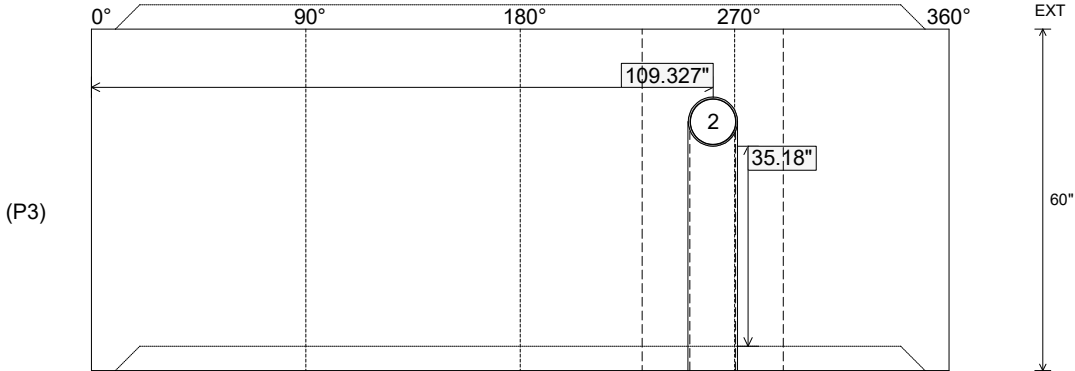

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 4168 lb Volume (Net): 1.06cu.yd
----------------------------------	------------------------------------	--	--	--
