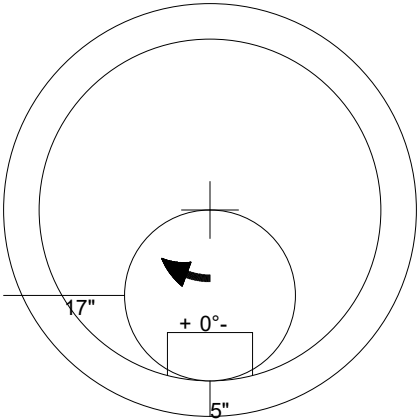



Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1 Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.		Plant: Beaver Dam 8/24/2026 8:12:31 AM	Tech: J. ROSS PC: E. BRADLEY	
Structure ID: B3 SS-MH				
P2 MH048CN36CDARED		ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 36" P1) 48" - MH BASE w/ConBlock-CDA Red - 30" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 5) MH Step ML-10-TDS-NCR - 10"		0 lb 2251 lb 3330 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 7295 lb	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 4. CASTING BY OTHERS 5. ADMIXTURE = CONBLOCK-CDA RED	
				
 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 36" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd
