


Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1 Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.					Plant: Beaver Dam 8/24/2026 8:16:58 AM		Tech: J. ROSS PC: E. BRADLEY				
Structure ID: B5 SS-MH											
P2 MH048RS48CDARED			MH RISER w/ConBlock-CDA Red								
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 36" P2) 48" - MH RISER w/ConBlock-CDA Red - 48" P1) 48" - MH BASE w/ConBlock-CDA Red - 30" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 9) MH Step ML-10-TDS-NCR - 10"					0 lb 2251 lb 3353 lb 3282 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 10609 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 4. CASTING BY OTHERS 5. ADMIXTURE = CONBLOCK-CDA RED				
Rim: 950.82' Rim to Invert: 10.08' Slack: 1.96" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

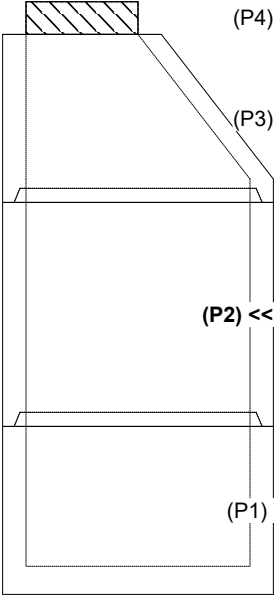


(P4)

(P3)

(P2) <<


(P1)

RIGHT-SIDE UP VIEW (int. dimensions)



Step: 0°
Horz: 0"

INSIDE WALL DIMENSIONS

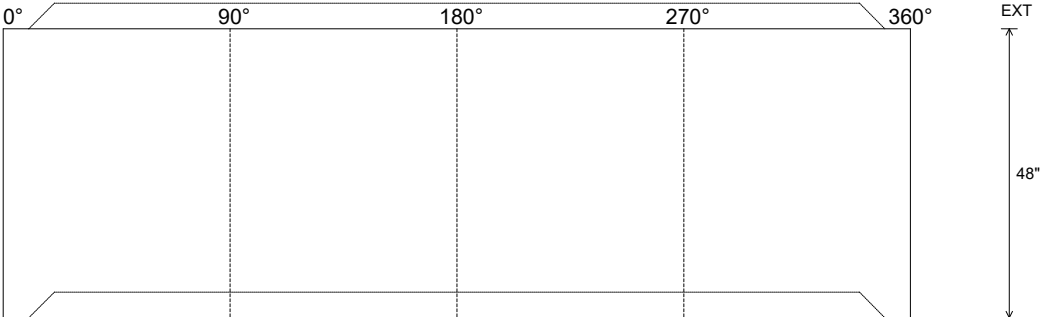

0° 90° 180° 270° 360°

(P2)

EXT 48"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3353 lb Volume (Net): 0.86cu.yd
----------------------------------	------------------------------------	--	--	--
