

Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1
Job Location: Nicholasville, KY
Contractor: The Allen Company, Inc.

Plant: Beaver Dam

Tech: J. ROSS

8/24/2026 8:12:39 AM

PC: E. BRADLEY



Structure ID: B7 SS-MH

P3 GR3CDARED

GRADE RING w/ConBlock-CDA Red

P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING w/ConBlock-CDA Red - 3"
P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 42"
P1) 48" - MH BASE w/ConBlock-CDA Red - 36"
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) CASTING - HOE MC-315 F/C Sanitary
1) 48" - Conseal CS-102 1.00" (Double)
2) 24" - Conseal CS-102 1.00" (Double)
3) PSX - 12-08 NYLO
7) MH Step ML-10-TDS-NCR - 10"

0 lb
202 lb
3116 lb
3701 lb
1440 lb
0 lb
0 lb
258 lb
0 lb
0 lb
24 lb
0 lb


Structure Total: 8742 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
4. CASTING BY OTHERS
5. ADMIXTURE = CONBLOCK-CDA RED

NOTES:


1. GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS
 - CONCRETE: 4,000 PSI @ 28 DAYS
 - REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)
2. WEIGHT: 3" 202 LBS.
3. ADMIXTURE: CONBLOCK-CDA RED

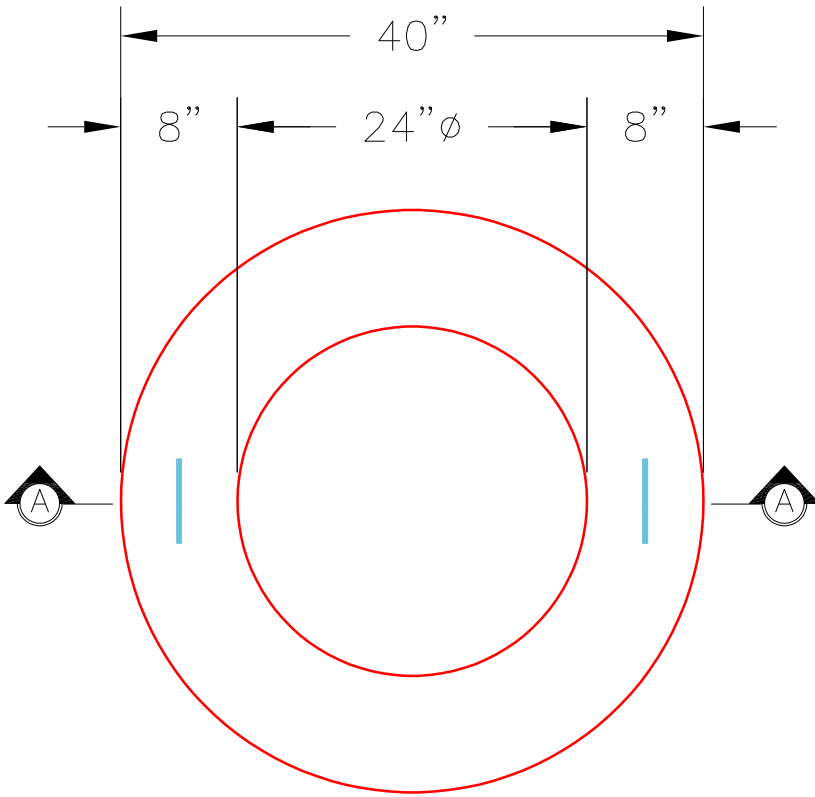

PLAN VIEW

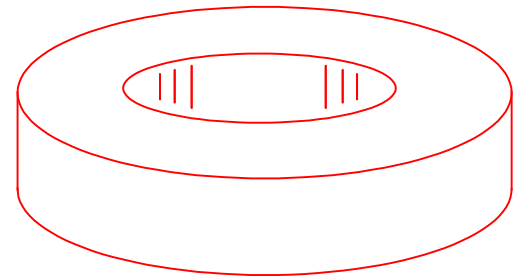

ISOMETRIC VIEW

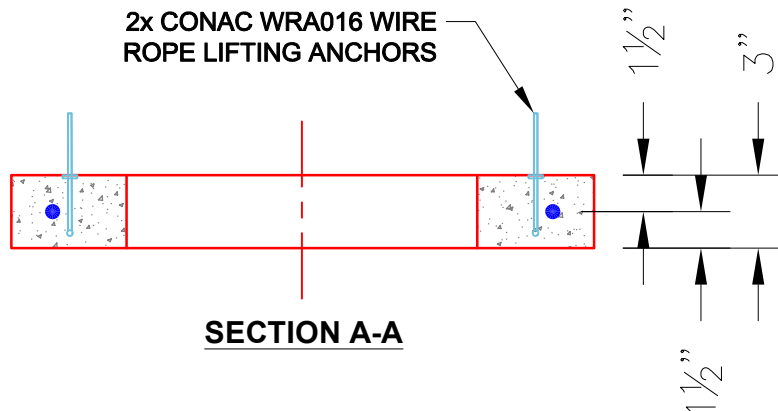

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 3"

Weight (Net): 202 lb
Volume (Net): 0.05cu.yd
