




Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1 Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.					Plant: Beaver Dam 8/24/2026 8:08:34 AM		Tech: J. ROSS PC: E. BRADLEY			
Structure ID: C2 SS-MH										
P1 MH048BA24CDARED			MH BASE w/ConBlock-CDA Red							
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 30" P2) 48" - MH RISER w/ConBlock-CDA Red - 72" P1) 48" - MH BASE w/ConBlock-CDA Red - 24" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 2) PSX - 12-06 NYLO 11) MH Step ML-10-TDS-NCR - 10"					0 lb 1961 lb 5030 lb 2815 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 16 lb 16 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 4. CASTING BY OTHERS 5. ADMIXTURE = CONBLOCK-CDA RED			
Rim: 959.04' Rim to Invert: 11.04' Slack: 1.48" Sump: 2" Step Position: 0°					Structure Total: 11537 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	948'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	948.1'	90°	45.553"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3	948.1'	200°	101.229"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0.2"	0"
Invert 4	948.1'	270°	136.659"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0.2"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

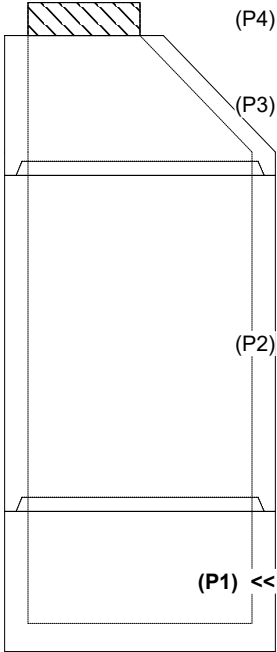


RIGHT-SIDE UP VIEW (int. dimensions)

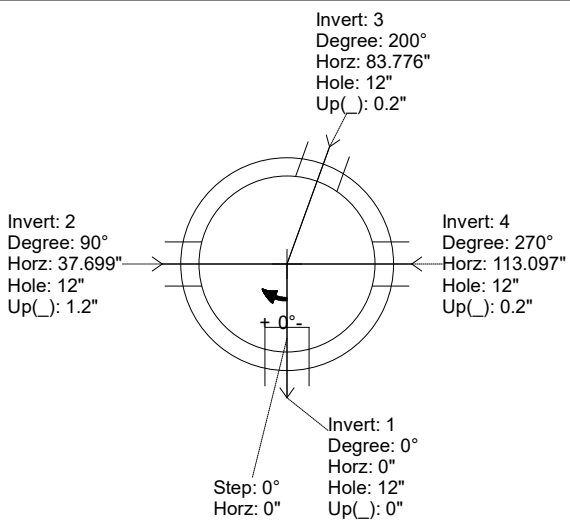

UPSIDE-DOWN VIEW (int. dimensions)

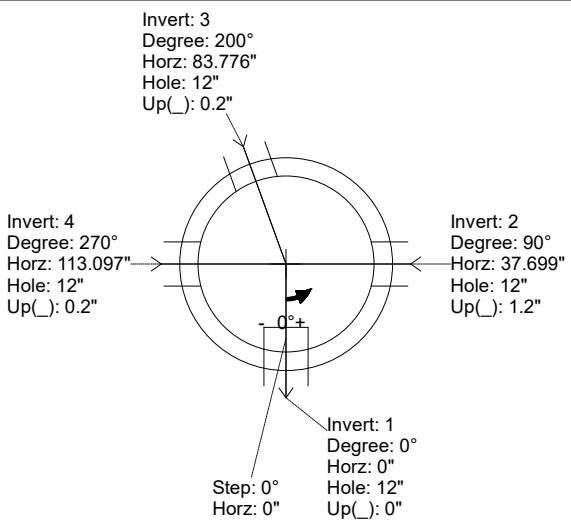

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2815 lb Volume (Net): 0.72cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1

Job Location: Nicholasville, KY

Contractor: The Allen Company, Inc.

Plant: Beaver Dam

8/24/2026 8:08:34 AM

Tech: J. ROSS

PC: E. BRADLEY

Structure ID: C2 SS-MH

P1 MH048BA24CDARED

MH BASE w/ConBlock-CDA Red

P4) 24" - CASTING HEIGHT - 7"

P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 30"

P2) 48" - MH RISER w/ConBlock-CDA Red - 72"

P1) 48" - MH BASE w/ConBlock-CDA Red - 24"

1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) CASTING - HOE MC-315 F/C Sanitary

2) 48" - Conseal CS-102 1.00" (Double)

1) 24" - Conseal CS-102 1.00" (Double)

2) PSX - 12-08 NYLO

2) PSX - 12-06 NYLO

11) MH Step ML-10-TDS-NCR - 10"

0 lb

1961 lb

5030 lb

2815 lb

1440 lb

0 lb

0 lb

258 lb

0 lb

0 lb

16 lb

16 lb

0 lb

Structure Total: 11537 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

4. CASTING BY OTHERS

5. ADMIXTURE = CONBLOCK-CDA RED

Rim: 959.04'

Rim to Invert: 11.04'

Slack: 1.48"

Sump: 2"

Step Position: 0°

INVERT CHANNEL DRAWING

FULL HEIGHT INVERT

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	948'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	948.1'	90°	45.553"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3	948.1'	200°	101.229"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0.2"	0"
Invert 4	948.1'	270°	136.659"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0.2"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 5"

Floor Height: 6"

Height (Int): 24"

Height (Ext): 30"

Weight (Net): 2815 lb

Volume (Net): 0.72cu.yd
