

Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1

Job Location: Nicholasville, KY

Contractor: The Allen Company, Inc.

Plant: Beaver Dam

8/24/2026 8:16:59 AM

Tech: J. ROSS

PC: E. BRADLEY



Structure ID: C2 SS-MH

P2 MH048RS72CDARED


MH RISER w/ConBlock-CDA Red

P4) 24" - CASTING HEIGHT - 7"	0 lb	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 4. CASTING BY OTHERS 5. ADMIXTURE = CONBLOCK-CDA RED
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 30"	1961 lb	
P2) 48" - MH RISER w/ConBlock-CDA Red - 72"	5030 lb	
P1) 48" - MH BASE w/ConBlock-CDA Red - 24"	2815 lb	
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT	1440 lb	
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb	
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb	
1) CASTING - HOE MC-315 F/C Sanitary	258 lb	
2) 48" - Conseal CS-102 1.00" (Double)	0 lb	
1) 24" - Conseal CS-102 1.00" (Double)	0 lb	
2) PSX - 12-08 NYLO	16 lb	
2) PSX - 12-06 NYLO	16 lb	
11) MH Step ML-10-TDS-NCR - 10"	0 lb	


	Structure Total:	
		11537 lb

Rim: 959.04' Rim to Invert: 11.04' Slack: 1.48" Sump: 2" Step Position: 0°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

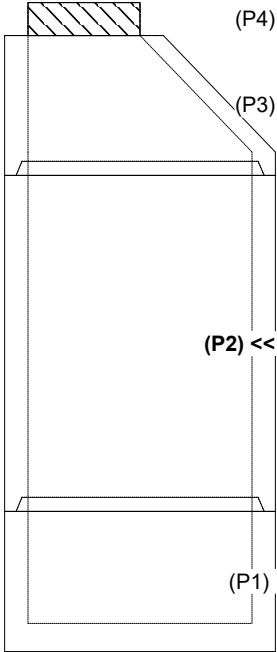

RIGHT-SIDE UP VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

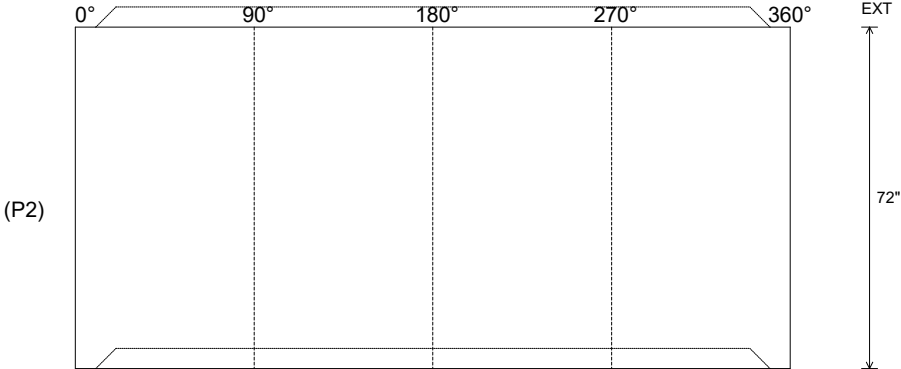

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 5"
Floor Height: 0"

Height (Int): 72"
Height (Ext): 72"

Weight (Net): 5030 lb
Volume (Net): 1.28cu.yd
