




Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1 Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.					Plant: Beaver Dam 8/24/2026 8:08:42 AM		Tech: J. ROSS PC: E. BRADLEY					
Structure ID: E6 SS-MH												
P1 MH048BA24CDARED			MH BASE w/ConBlock-CDA Red									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 30" P1) 48" - MH BASE w/ConBlock-CDA Red - 24" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 5) MH Step ML-10-TDS-NCR - 10"						0 lb 1961 lb 2911 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 6586 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 4. CASTING BY OTHERS 5. ADMIXTURE = CONBLOCK-CDA RED				
Rim: 941.24' Rim to Invert: 5.1' Slack: 2.2' Sump: 2' Step Position: 0°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	936.14'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"		
Invert 2	936.24'	180°	91.106"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

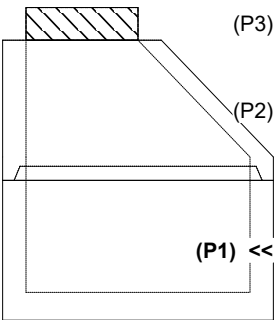


RIGHT-SIDE UP VIEW (int. dimensions)

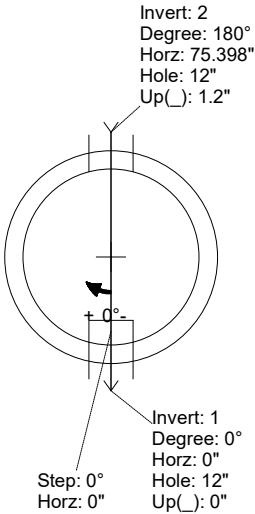

UPSIDE-DOWN VIEW (int. dimensions)

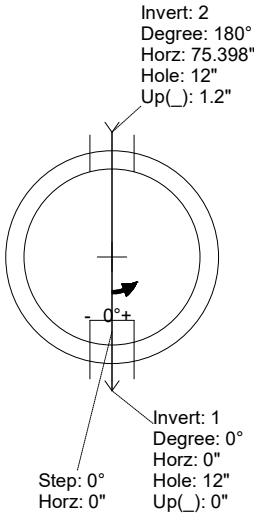


INSIDE WALL DIMENSIONS




Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2911 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--


Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1 Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.					Plant: Beaver Dam 8/24/2026 8:08:42 AM		Tech: J. ROSS PC: E. BRADLEY				
Structure ID: E6 SS-MH											
P1 MH048BA24CDARED			MH BASE w/ConBlock-CDA Red								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 30" P1) 48" - MH BASE w/ConBlock-CDA Red - 24" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 5) MH Step ML-10-TDS-NCR - 10"						0 lb 1961 lb 2911 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 6586 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 4. CASTING BY OTHERS 5. ADMIXTURE = CONBLOCK-CDA RED			
Rim: 941.24' Rim to Invert: 5.1' Slack: 2.2' Sump: 2' Step Position: 0°						INVERT CHANNEL DRAWING FULL HEIGHT INVERT					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	936.14'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	936.24'	180°	91.106"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

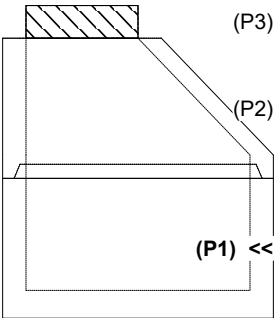


RIGHT-SIDE UP VIEW (int. dimensions)

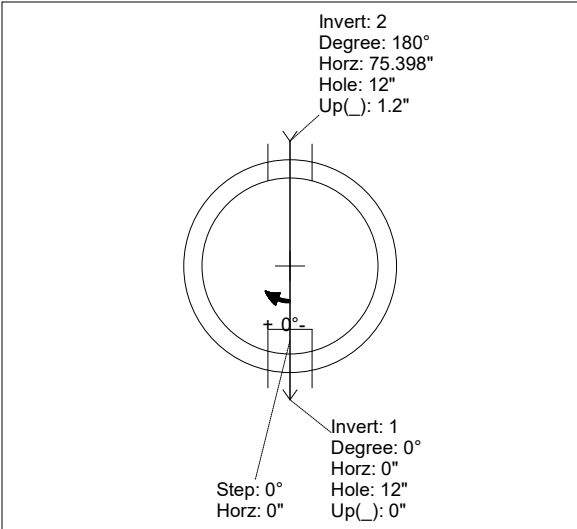

UPSIDE-DOWN VIEW (int. dimensions)

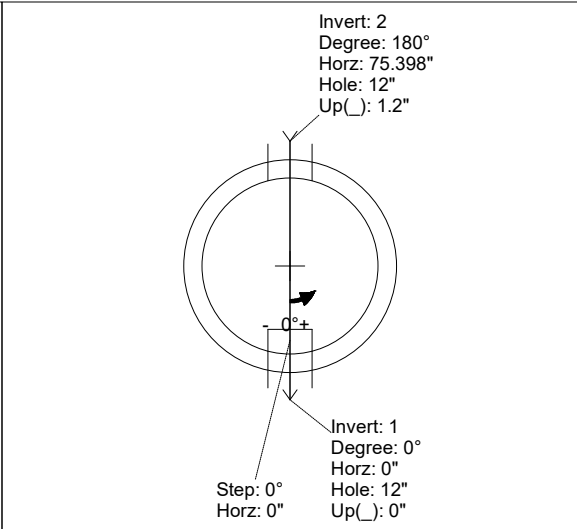

INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 24"
Height (Ext): 30"

Weight (Net): 2911 lb
Volume (Net): 0.74cu.yd
