



Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1 Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.					Plant: Beaver Dam 8/24/2026 8:17:08 AM		Tech: J. ROSS PC: E. BRADLEY				
Structure ID: I2 SS-MHD											
P2		MH048RS72SCDARED		MH RISER w/DROP/ConBlock-CDA Red							
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red - 3" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 42" P2) 48" - MH RISER w/DROP/ConBlock-CDA Red - 72" P1) 48" - MH BASE w/DROP/ConBlock-CDA Red - 36" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) Drop Tee - 8" PVC 1) Drop Elbow - 8" PVC 13) MH Step ML-10-TDS-NCR - 10"					0 lb 202 lb 3116 lb 5006 lb 3773 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 8 lb 0 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 4. CASTING BY OTHERS 5. ADMIXTURE = CONBLOCK-CDA RED				
Rim: 956.09' Rim to Invert: 13.22' Slack: 0.64" Sump: 2'					Structure Total: 13804 lb Step Position: 0						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2	950.16'	171°	86.551"	8" PVC SDR35	8.5"	Drop Tee 8" PVC	8.5"	8.545"	48.98"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

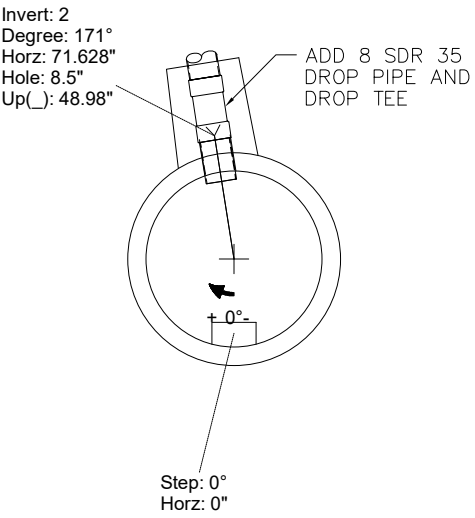

INSIDE WALL DIMENSIONS

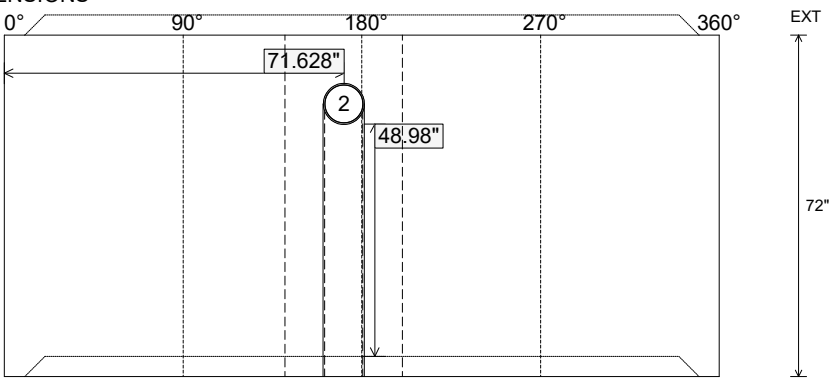

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 72" Height (Ext): 72"	Weight (Net): 5006 lb Volume (Net): 1.28cu.yd
----------------------------------	------------------------------------	--	--	--
