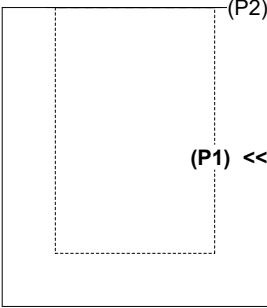
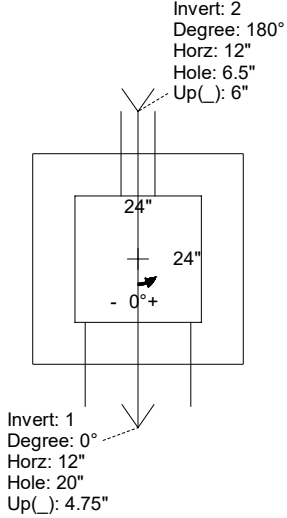
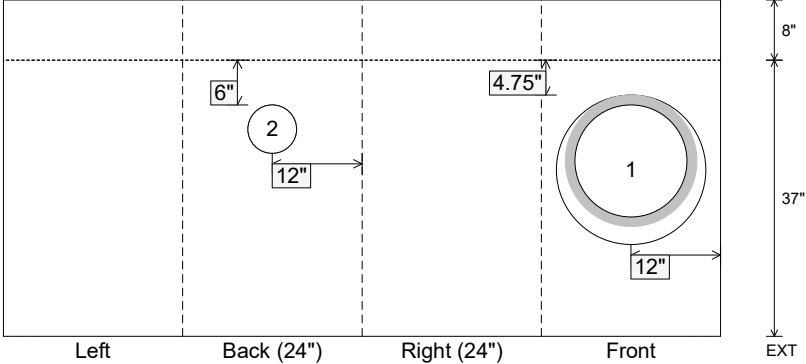


Job Name: 26-2564 - Taubensee Steel Job Location: Henderson, KY Contractor: K&K Excavating Inc.					Plant: 100 6/24/2026 6:15:15 AM		Tech: J. Horsley PC: T. Lewis				
Structure ID: 302 ST-OCS											
P1 BX2424-08BAVF			BOX BASE 8inW, 8inF, Variable Ht F/n								
P2) 24" x 24" - CASTING HEIGHT - 0" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 37" 1) CASTING - TRASHRACKS LFS-2424-P SQ. Flush Mount Grate 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 6.5						0 lb 4020 lb 59 lb 0 lb 0 lb 0 lb Structure Total: 4079 lb		Structure Notes: 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 4,500 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. TRASHRACKS LFS-2424 SQUARE FLUSH MOUNT GRATE SUPPLIED BY ICAST			
Rim: 384.1' Rim to Invert: 2.6' Slack: 0.2" Sump: 6" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	381.5'	0°	20"	15" HDPE	17.6"	Hole 20	20"	20"	4.75"	0"	
Invert 2	381.5'	180°	20"	6.5" Orifice	6.5"	Hole 6.5	6.5"	6.5"	6"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions)   INSIDE WALL DIMENSIONS  Coating (Int): Coating (Ext): Seam Up: Flat Seam Dn: n/a Wall Thickness: 8" Floor Height: 8" Height (Int): 37" Height (Ext): 45" Weight (Net): 4020 lb Volume (Net): 1.03cu.yd											
