



Job Name: 26-2564 - Taubensee Steel Job Location: Henderson, KY Contractor: K&K Excavating Inc.				Plant: 100 6/24/2026 6:15:16 AM		Tech: J. Horsley PC: T. Lewis				
Structure ID: 402 ST-AD										
P1 BX2424-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n						
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 29" 1) CASTING - HOE-326-BH F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 24				0 lb 3338 lb 289 lb 0 lb 0 lb ----- Structure Total: 3627 lb		Structure Notes: 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 4,500 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE-326-BH FRAME & BEEHIVE GRATE SUPPLIED BY ICAST				
Rim: 385.7' Rim to Invert: 2.67' Slack: 0.64" Sump: 1.6" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	383.03'	0°	20"	18" HDPE	21.2"	Hole 24	24"	24"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

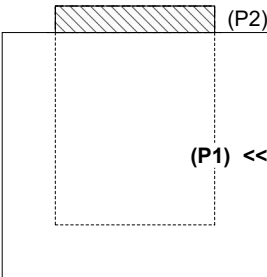


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)



INSIDE WALL DIMENSIONS

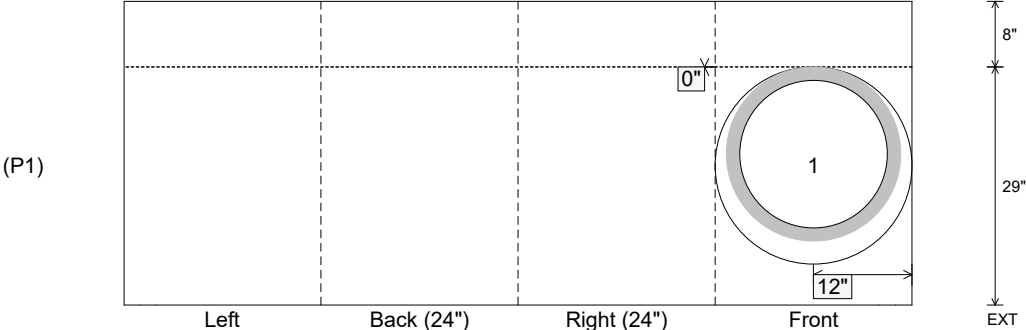

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 29"
Height (Ext): 37"

Weight (Net): 3338 lb
Volume (Net): 0.85cu.yd
