



Job Name: 26-2582 - 739729 Teal Drive Job Location: Nashville, TN Contractor: Contech Engineering Solutions					Plant: Beaver Dam 6/16/2026 1:01:56 PM		Tech: J. Coppage PC: T. Sekula				
Structure ID: 10-CS-8											
P3		MH096RS72		MH RISER T/G							
P5) 24" - CASTING HEIGHT - 4" P4) 96" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 17" P3) 96" - MH RISER T/G - 72" P2) 96" - MH RISER T/G - 36" P1) 96" - MH MONOBASE 13F, Custom Ht T/n - 24" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 3) 96" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 42					0 lb 10015 lb 15782 lb 8968 lb 17113 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 51879 lb Structure Total:		Structure Notes: SITE DESIGNATION: STM-C2 (4" TALL CASTING PROVIDED BY OTHERS) CONTROL RISER TO BE MECHANICALLY ATTACHED TO THE BOTTOM OF THE 72" TALL RISER. ICAST TO INSTALL THE INTERNALS CONTECH'S LOGO AS WELL AS THE INLET AND THE OUTLET MUST BE STENBCILED ONTO THE STRUCTURE				
Rim: 471.23'		Rim to Invert: 6.47'		Slack: 7.64"		Sump: 83"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	464.76'	270°	268.606"	30" RCP B WALL	37"	Hole 42	42"	43.47"	12"	0"	
Invert 2	464.76'	128°	127.339"	30" RCP B WALL	37"	Hole 42	42"	43.47"	12"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

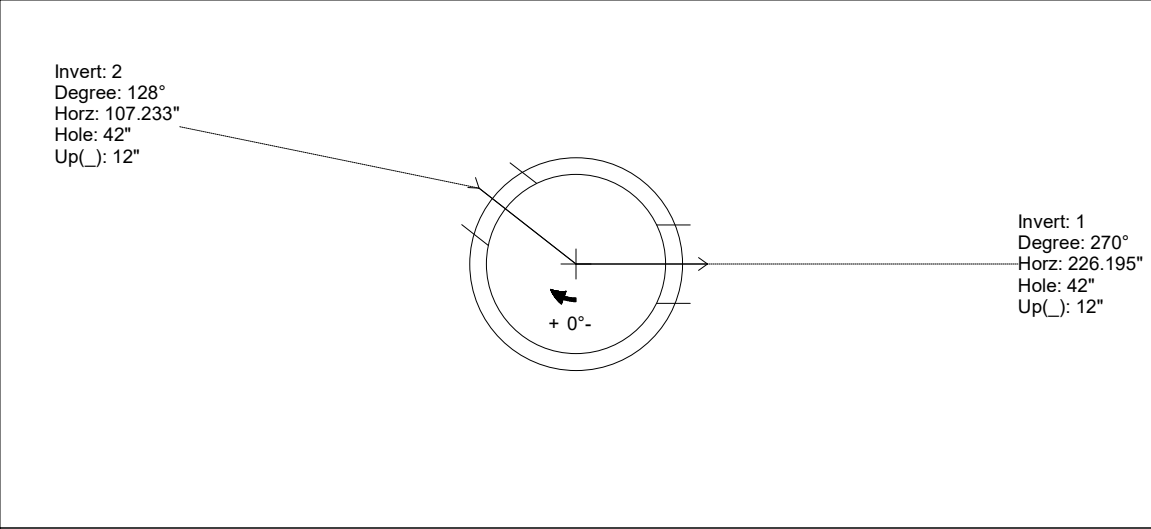

INSIDE WALL DIMENSIONS

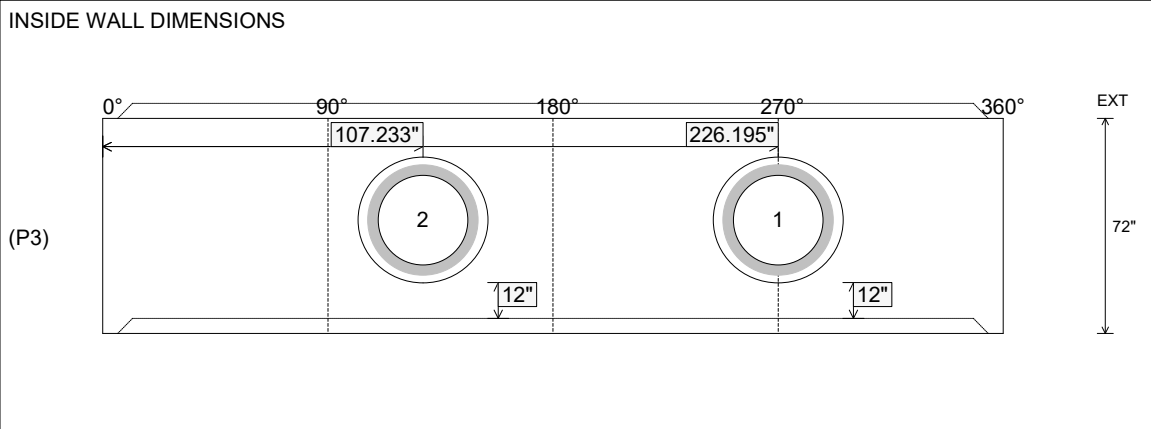

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 9" Floor Height: 0"	Height (Int): 72" Height (Ext): 72"	Weight (Net): 15782 lb Volume (Net): 4.03cu.yd
----------------------------------	------------------------------------	--	--	---
