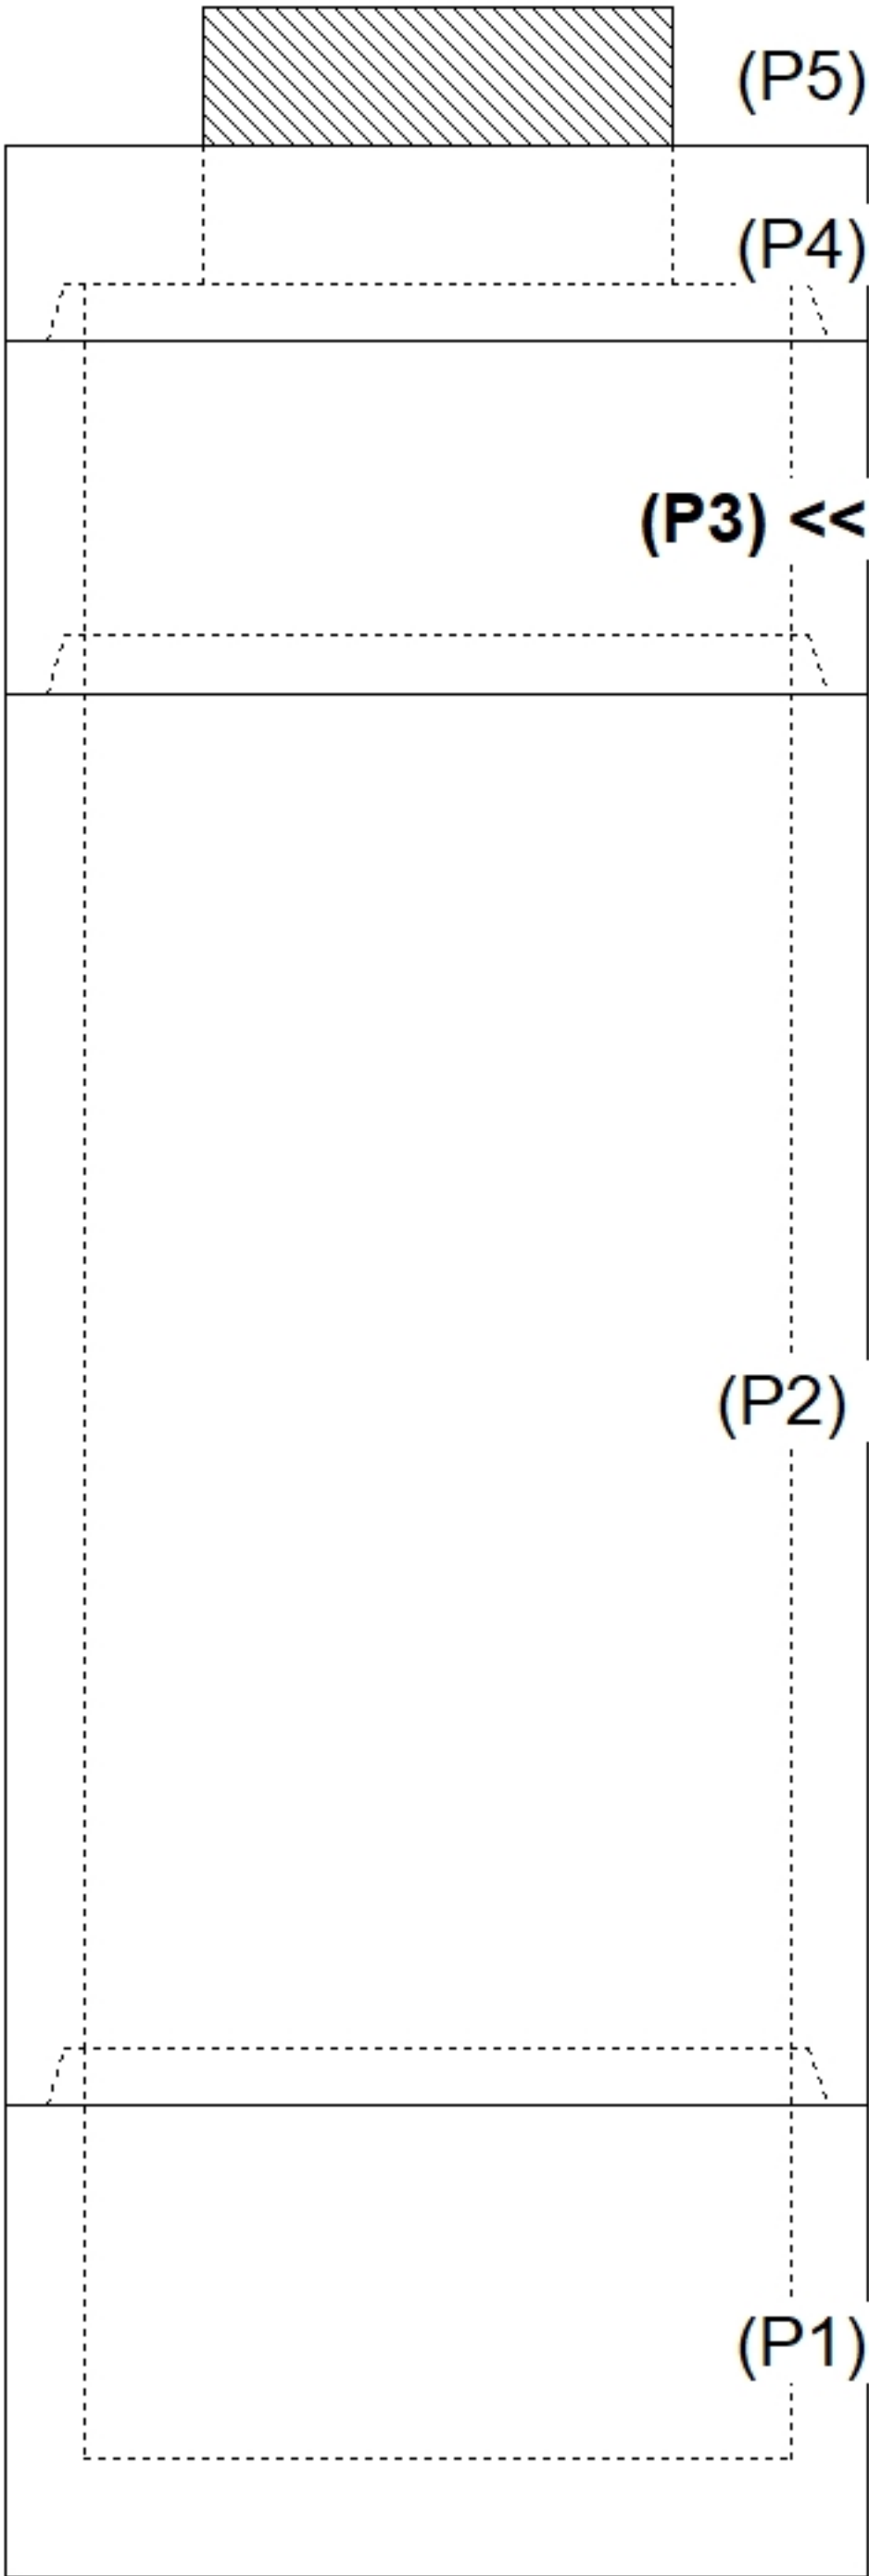
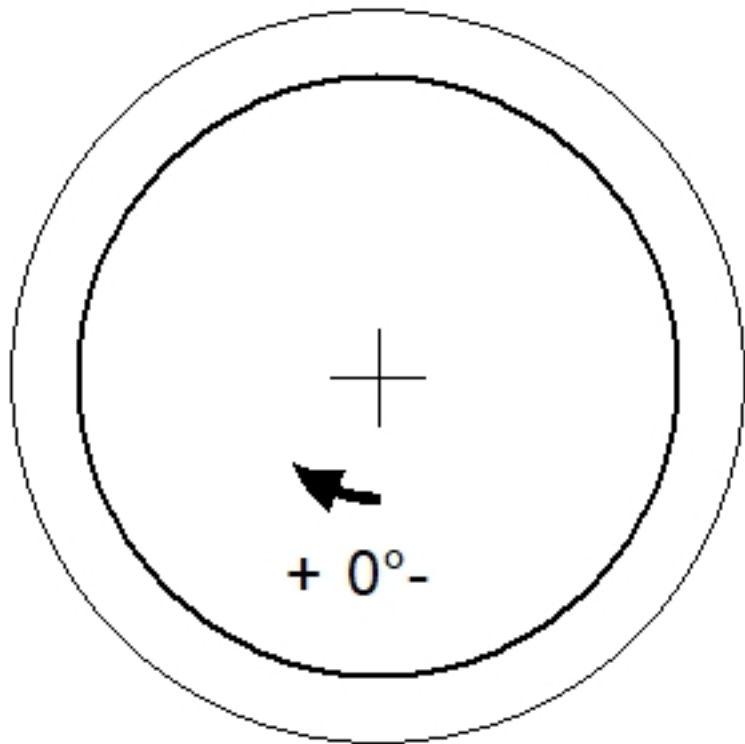
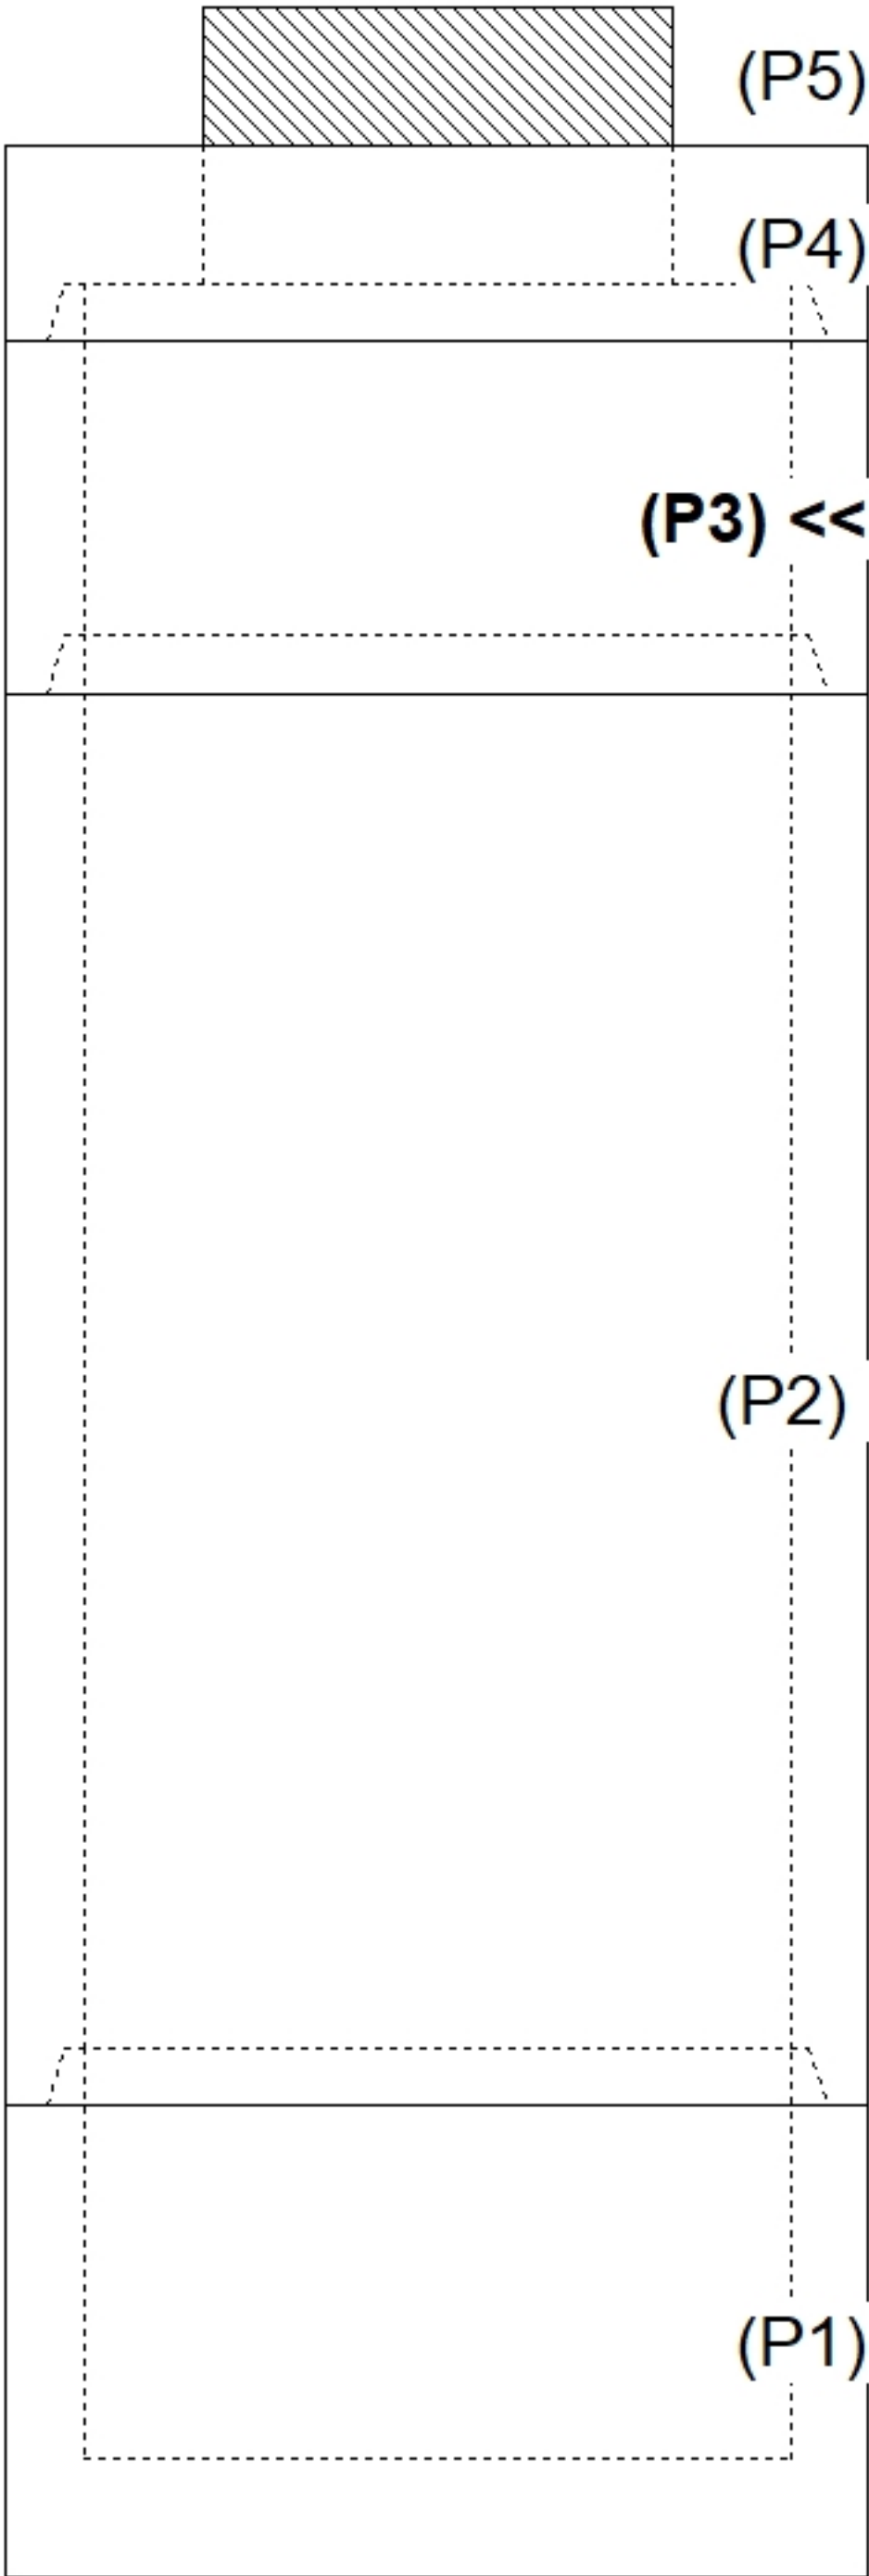
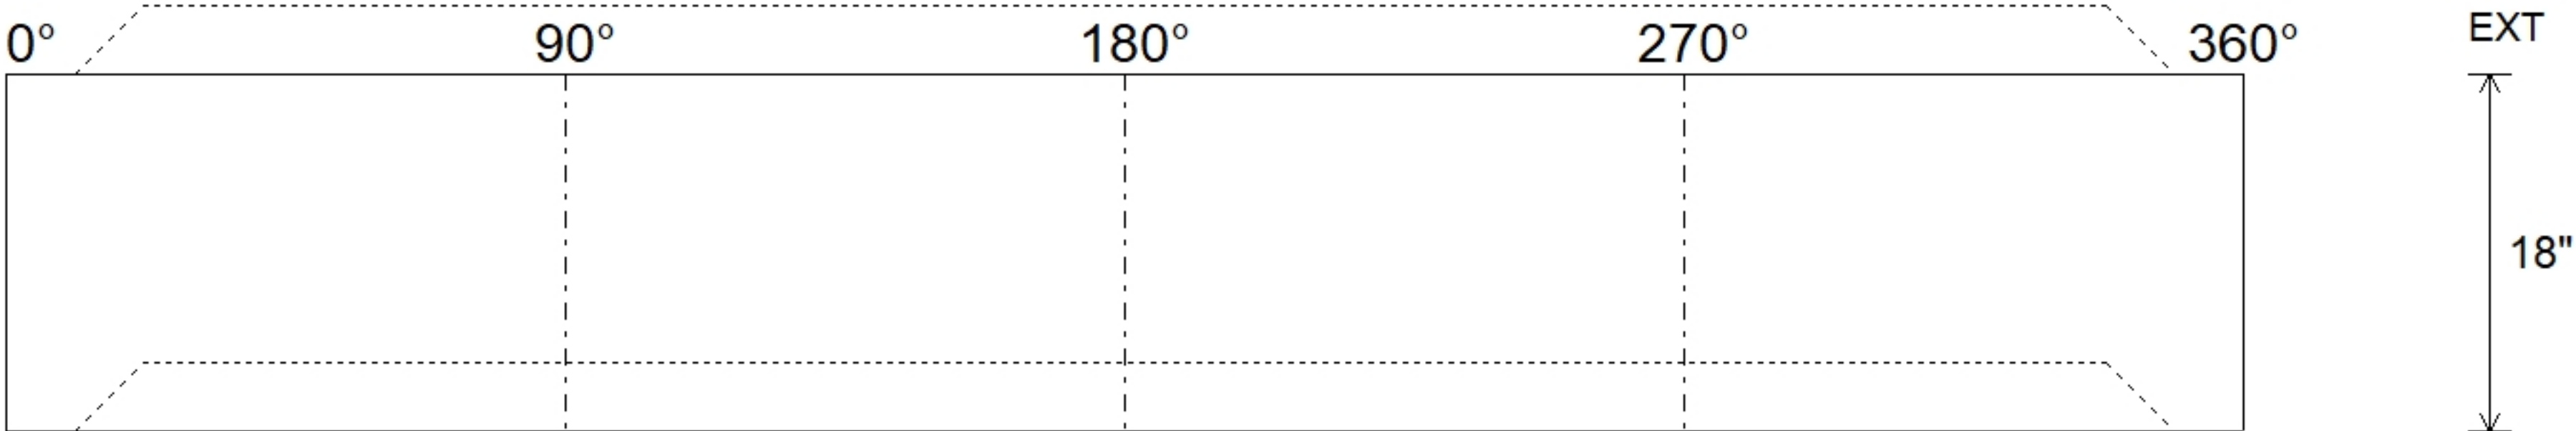


Job Name: 26-2604 ADS Abound Credit Union Job Location: Louisville, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 7/7/2026 8:30:45 AM		Tech: S. Felletter PC: T. Ryan						
Structure ID: AR3PC													
P3			MH036RS18			MH RISER T/G							
P5) 24" - CASTING HEIGHT - 7" P4) 36" - MH FLAT TOP w/ 24" Ctr. Hole F/G - 10" P3) 36" - MH RISER T/G - 18" P2) 36" - MH RISER T/G - 72" P1) 36" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Storm 3) 36" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) Hole - 12						0 lb 896 lb 759 lb 2937 lb 1525 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb ----- 6388 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 742.78' Rim to Invert: 5.92' Slack: 1" Sump: 54.96" Step Position:													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 4" Floor Height: 0"		Height (Int): 18" Height (Ext): 18"		Weight (Net): 759 lb Volume (Net): 0.19cu.yd			
