


Contractor: McCain Bros Excavating LLC

Plant: Beaver Dam



Slack: 0.6"


Structure Total: 20109 lb

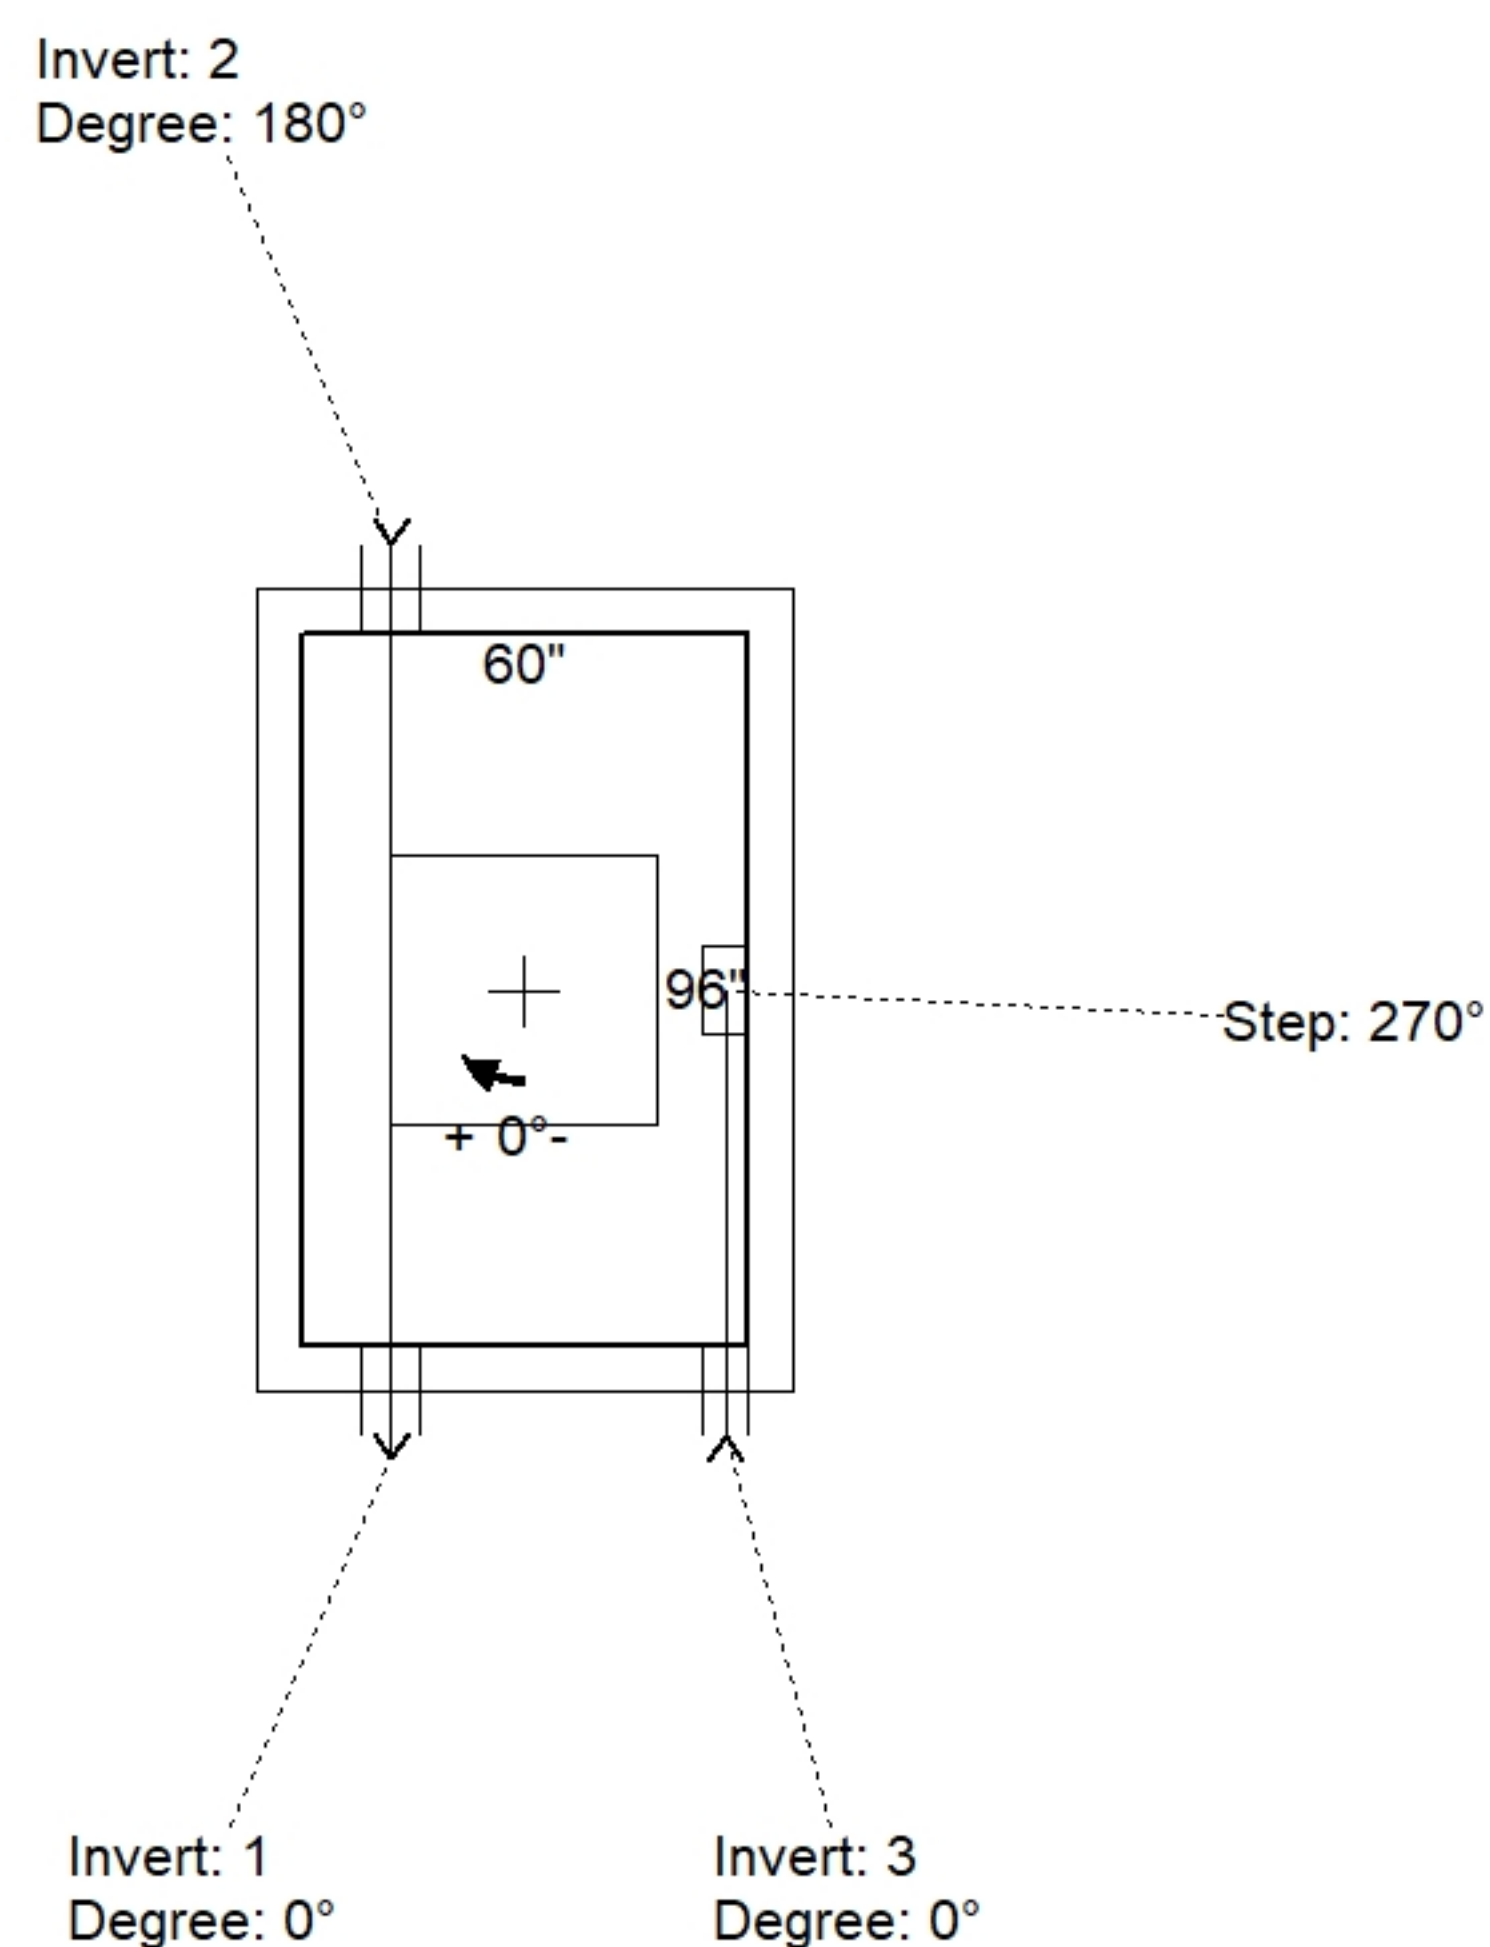

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	6.5'							
Reducer								
Invert 1	1.833'	0°	4" DI	4.75"	8"	Hole 8	20.6"	P1
Invert 2	1.833'	180°	4" DI	4.75"	8"	Hole 8	20.6"	P1
Invert 3	0.033'	0°	4" HDPE	4.8"	6"	Hole 6	0"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

60" x 96" - BOX BASE 6inW, 6inF, Variable Ht F/n - 70" - (P1)

Default - Interior Dimensions

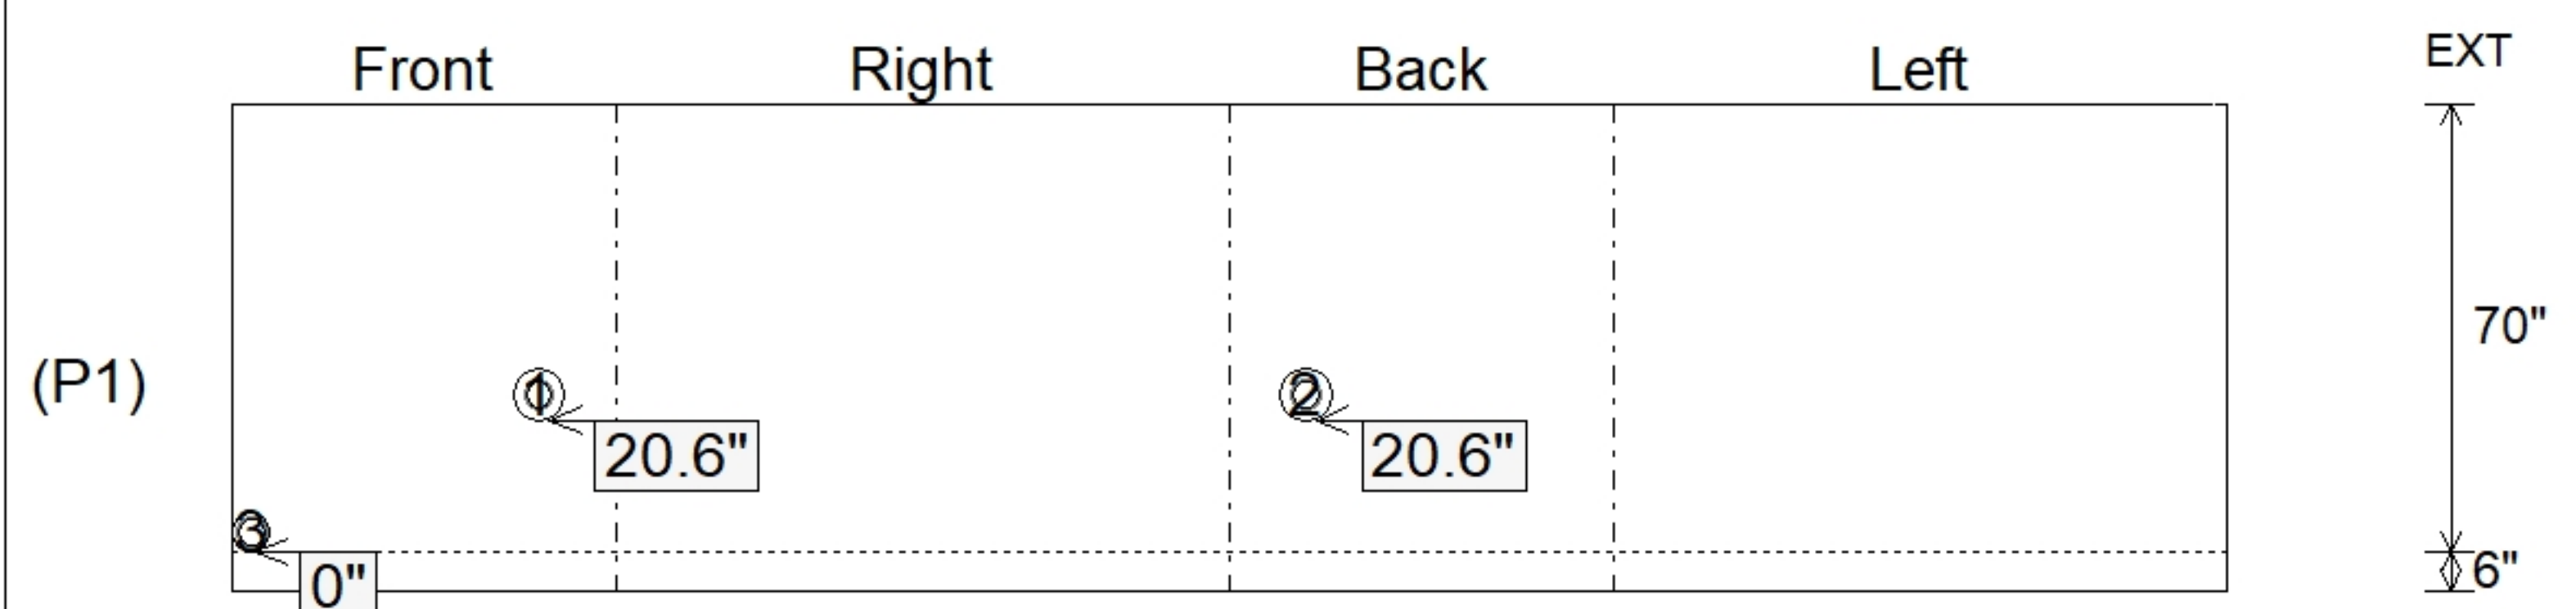

SUBMITTAL
APPROVED BY:
