

Job Name: 26-2642 - Daviess County Detention Center
Job Location: Owensboro, KY
Contractor: Winwater Hartford KY Co.

Plant: Beaver Dam

10/13/2026 2:58:19 PM

Tech: J. Coppinge

PC: A. Chambers



Structure ID: AMH2 SS-MH

P2 MH048RS48SCDARED

MH RISER w/DROP/ConBlock-CDA Red

- P4) 24" - CASTING HEIGHT - 7"
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 36"
P2) 48" - MH RISER w/DROP/ConBlock-CDA Red - 48"
P1) 48" - MH BASE w/DROP/FLG Cust. Ht. w/ConBlock-CDA Red - 63"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
1) CASTING - HOE MC-315 F/C RWRA
2) 48" - Con seal CS-102 1.00" (Double)
1) 24" - Con seal CS-102 1.00" (Double)
3) PSX - 12-08 NYLO
1) Drop Tee - 8" PVC
1) Drop Elbow - 8" PVC
12) MH Step ML-10-TDS-NCR - 10"



- 0 lb
2251 lb
3353 lb
9619 lb
0 lb
0 lb
1440 lb
258 lb
0 lb
0 lb
24 lb
0 lb
0 lb
0 lb
- Structure Notes:**
1. JR HOE MC-315 SAN. PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. ADMIXTURE = CONBLOCK CDA RED.
5. REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 16945 lb

Rim: 400.22' Rim to Invert: 12.72' Slack: 0.64" Sump: 2" Step Position: 0°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

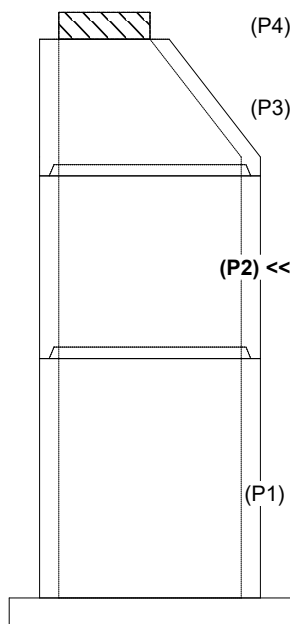

Step: 0°
Horz: 0°

INSIDE WALL DIMENSIONS

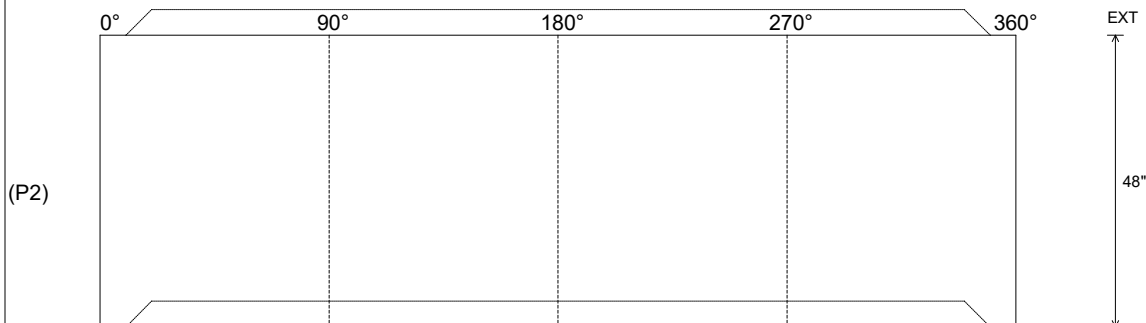

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 5"
Floor Height: 0"

Height (Int): 48"
Height (Ext): 48"

Weight (Net): 3353 lb
Volume (Net): 0.86cu.yd
