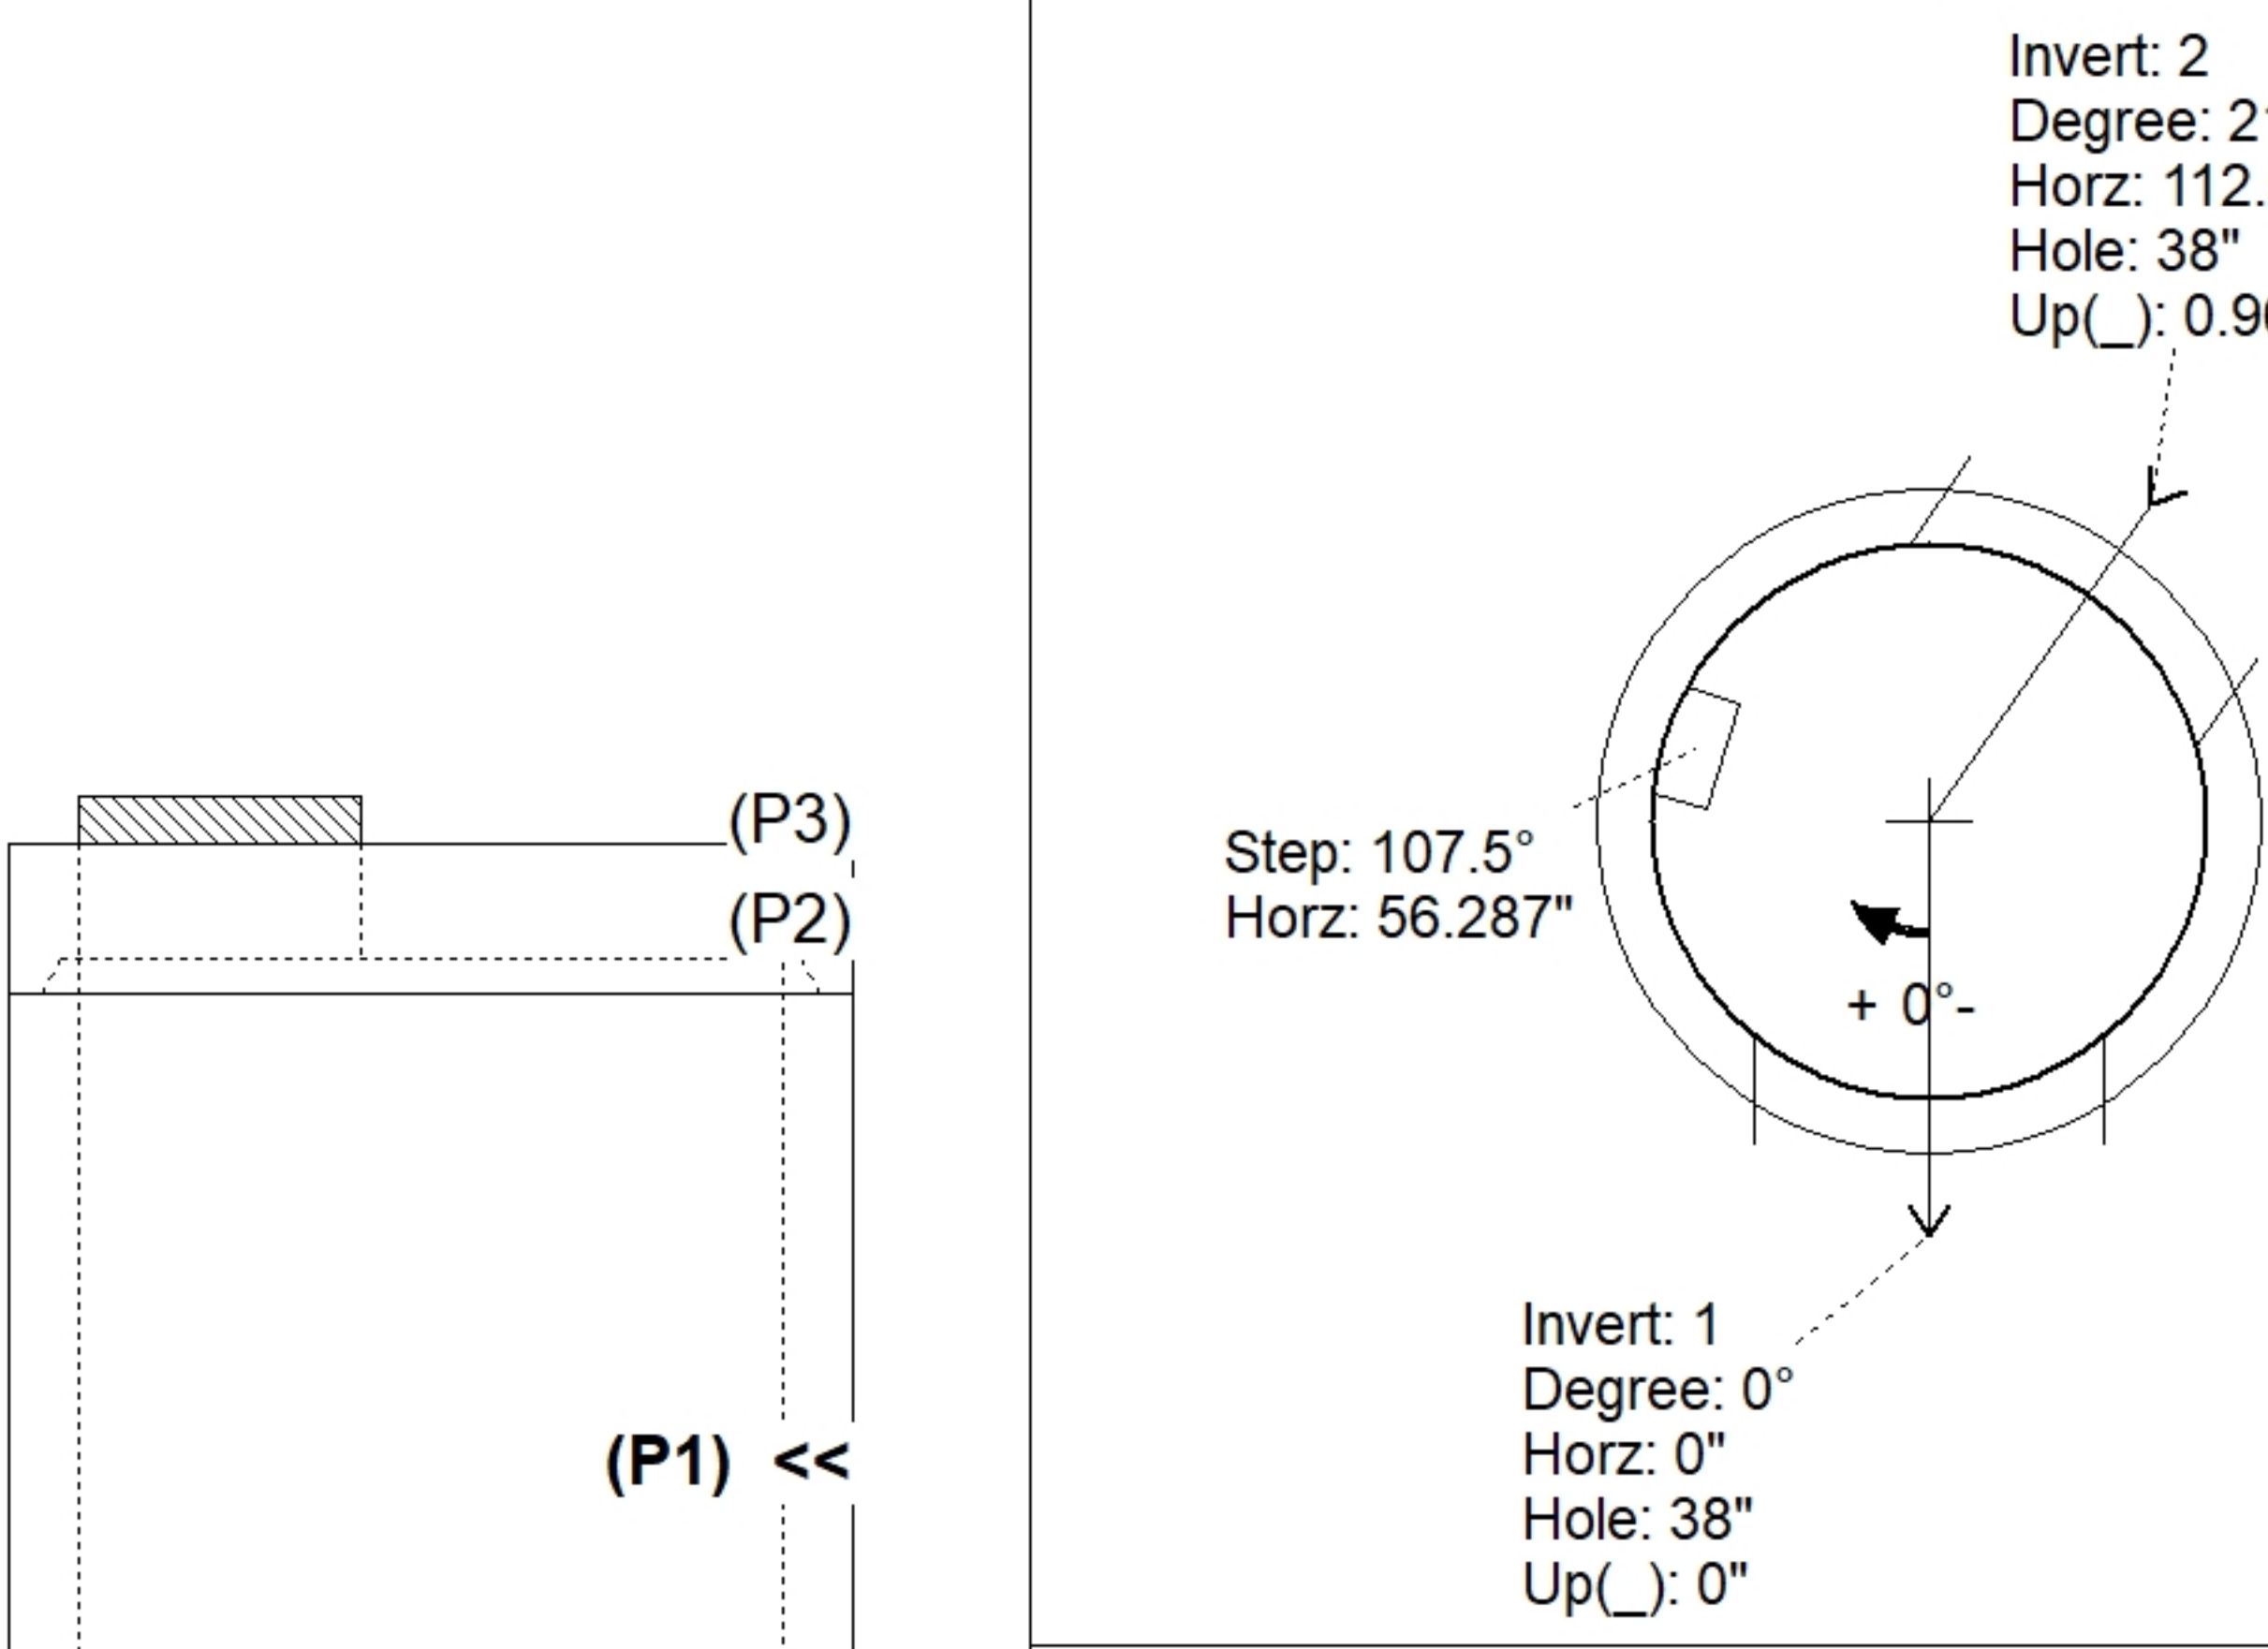
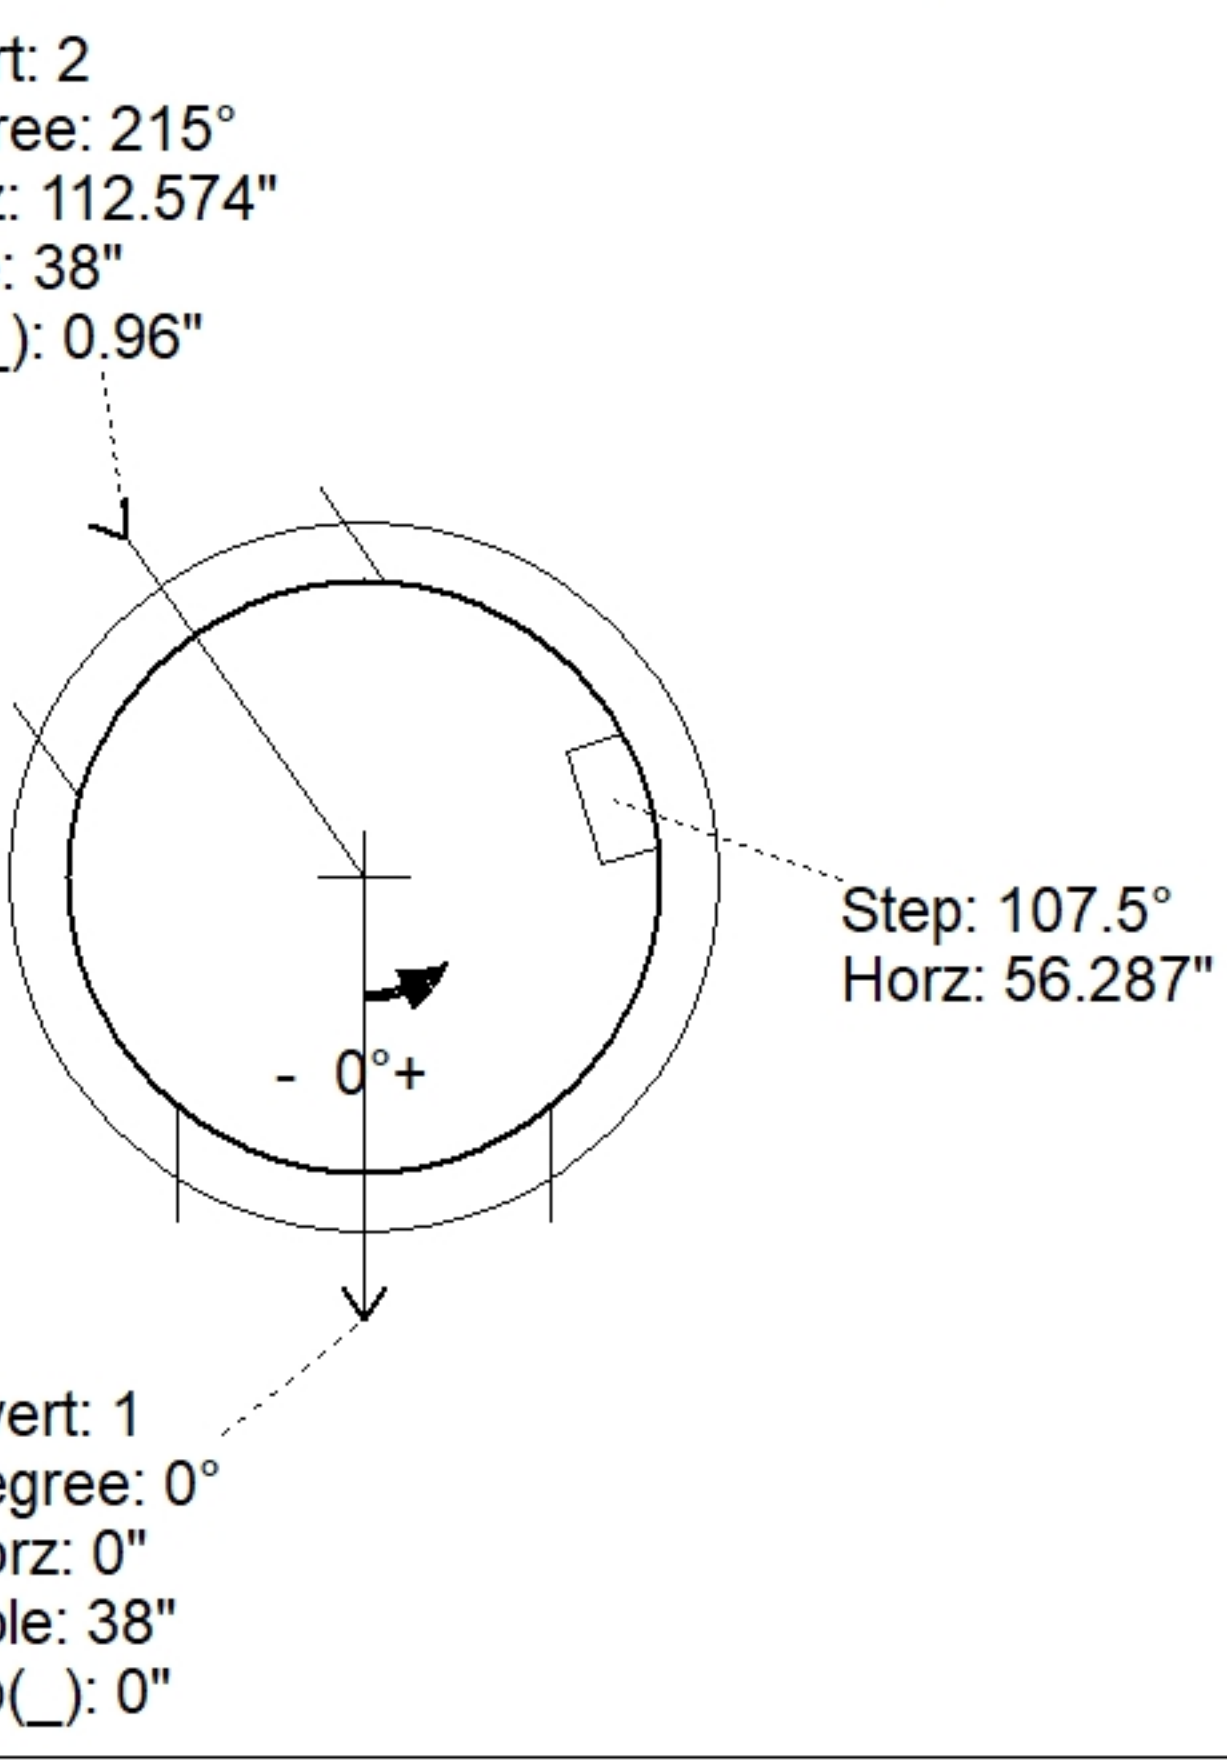
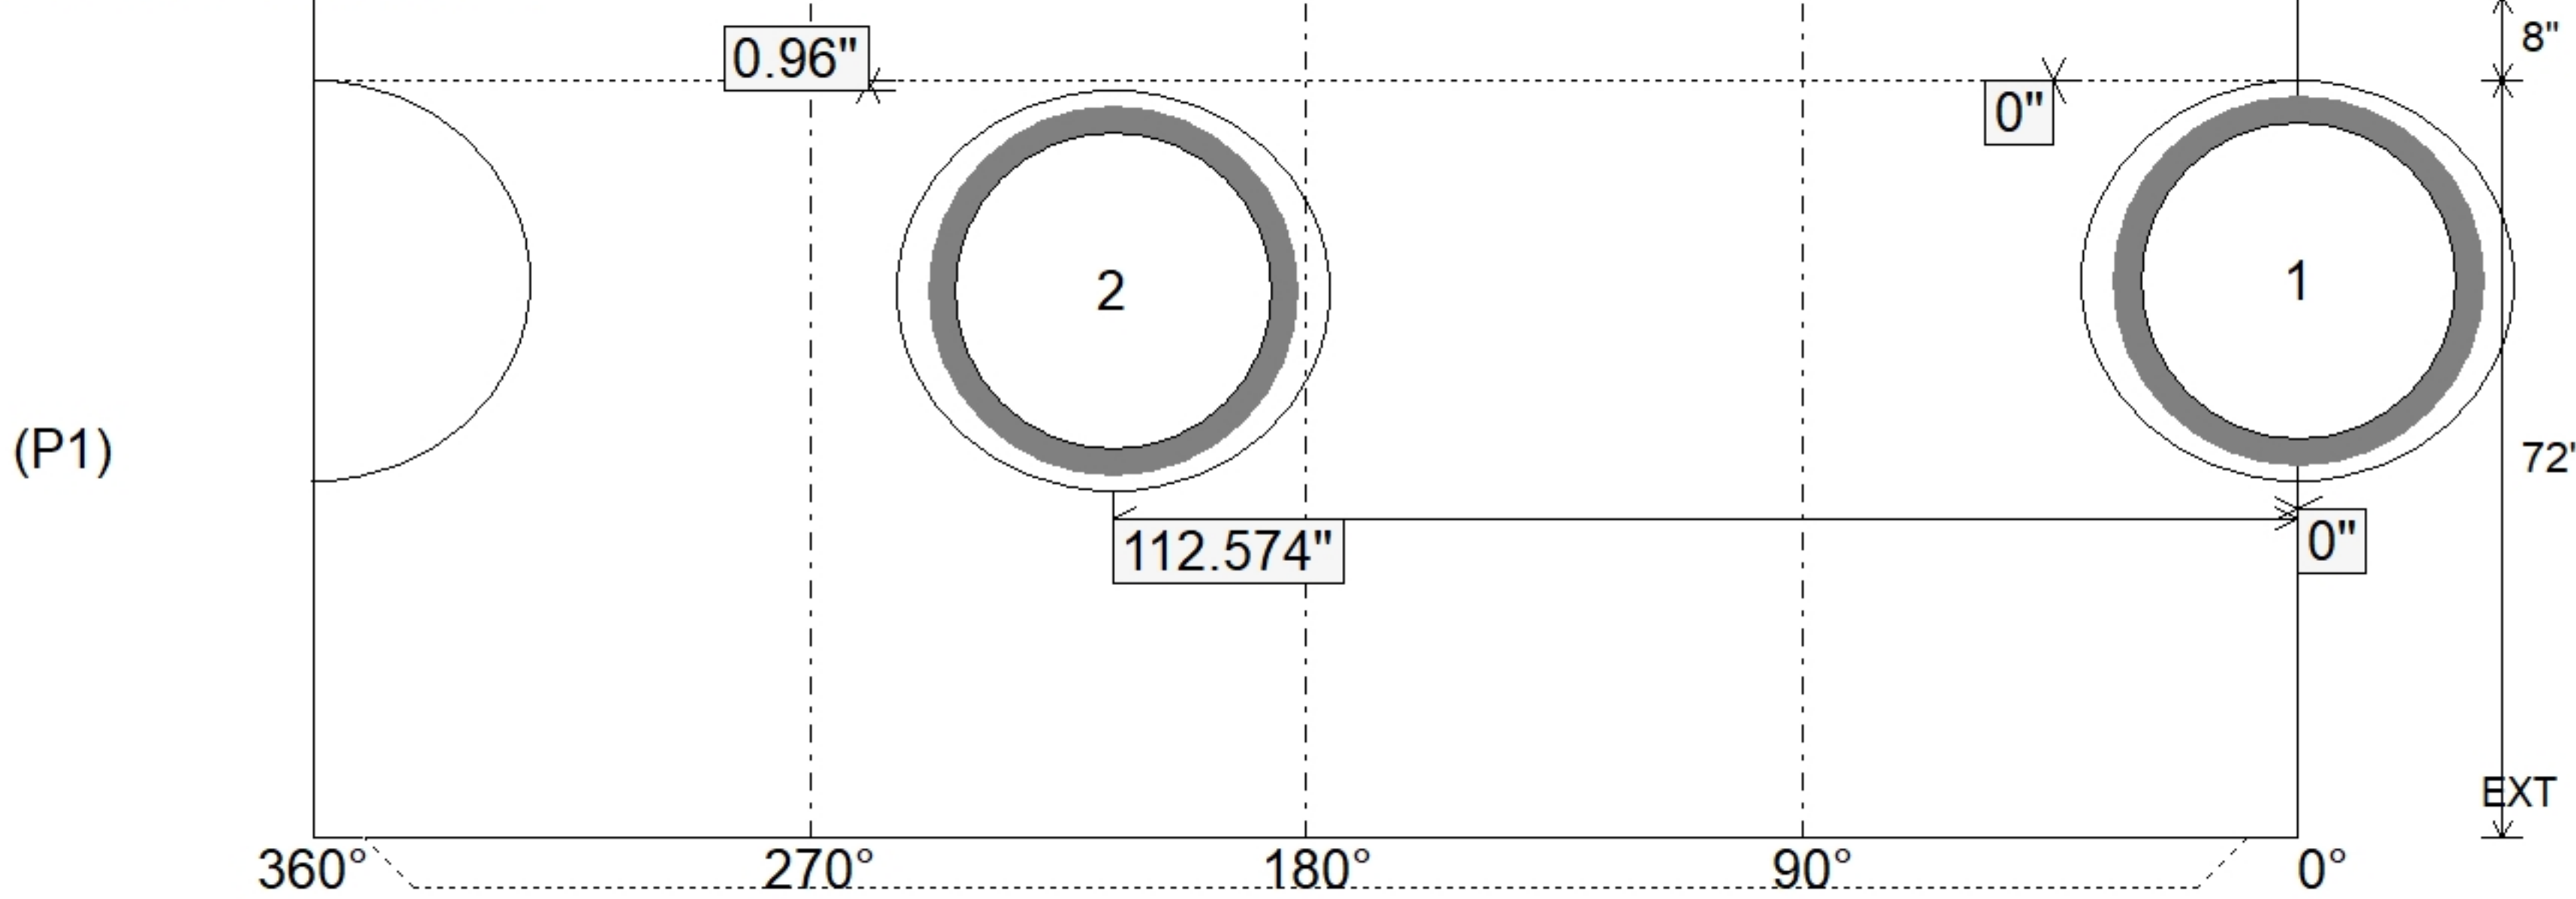


Job Name: 26-2648 Midtown Commons Apartments Job Location: Madisonville, KY Contractor: Steve Pleasant Excavating					Plant: Beaver Dam 7/20/2026 10:44:14 AM		Tech: S. Felletter PC:						
Structure ID: 2.2 MHA													
P1		MH060BA72		MH BASE T/n									
P3) 24" - CASTING HEIGHT - 4" P2) 60" - MH FLAT LID w/24in ECC Hole F/G - 13" P1) 60" - MH BASE T/n - 72" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 60" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 38 6) MH Step ML-10-TDS-NCR - 10"						0 lb 2800 lb 9030 lb 206 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 12036 lb		Structure Notes: 1. PER KYTC MH A / ASTM C478 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C). . REINFORCING PER ASTM A615 (GRADE 60.) - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.					
Rim: 435'		Rim to Invert: 7.15'		Slack: 0.8"		Sump: 4"		Step Position: 107.5°					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	427.85'	0°	0"	30" ADS N-12	35.1"	Hole 38	38"	41.151"	0"	0"			
Invert 2	427.93'	215°	135.088"	30" ADS N-12	35.1"	Hole 38	38"	41.151"	0.96"	0"			
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS 													
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 6" Floor Height: 8"		Height (Int): 72" Height (Ext): 80"		Weight (Net): 9030 lb Volume (Net): 2.31cu.yd				
